

TYPICAL DETAIL FOR CONSTRUCTION SIGNS
ON TWO LANE OR MULTILANE UNDIVIDED LOW SPEED HIGHWAY


FED. ROAD DIST. NO. STATE PROJ. NO. FISCAL SHEET NO. SHEETS


HAWAII HAW. 50C-01-07M 2007 24 24


Work Zone Note:

- 1. This Work Zone Sign Plan is intended for use on long-term stationary work zones/construction phases (3 days or more). All work zones or construction phases less than 3 days duration will use Traffic Control Plans shown in Section 645 of the Special Provisions.
- 2. All existing regulatory speed limit signs with posts within the work zone/project limits shall be removed and replaced with work zone speed limit sign assemblies (R2-1(XX) and R2-5b(XX) with "CONSTRUCTION AREA" and "\$250 FINE HRS 291C-104" Supplemental Signs).
- 3. Construction sign assemblies shall be installed on both the approaching and trailing ends of each work zone as shown on this plan.
- 4. Each construction warning sign and work zone speed limit assembly shall have a minimum of two (2) Type II OM. Installation of each Type II OM shall be considered incidental to Item No. 645.0100 Traffic Control.
- 5. Upon the completion of all physical work or as directed by the Engineer, all construction signs and work zone speed limit assemblies shall be removed. All speed limit signs and posts that were existing at the start of the project within the work zone/project imits shall be restored back to their original locations and configurations.
- 6. Placement of construction signs shall not obstruct the path of pedestrians and bicyclists.
- 7. The removal and restoration of existing regulatory speed limit signs shall be considered incidental to Item No. 645.0100 Traffic Control.
- 8. The installation, maintenance and removal of work zone speed limit sign assemblies shall be paid for under Item No. 645.0100 Traffic Control.
- 9. The work zone speed limit signs shall be new and become the property of the Contractor.


TABLE I GUIDELINE FOR ADVANCE PLACEMENT OF SPEED REDUCTION SIGN R2-5b(XX)-A, CONSTRUCTION AREA SPEED LIMIT		
YY – EXISTING POSTED SPEED LIMIT (MPH)	XX - NEW CONSTRUCTION AREA SPEED LIMIT (MPH)	D-REDUCED SPEED LIMIT SIGN SPACING TO FIRST CONSTRUCTION AREA SPEED LIMIT SIGN (FEET)
≤25	EXIST. SPEED LIMIT TO REMAIN	
30	25	100
35	25	175
40	30	175



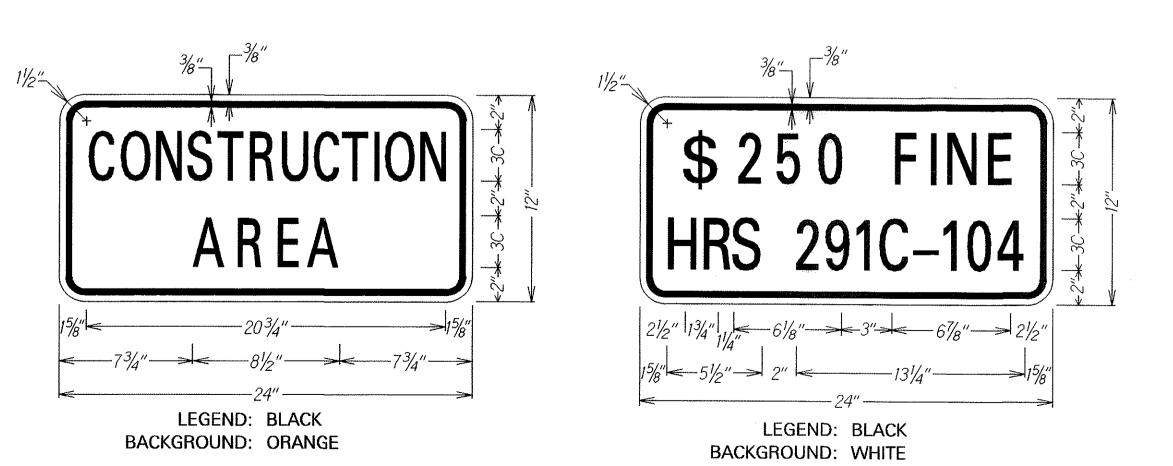

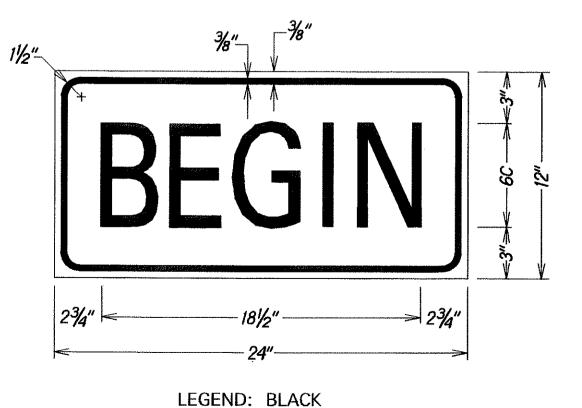

BACKGROUND: ORANGE

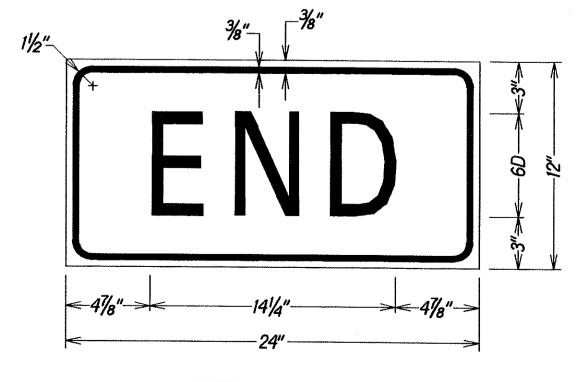

LEGEND: BLACK BACKGROUND: ORANGE STATE OF HAWAII
DEPARTMENT OF TRANSPORTATION
HIGHWAYS DIVISION

LOW SPEED UNDIVIDED HIGHWAY
WORK TONE SIGNING DIAN NOTESADETA

WORK ZONE SIGNING PLAN, NOTES&DETAILS

KAUMUALII HIGHWAY RESURFACING
Halewili Road to Vicinity of Wahiawa Bridge

Project No. 50C-01-07M

Not to Scale

Date: October 2006

SHEET No. 2 OF 2 SHEETS
