





Work Zone Notes:

- 1. This Work Zone Sign Plan is intended for use on long-term stationary work zones/construction phases (3 days or more). All work zones or construction phases less than 3 days duration will use Traffic Control Plans shown in Section 645 of the Special Provisions.
- 2. All existing regulatory speed limit signs with posts within the work zone/project limits shall be removed and replaced with work zone speed limit sign assemblies (R2-1(40) and CW3-5(40) with "CONSTRUCTION AREA" and "\$250 FINE HRS 291C-104" Supplemental Signs).
- 3. Construction sign assemblies shall be installed on both the approaching and trailing ends of each work zone as shown on this plan.
- 4. Each construction warning sign and work zone speed limit assembly shall have a minimum of two (2) Type II OM. Installation of each Type II OM shall be considered incidental to Item No. 645.1000, Traffic Control.
- 5. Upon the completion of all physical work or as directed by the Engineer, all construction signs and work zone speed limit assemblies shall be removed. All speed limit signs and posts that were existing at the start of the project within the work zone/project imits shall be restored back to their original locations and configurations.
- 6. Placement of construction signs shall not obstruct the path of pedestrians and bicyclists.
- 7. Removing and restoring existing regulatory speed limit signs and furnishing new posts along with furnishing, installing, maintaining and removing work zone speed limit sign assemblies shall be considered incidental to Item No. 645.1000, Traffic Control.



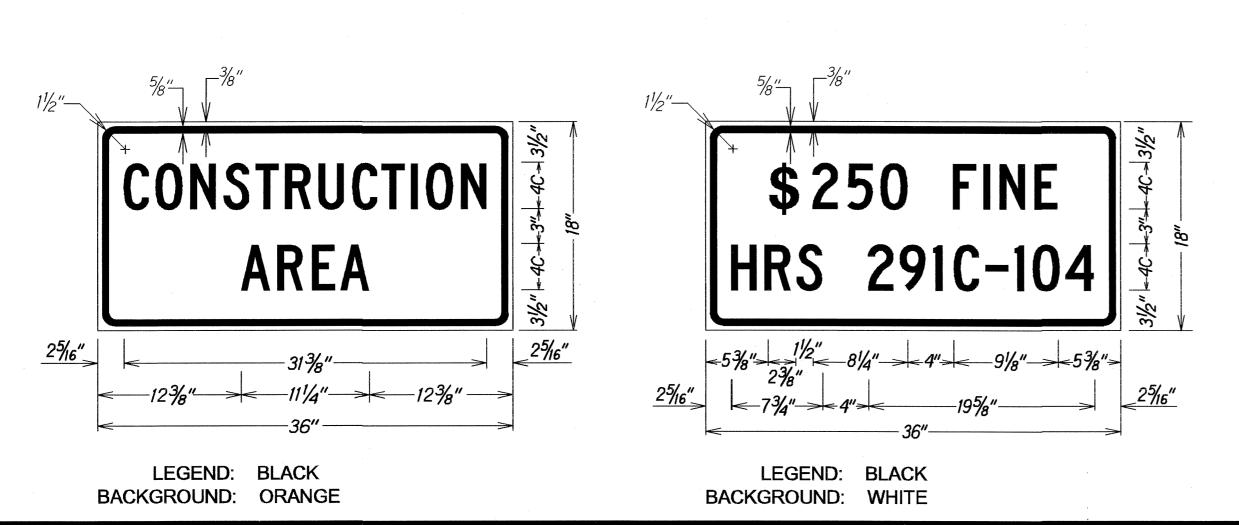

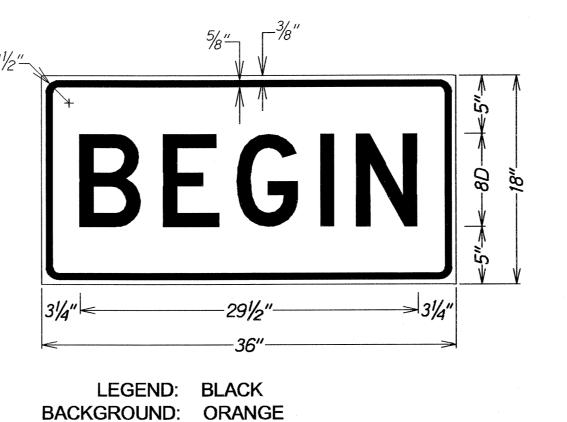

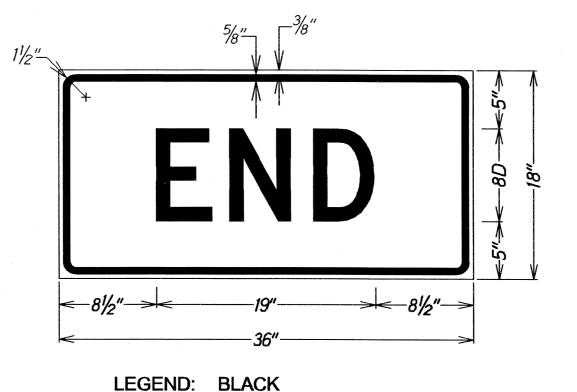

BACKGROUND: ORANGE

STATE OF HAWAII **DEPARTMENT OF TRANSPORTATION** HIGH SPEED UNDIVIDED HIGHWAY WORK ZONE SIGNING PLAN, NOTES #DETAILS KUHIO HIGHWAY DRAINAGE IMPROVEMENTS

Vicinity of M.P. 18.3

Proj. No. 56AC-01-04 Date: June 2007 Not to Scale

> SHEET No. 1 OF 1

SHEETS
