


FED. ROAD DIST. NO.	STATE	FED. AID PROJ. NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
HAWAII	HAW.	I-HI-1(110)15	1973	4	220

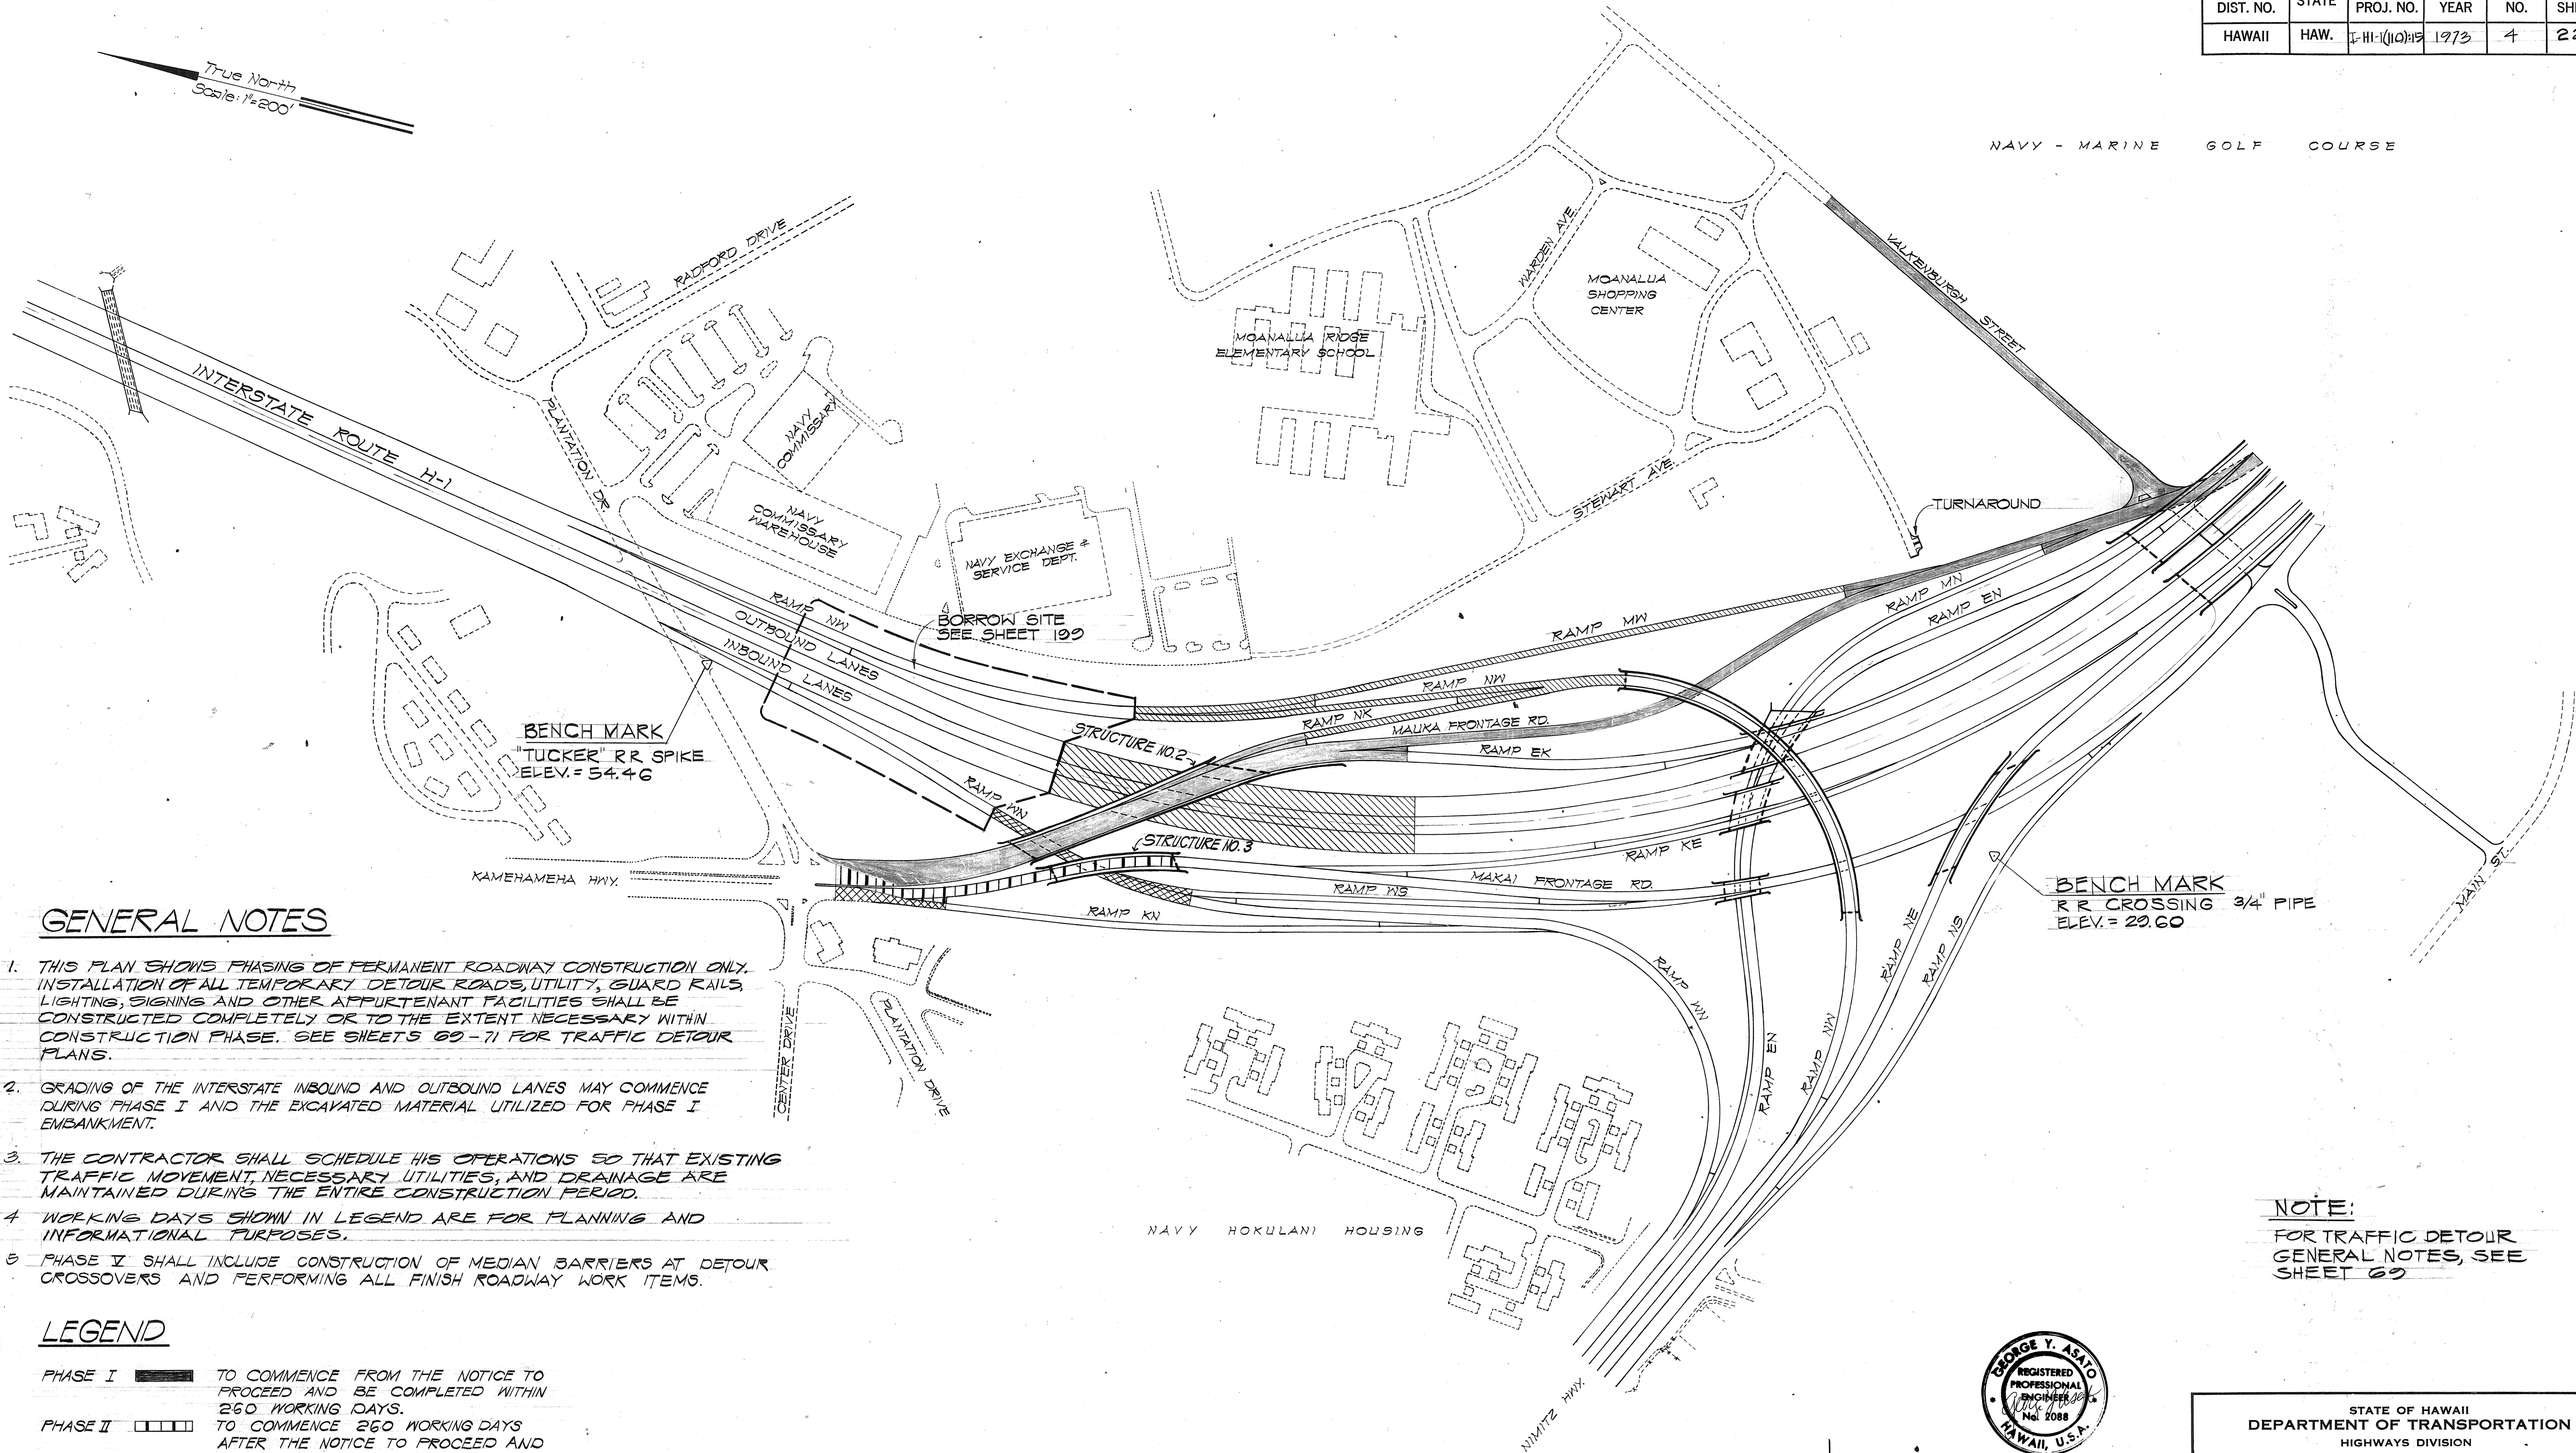

GENERAL NOTES

- 1. THIS PLAN SHOWS PHASING OF PERMANENT ROADWAY CONSTRUCTION ONLY. INSTALLATION OF ALL TEMPORARY DETOUR ROADS, UTILITY, GUARD RAILS, LIGHTING, SIGNING AND OTHER APPURTENANT FACILITIES SHALL BE CONSTRUCTED COMPLETELY OR TO THE EXTENT NECESSARY WITHIN CONSTRUCTION PHASE. SEE SHEETS 69-71 FOR TRAFFIC DETOUR PLANS.
- 2. GRADING OF THE INTERSTATE INBOUND AND OUTBOUND LANES MAY COMMENCE DURING PHASE I AND THE EXCAVATED MATERIAL UTILIZED FOR PHASE I EMBANKMENT.
- 3. THE CONTRACTOR SHALL SCHEDULE HIS OPERATIONS SO THAT EXISTING TRAFFIC MOVEMENT, NECESSARY UTILITIES, AND DRAINAGE ARE MAINTAINED DURING THE ENTIRE CONSTRUCTION PERIOD.
- 4. WORKING DAYS SHOWN IN LEGEND ARE FOR PLANNING AND INFORMATIONAL PURPOSES.
- 5. PHASE I SHALL INCLUDE CONSTRUCTION OF MEDIAN BARRIERS AT DETOUR CROSSOVERS AND PERFORMING ALL FINISH ROADWAY WORK ITEMS.

LEGEND

- PHASE I [diagonal lines] TO COMMENCE FROM THE NOTICE TO PROCEED AND BE COMPLETED WITHIN 260 WORKING DAYS.
- PHASE II [horizontal lines] TO COMMENCE 260 WORKING DAYS AFTER THE NOTICE TO PROCEED AND BE COMPLETED WITHIN 140 WORKING DAYS.
- PHASE III [vertical lines] TO COMMENCE 260 WORKING DAYS AFTER THE NOTICE TO PROCEED AND BE COMPLETED WITHIN 200 WORKING DAYS (END OF CONTRACT TIME).
- PHASE IV [cross-hatch] TO COMMENCE 400 WORKING DAYS AFTER THE NOTICE TO PROCEED AND BE COMPLETED WITHIN 60 WORKING DAYS (END OF CONTRACT TIME).

NOTE:
FOR TRAFFIC DETOUR
GENERAL NOTES, SEE
SHEET 69

DATE	7/23/75
ORIGINAL PLAN	NO.
DESIGNED BY	WILLIAM T. TAKAMURA
TRACED BY	WILLIAM T. TAKAMURA
NOTE BOOK	NO.
DESIGNED BY	WILLIAM T. TAKAMURA
TRACED BY	WILLIAM T. TAKAMURA
NOTE BOOK	NO.
DESIGNED BY	WILLIAM T. TAKAMURA
TRACED BY	WILLIAM T. TAKAMURA
NOTE BOOK	NO.

7/23/75	ADDED NOTE NO. 3.
DATE	REVISION

WILLIAM T. TAKAMURA
REGISTERED PROFESSIONAL ENGINEER
No. 1684
HAWAII, U.S.A.

THIS WORK WAS PREPARED BY ME
OR UNDER MY SUPERVISION

STATE OF HAWAII
DEPARTMENT OF TRANSPORTATION
HIGHWAYS DIVISION

CONSTRUCTION PHASING
PACKAGE I

PEARL HARBOR INTERCHANGE
F.A.I. Proj. No. I-HI-1(110)15

Scale: As Shown Date: MAY 28 1973

SHEET No. 4 OF 4 SHEETS
