



GENERAL NOTES:

1. It is proposed to route traffic through the project site along H-1 Outbound & H-1 Inbound lanes (at least 2 lanes of traffic in each direction), Kamehameha Highway Connector (Inbound lanes), Temporary Connectors #1, #2, Loop #5 and Waipahu Street Realignment & Connector immediately upon the completion of Phase III. Where falsework is to remain in areas open to traffic, the lateral clearance between such falsework and the edge of travel way designated for traffic routing shall be not less than six (6) feet. The Contractor shall consider the foregoing when arranging for the shoring of Structures.
2. All utility, guardrail, lighting, signing and other related work within each individual construction phase shall be performed completely or to the extent necessary in such timely sequence as to preclude duplication of efforts (as reexcavation for installation of utilities) and hazardous roadside construction (as installation of guardrail on roadways open to public traffic).
3. All hydro-mulching may be done within the time limit for Phase IV.

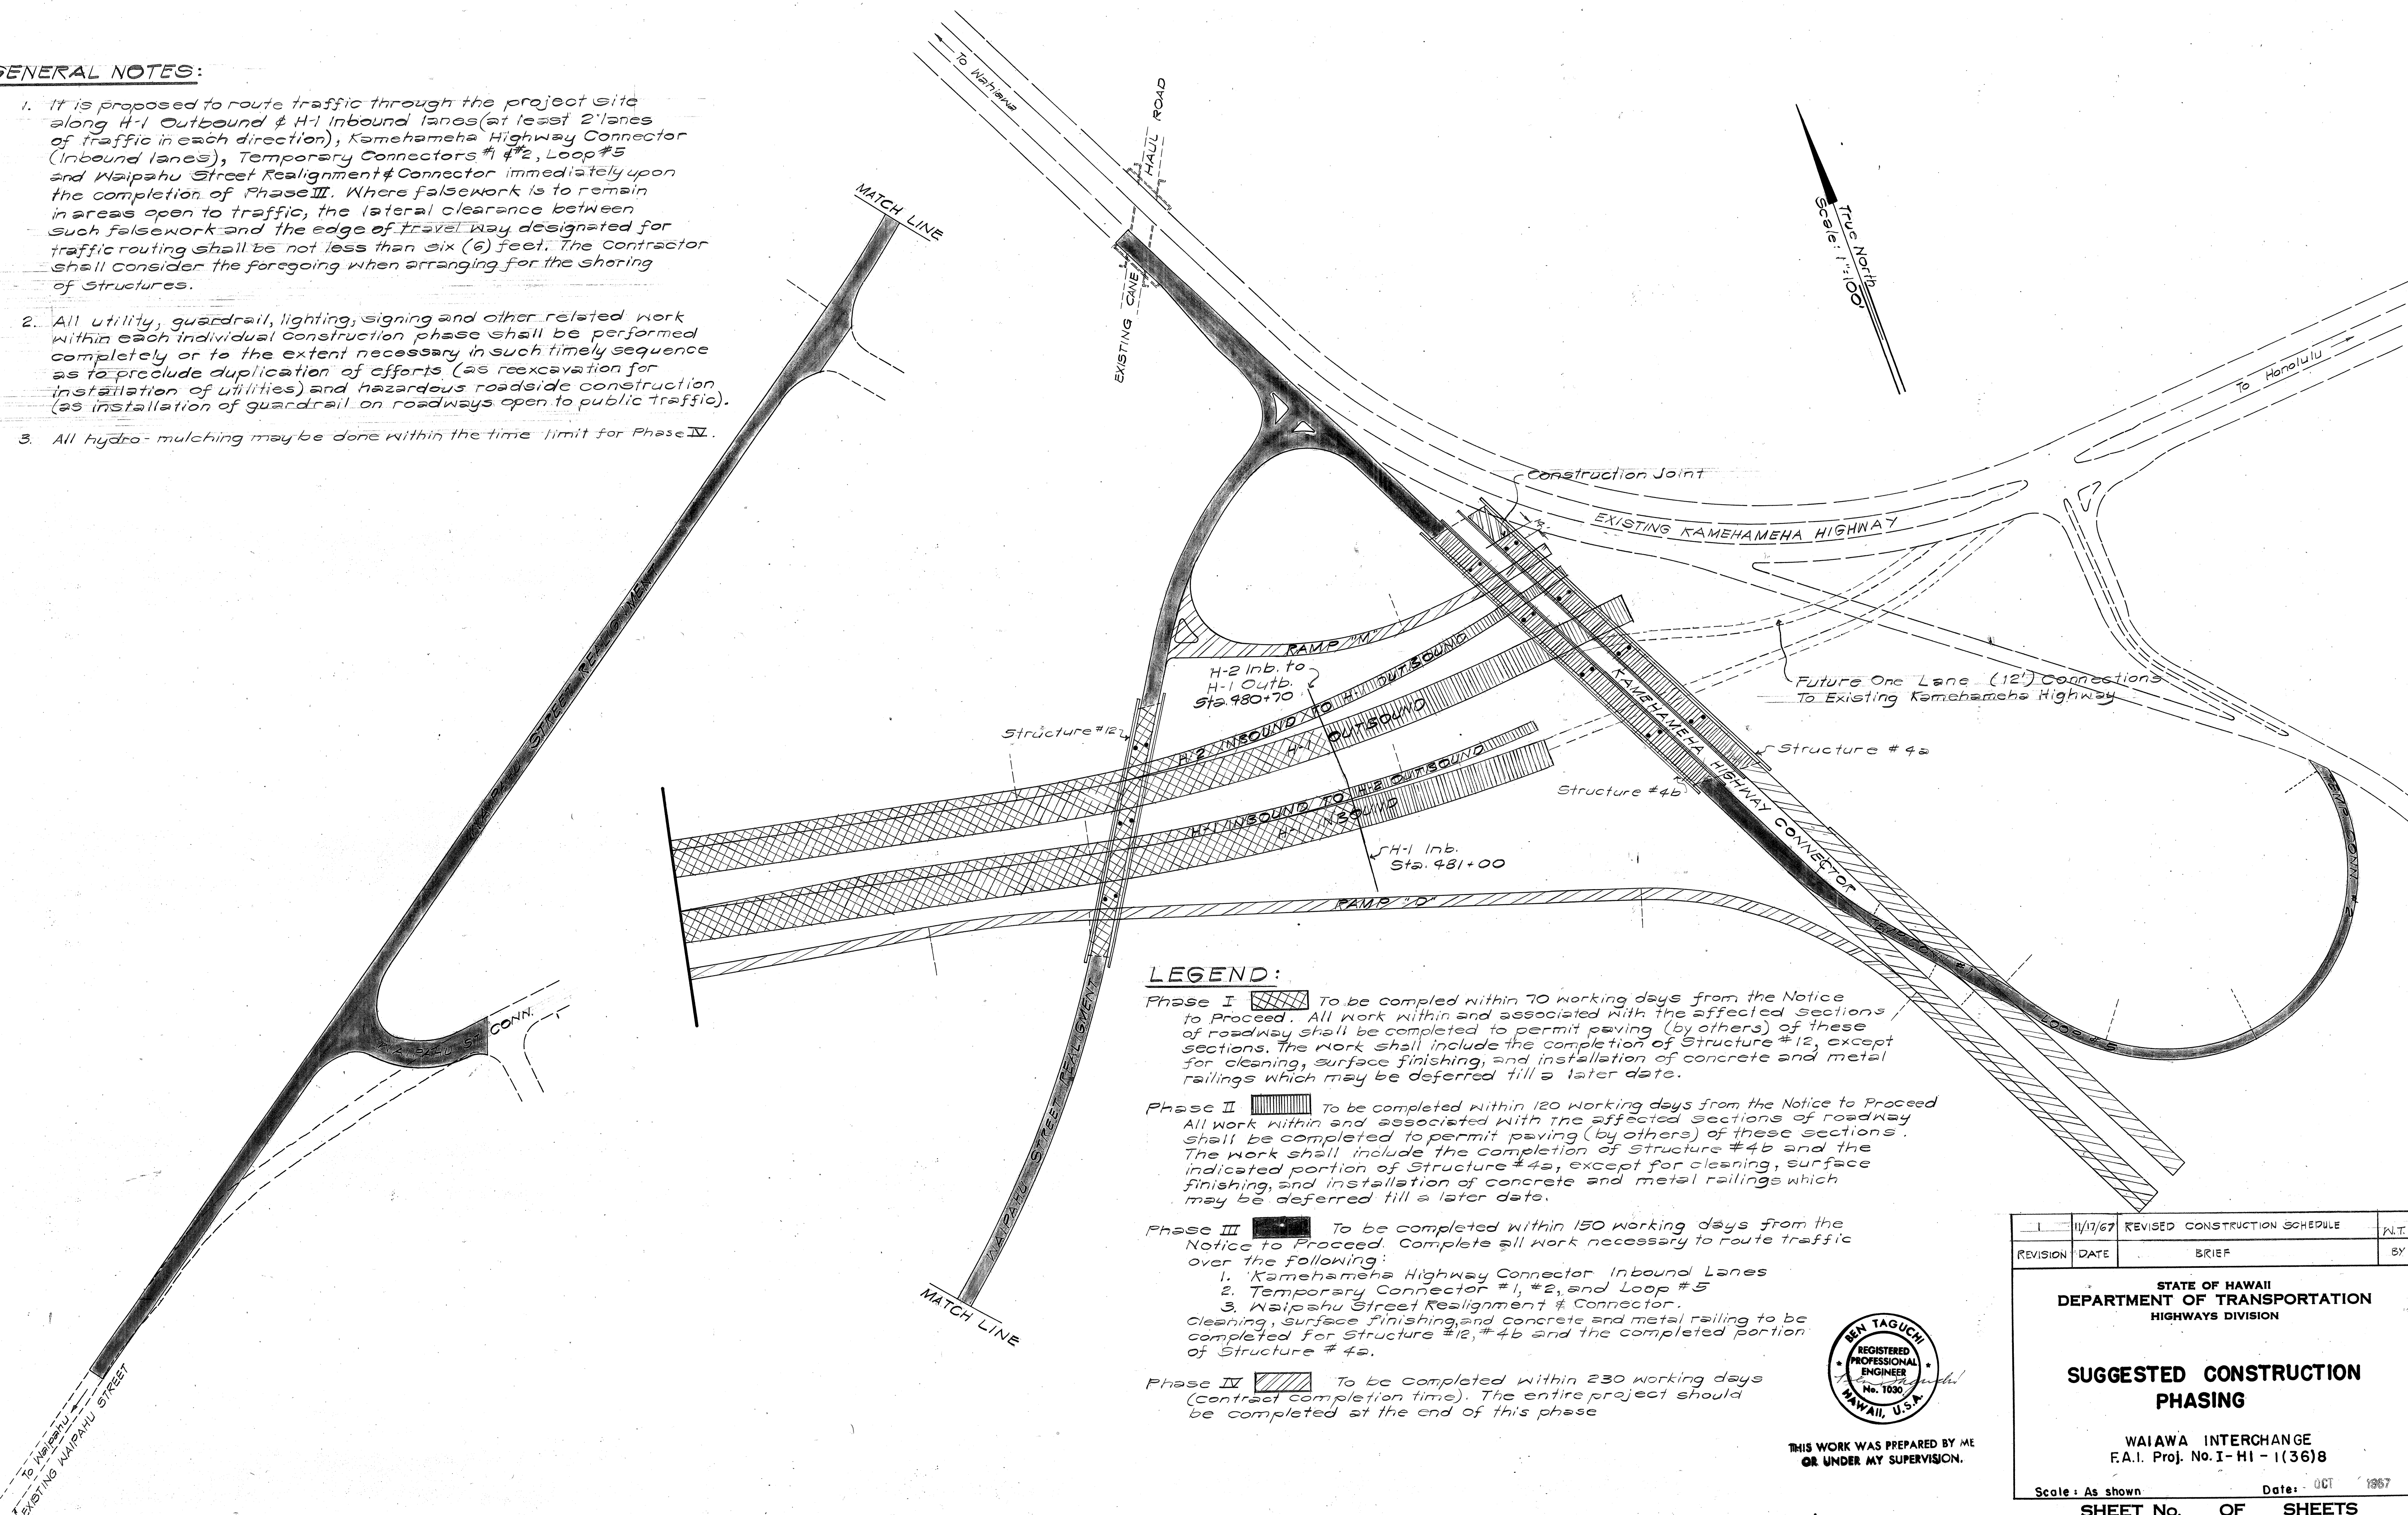

LEGEND:

- Phase I** [Hatched Pattern] To be completed within 70 working days from the Notice to Proceed. All work within and associated with the affected sections of roadway shall be completed to permit paving (by others) of these sections. The work shall include the completion of Structure #12, except for cleaning, surface finishing, and installation of concrete and metal railings which may be deferred till a later date.
- Phase II** [Horizontal Line Pattern] To be completed within 120 working days from the Notice to Proceed. All work within and associated with the affected sections of roadway shall be completed to permit paving (by others) of these sections. The work shall include the completion of Structure #4b and the indicated portion of Structure #4a, except for cleaning, surface finishing, and installation of concrete and metal railings which may be deferred till a later date.
- Phase III** [Solid Black Pattern] To be completed within 150 working days from the Notice to Proceed. Complete all work necessary to route traffic over the following:
1. Kamehameha Highway Connector Inbound Lanes
2. Temporary Connector #1, #2, and Loop #5
3. Waipahu Street Realignment & Connector.
Cleaning, surface finishing, and concrete and metal railing to be completed for Structure #12, #4b and the completed portion of Structure #4a.
- Phase IV** [Diagonal Line Pattern] To be completed within 230 working days (contract completion time). The entire project should be completed at the end of this phase.



THIS WORK WAS PREPARED BY ME
OR UNDER MY SUPERVISION.

1	11/17/67	REVISED CONSTRUCTION SCHEDULE	P.L.T.
REVISION	DATE	BRIEF	BY
STATE OF HAWAII DEPARTMENT OF TRANSPORTATION HIGHWAYS DIVISION			
SUGGESTED CONSTRUCTION PHASING			
WAIAWA INTERCHANGE F.A.I. Proj. No. I-H-11368			
Scale: As shown		Date: OCT 1967	
SHEET No. 1		OF 22 SHEETS	

ADDENDUM No. 1

22

ADDENDUM No. 1

DATE	_____
SURVEY PLOTTED BY	_____
DRAWN BY	_____
DESIGNED BY	_____
QUANTITIES BY	_____
CHECKED BY	_____
ORIGINAL PLAN	_____
NOTE BOOK	_____
No.	_____
