


FED. ROAD DIST. NO.	STATE	FED. AID PROJ. NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
HAWAII	HAW.	I-H-1(69)8	1968	4	144

GENERAL NOTES:


- The Contractor shall schedule his operations so that bi-directional Naianae-Honolulu public traffic and access to existing driveways along Kamehameha Highway are permitted at all times during construction.
- All utility, guard rail, lighting, signing, hydro-mulching and other related work within each individual construction phase shall be performed completely or to the extent necessary in such timely sequence as to preclude duplication of efforts (as reexcavation for installation of utilities) and hazardous roadside construction (as installation of guard rails or signs on roadways open to public traffic).

LEGEND:

- Phase I [diagonal lines] To commence from the Notice to Proceed and be completed within 200 working days.
- Phase II [solid black] To commence 60 working days after the Notice to Proceed and be completed within 80 working days. Complete all work to accommodate detouring of H-1 traffic during Phase III construction.
- Phase III [horizontal lines] To commence 140 working days after the Notice to Proceed and be completed within 60 working days. Complete all work to route traffic on H-1 Inbound and Loop #3, including the surcharging of Abutment #1 for Structure #5 and Abutment #2 for Structure #6. Surcharging shall be the first order of work for this phase and be done immediately after Phase II construction and be completed within 10 working days to expedite ultimate settlement. See sht. 32 for detouring of traffic during this phase.
- Phase IV [diagonal lines] To commence 200 working days after the Notice to Proceed and be completed within 250 working days. See sht. 33 & 34 for detouring of traffic during this phase.
- Phase V [cross-hatch] The contractor shall not commence work in this phase without approval by the Engineer. Approval shall include inspection for stability of embankments to preclude excessive post-construction settlements. Following the Engineer's approval, work shall commence 330 working days after the Notice to Proceed and be completed within 60 working days. The entire project should be completed by the end of this phase.

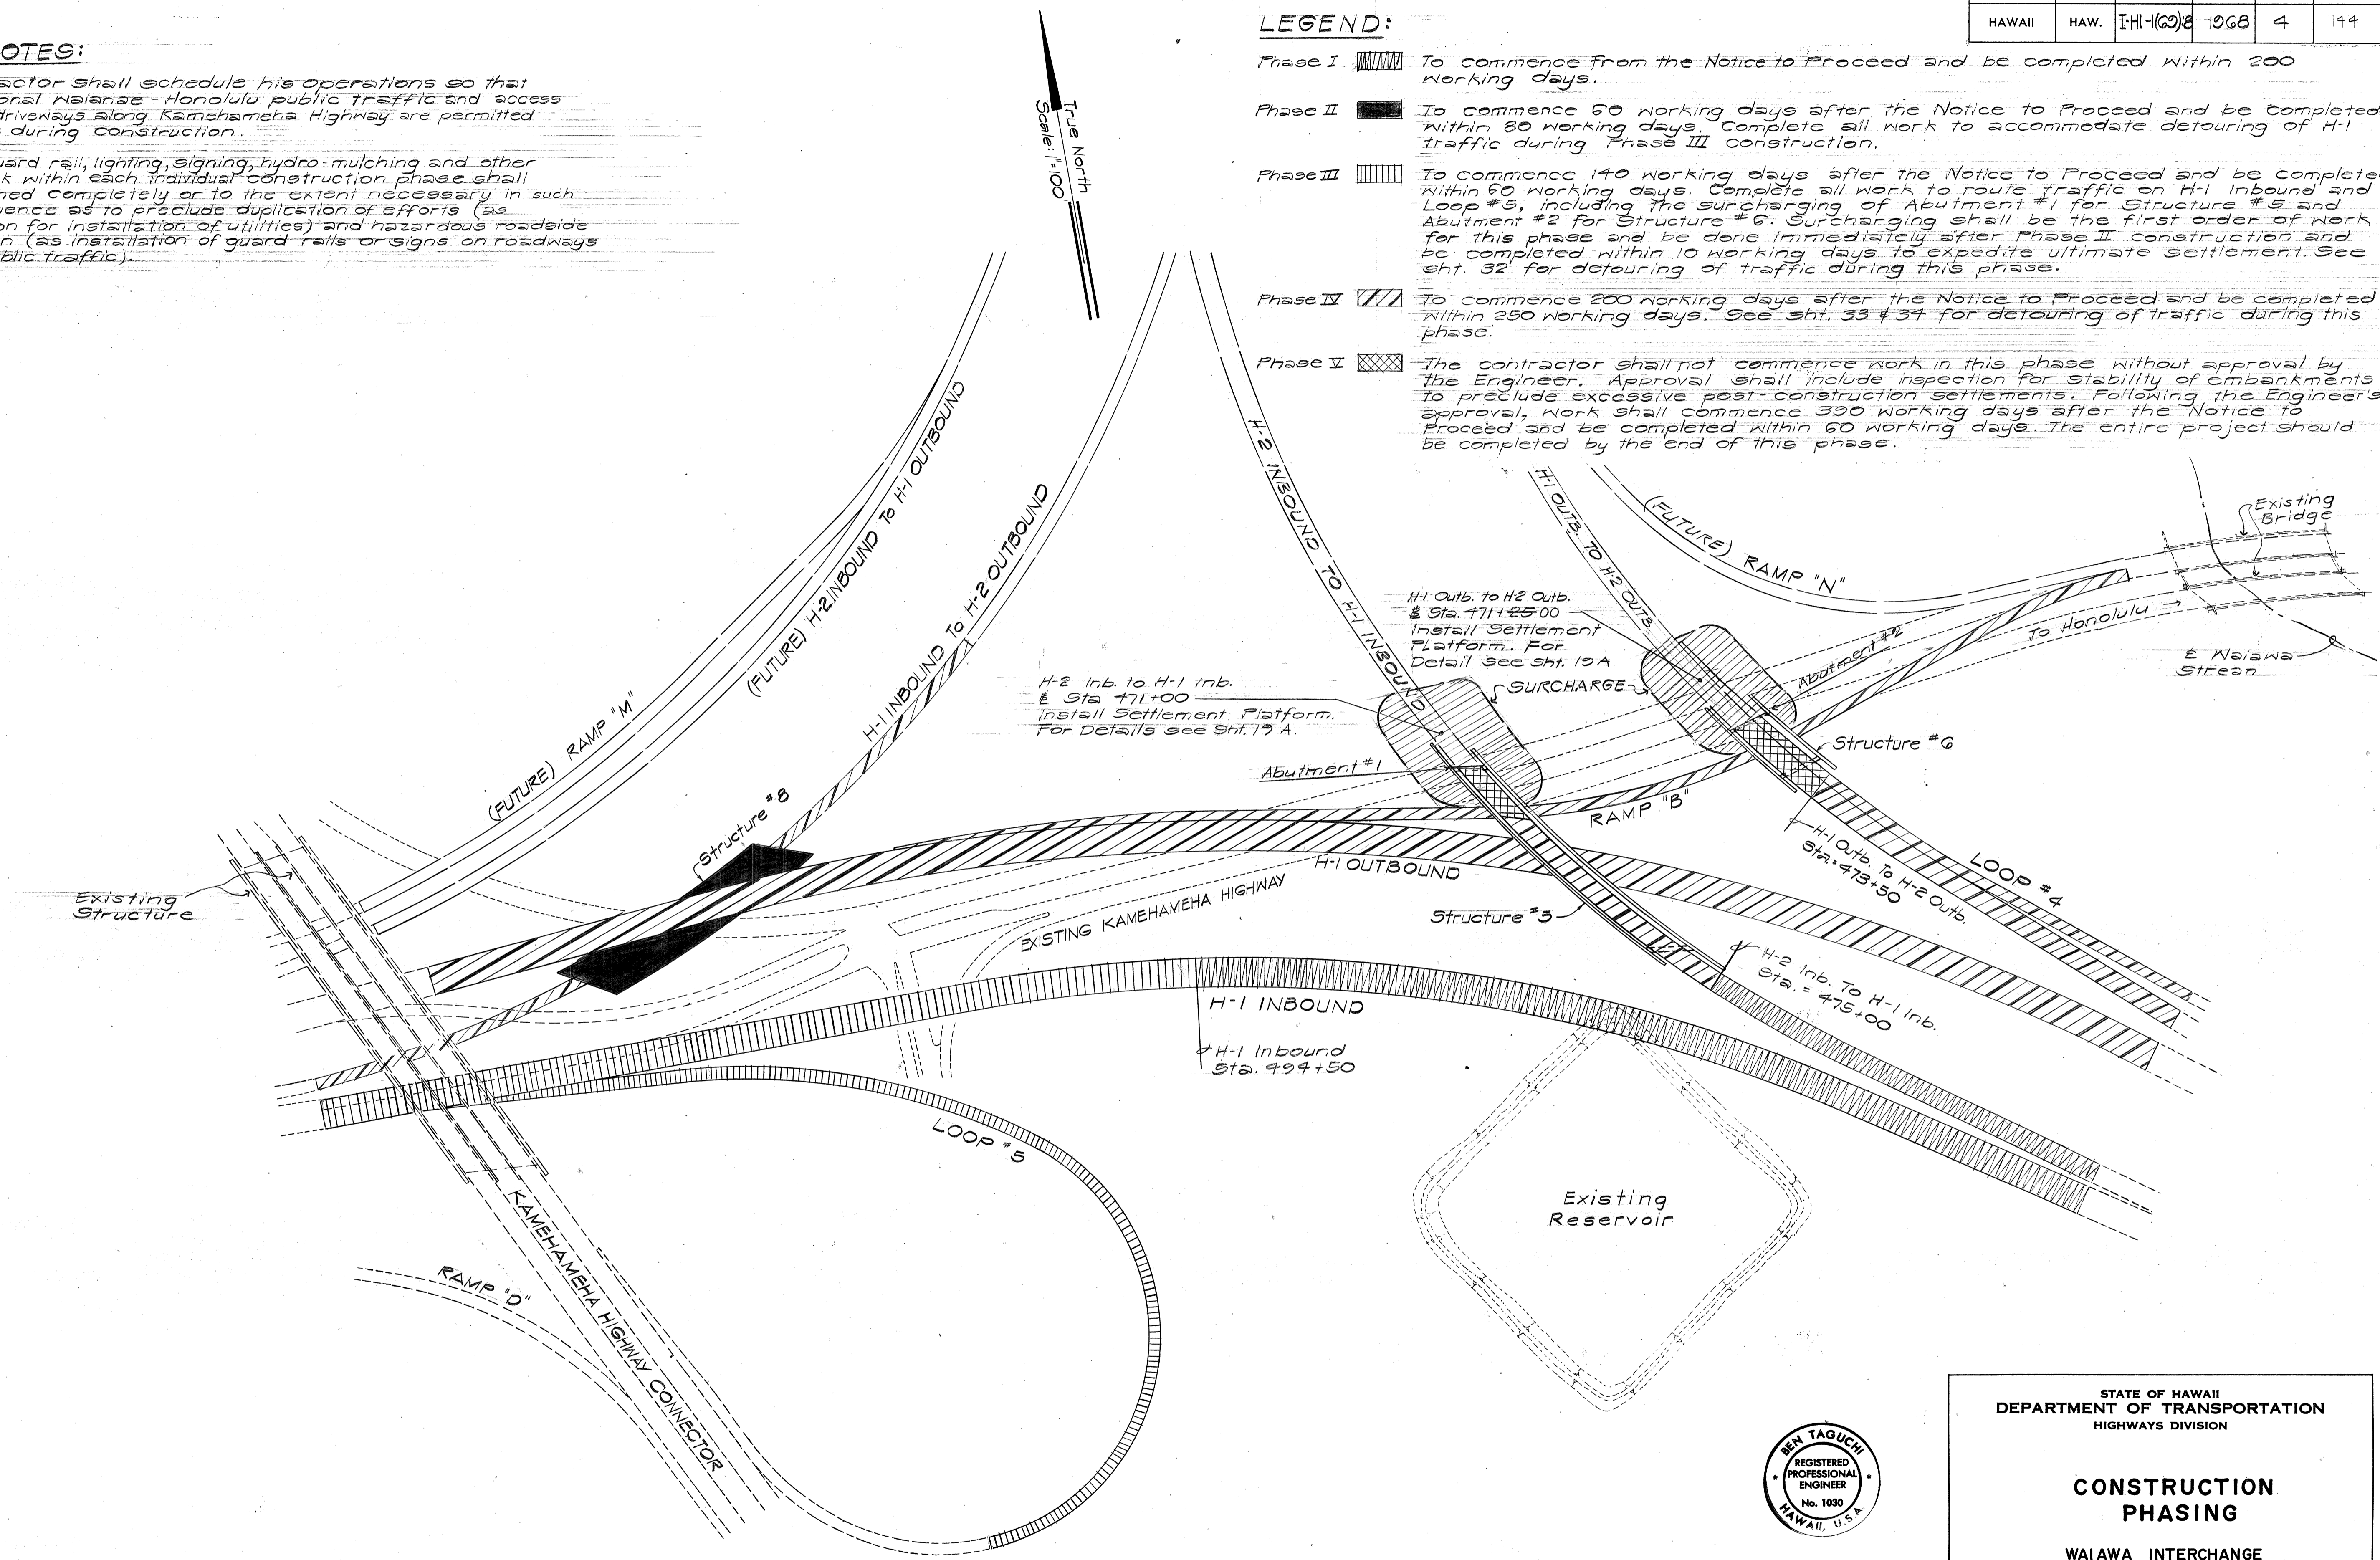

DATE	BY
DESIGNED BY	
CHECKED BY	
NO.	



THIS WORK WAS PREPARED BY ME OR UNDER MY SUPERVISION.
Ken Taguchi

STATE OF HAWAII
DEPARTMENT OF TRANSPORTATION
HIGHWAYS DIVISION

CONSTRUCTION PHASING

WAIAWA INTERCHANGE
F.A.I. Proj. No. I-H-1(69)-8

Scale: As shown Date: OCT. 1968
SHEET No. 1 OF 1 SHEETS
