

ORDER OF WORK AND DETOURS

PHASE I

1. Build Waialeale Stream Bridge, Mauka half of Kapakahi Stream Culvert, and Mauka half of Waipahu Canal Bridge.
 2. Construct Outbound Lanes.
 3. Traffic to use existing highway without any changes.
- The existing traffic signal system shall remain in operation throughout Phase I.

PHASE II

1. Build crossover to use new lanes. Barricade old road except for local traffic.
2. Traffic to use newly constructed outbound lanes. Where existing highway is shown to be one way, at least one lane shall be kept open to traffic and where shown to be two-way, at least two 10' lanes shall be kept open to traffic. The temporary traffic signal system for Phase II shall be kept in operation until otherwise directed by the Engineer.
3. Build Makai half of Kapakahi Stream Culvert and Waipahu Canal Bridge.
4. Open up inbound lanes at end of Phase II.

GENERAL NOTES


1. Pavement markings to be done by others.
2. Barricades as shown on the plans are intended as a guide only, and the exact type, number and locations of barricades shall be as directed by the Engineer.
3. Barricades used at bridges under construction shall be of a substantial nature.
4. Rental (including installation and maintenance) of barricades, blinkers, and amber beacons will be paid for under item 115 "Maintaining Detours".
5. These four (4) sheets of detour plans show the pattern of traffic for Phase II only.
6. When ordered by the Engineer, the Contractor shall remove and stockpile at the jobsite, the temporary directional, regulatory, warning, and construction signs used for the detour during phase II.

SUMMARY OF SIGNS

SIGN No.	MESSAGE AND DESCRIPTION	No.
R1-1	STOP	1
R1-2	YIELD	1
R3-1	NO RIGHT TURN	1
R3-2	↑	2
R4-1	DO NOT PASS	2
R4-2	PASS WITH CARE	1
R5-1	DO NOT ENTER	4
R6-1(L)	ONE WAY ←	4
R6-1(R)	ONE WAY →	-
R6-3	TWO WAY TRAFFIC AHEAD	2
R10-2	ROAD CLOSED	6
R10-3	ROAD CLOSED (LOCAL TRAFFIC ONLY)	1
RM-1	1-Plate (Clear) Delineator	21
RM-3	3-Plate (Amber) Delineators	3
W1-4(L)	↑	2
W1-4(R)	↑	1
W1-6(R)	→	3
W13-1(25)	Advisory 25 M.P.H.	2
W20-1d	ROAD CONSTRUCTION AHEAD	2
W20-2D	DETOUR AHEAD	1
W20-4D	ONE LANE ROAD AHEAD	1
M5-7(L)	← DETOUR	5
M5-7(R)	→ DETOUR	3
CW-1	BRIDGE UNDER CONSTRUCTION	4
	BARRICADE	31


LEGEND

- Existing roadway
- Proposed roadway constructed during PHASE I.
- Temporary roadway
- Direction of through traffic.
- Direction of local traffic.

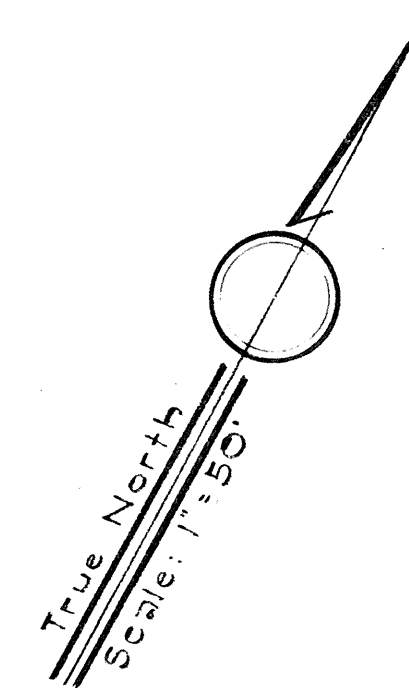

PUPUKAHI ST

STA. 83+00

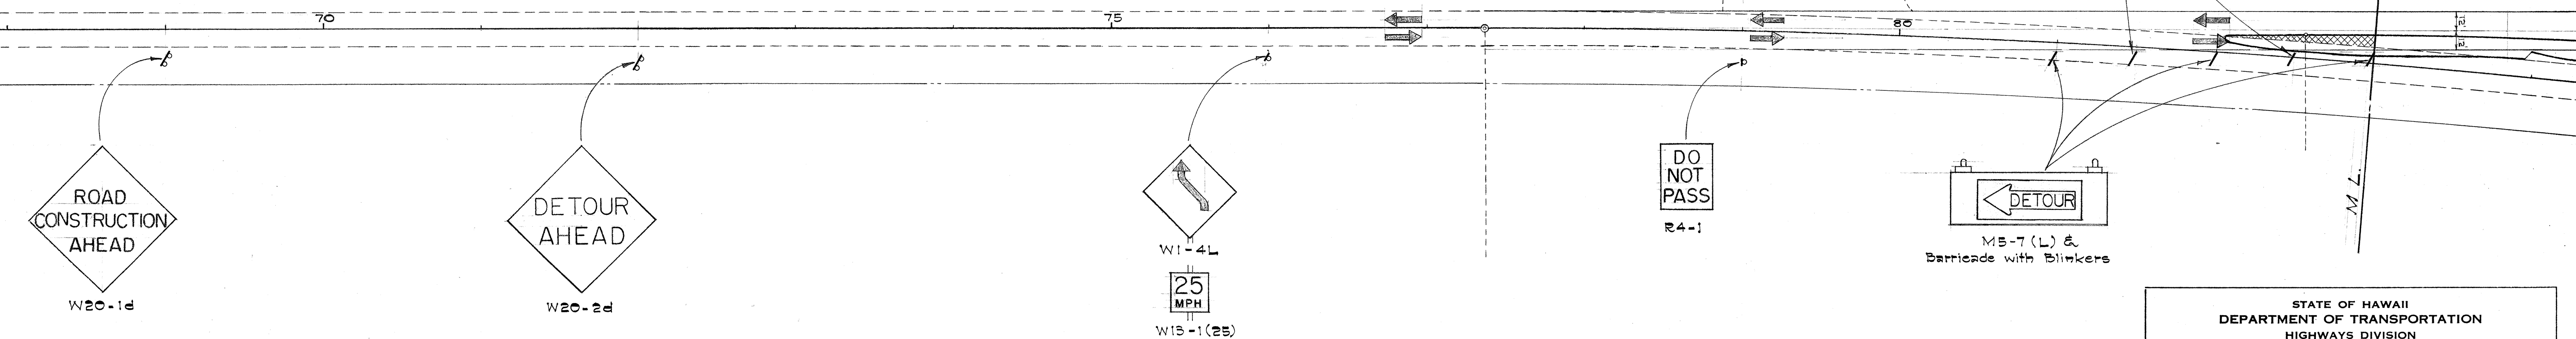

STATE OF HAWAII
DEPARTMENT OF TRANSPORTATION
HIGHWAYS DIVISION


ORDER OF WORK AND DETOURS

FARRINGTON HIGHWAY
PROJECT N2 F-020-1(7)

Scale: 1"=50' Date: Jan. 1962

SHEET No. 1 OF 4 SHEETS

FED. ROAD DIST. NO.	STATE	FED. AID PROJ. NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
HAWAII	HAW	F020-1(7)	1962	16	127

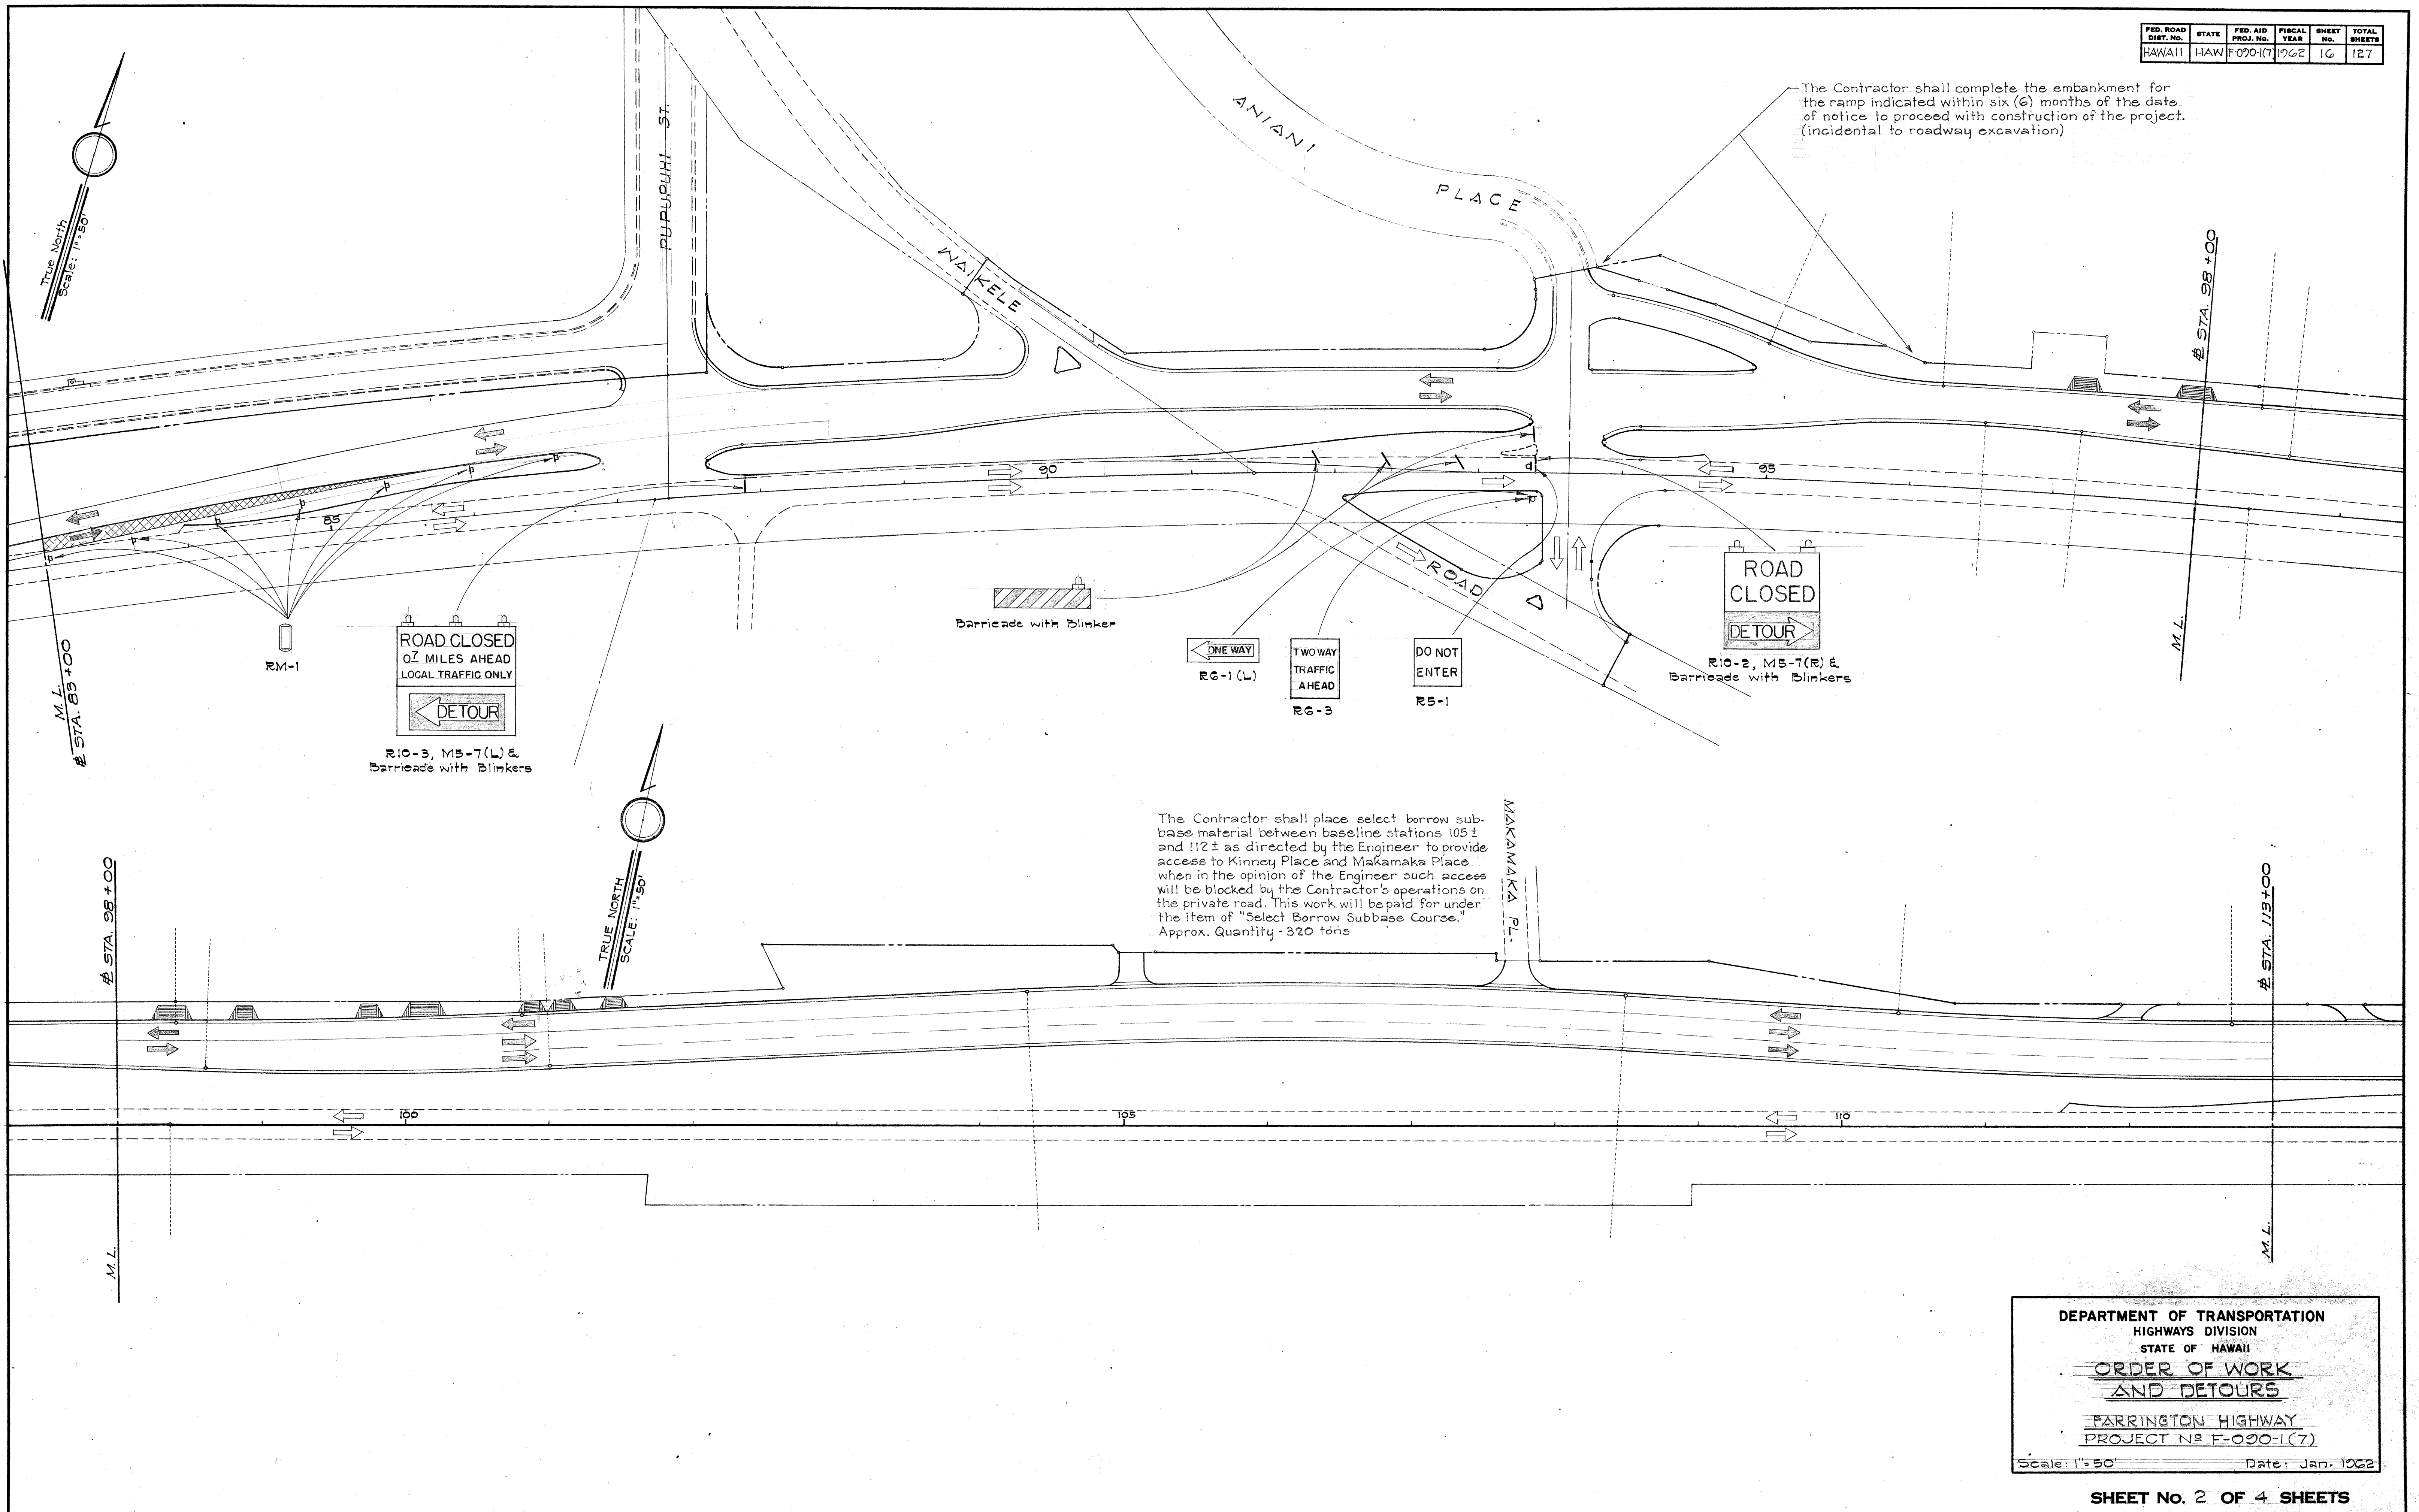

ORIGINAL PLAN	DATE
DESIGNED BY	
DRAWN BY	
CHECKED BY	
NOTED BY	
QUANTITIES CHECKED BY	
NO.	

DEPARTMENT OF TRANSPORTATION
HIGHWAYS DIVISION
STATE OF HAWAII


**ORDER OF WORK
AND DETOURS**

FARRINGTON HIGHWAY
PROJECT NO. F-020-1(7)

Scale: 1"=50' Date: Jan. 1962

SHEET No. 2 OF 4 SHEETS

FED. ROAD DIST. NO.	STATE	FED. AID PROJ. NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
HAWAII	HAW.	F-090-1(7)	1962	18	127

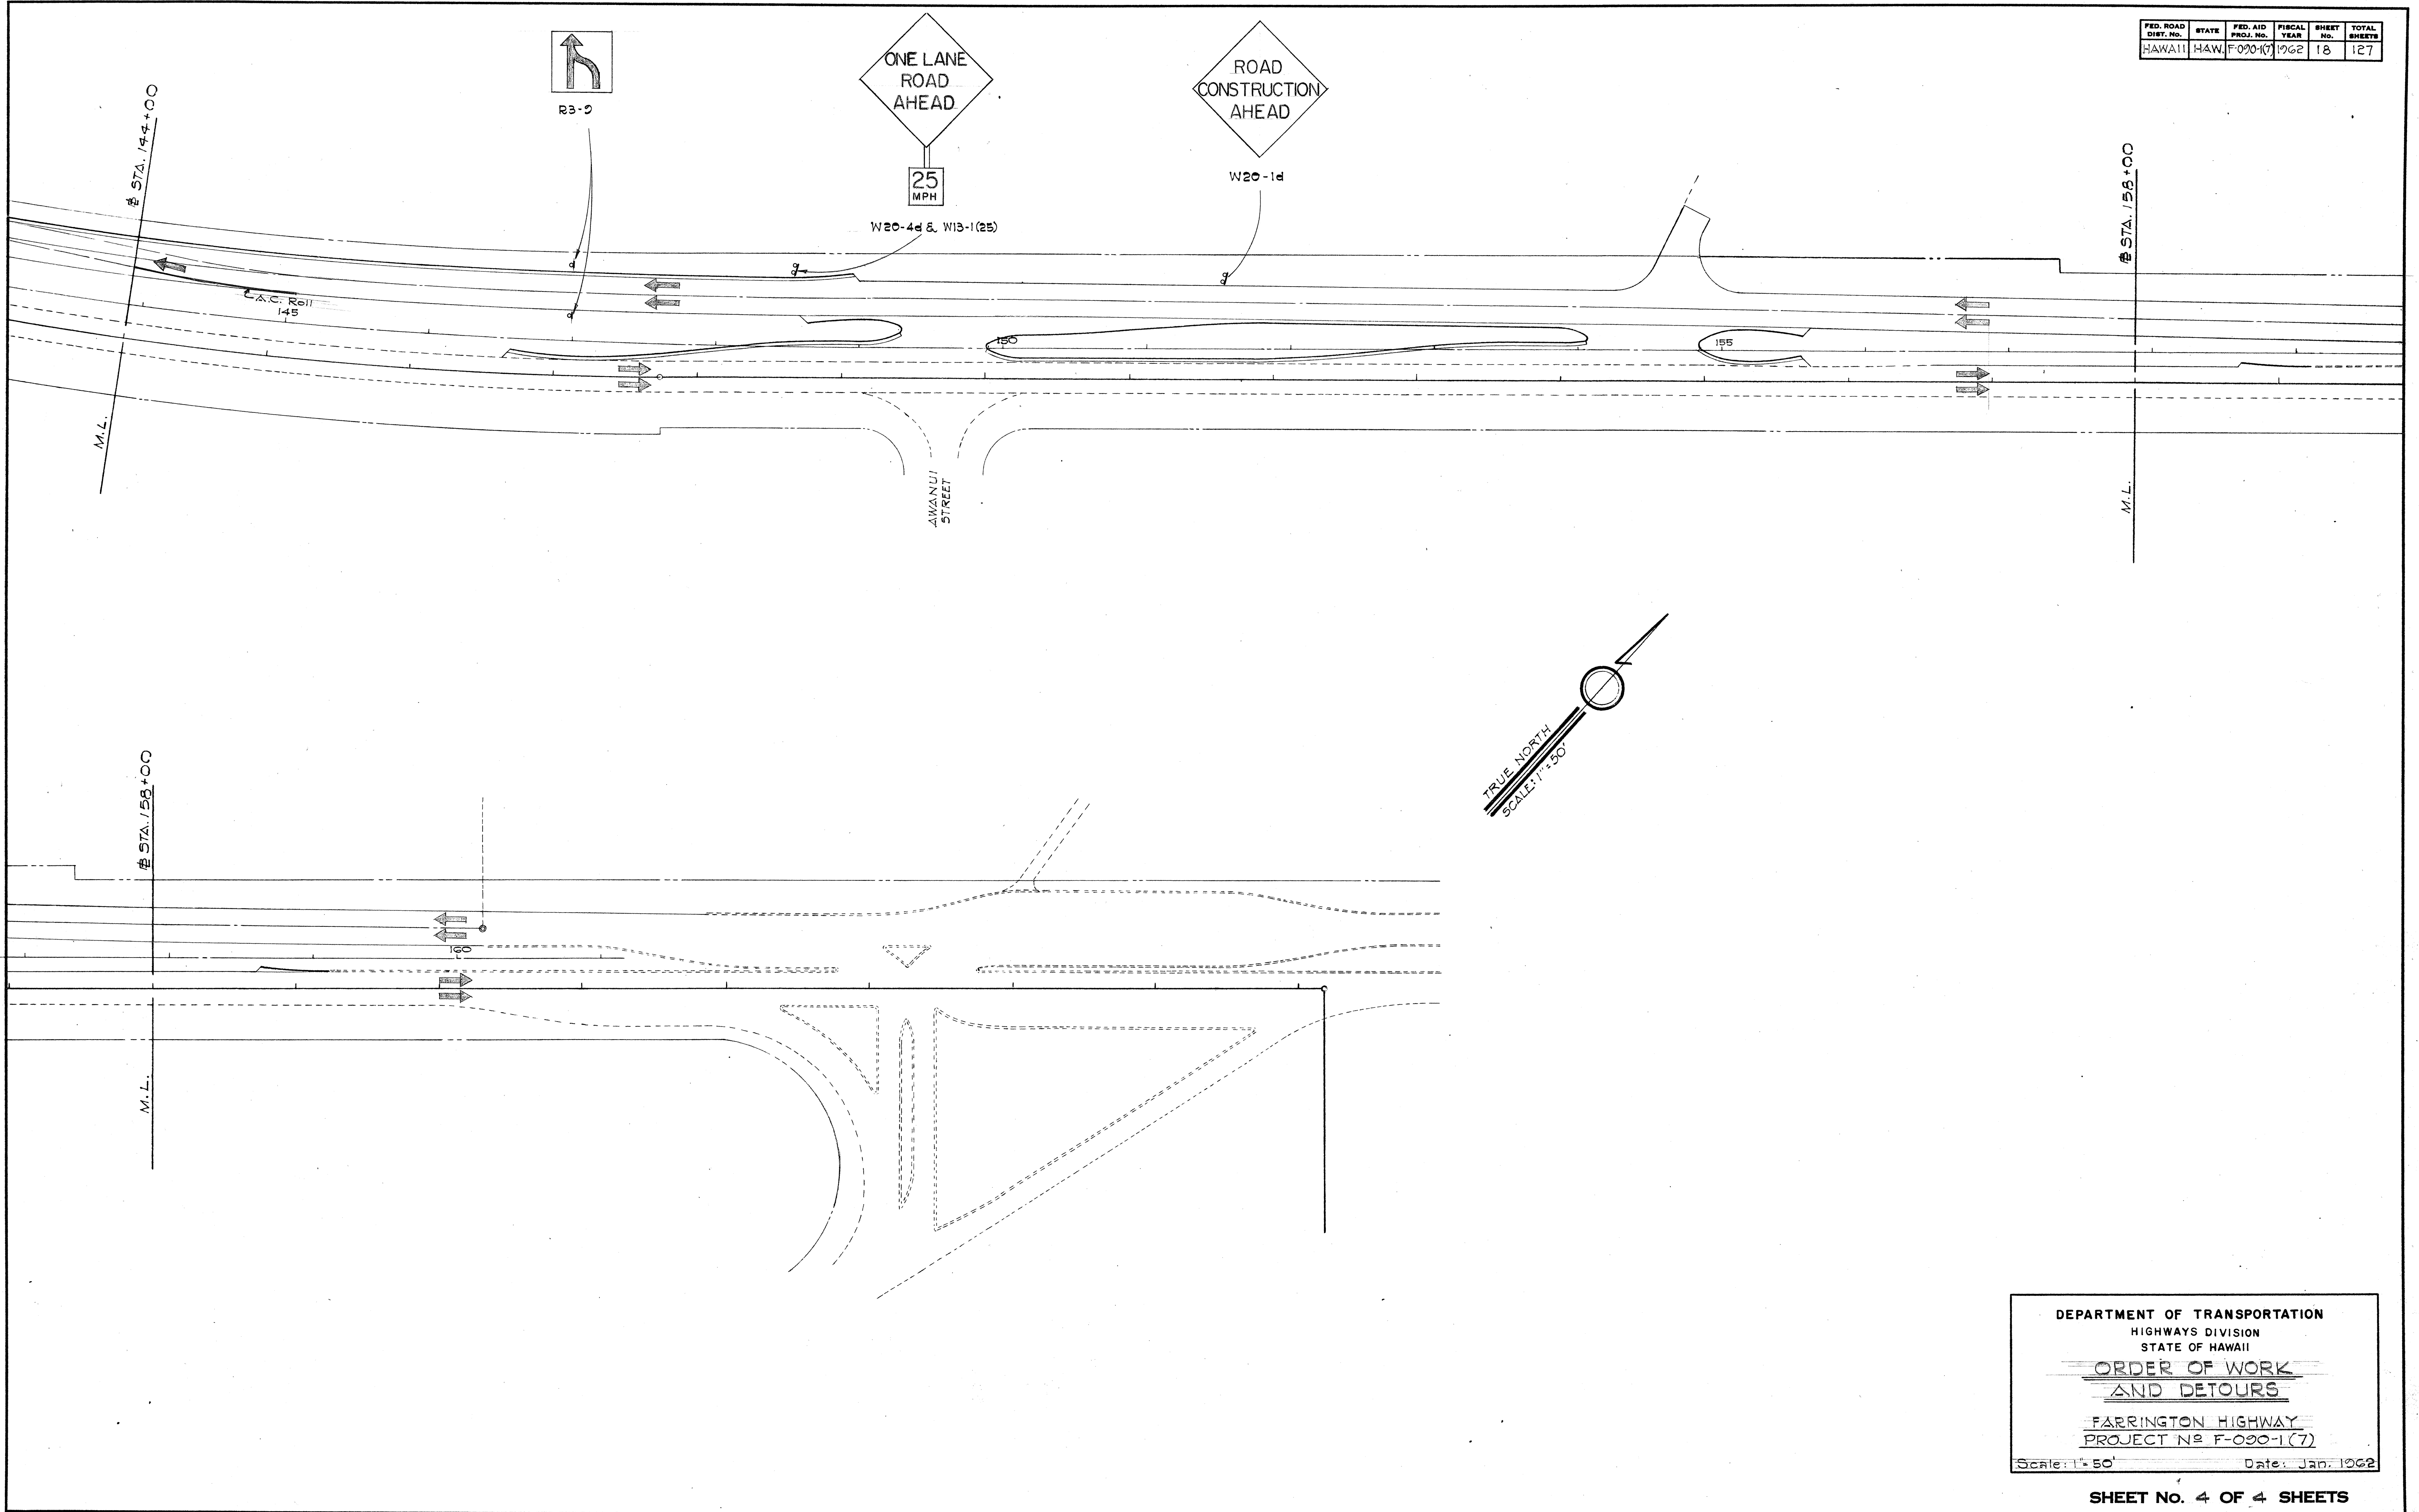

ORIGINAL PLAN	DATE
DESIGNED BY	
TRACED BY	
QUANTITIES BY	
CHECKED BY	
NOTE BOOK No.	

DEPARTMENT OF TRANSPORTATION
HIGHWAYS DIVISION
STATE OF HAWAII

**ORDER OF WORK
AND DETOURS**

FARRINGTON HIGHWAY
PROJECT NO. F-090-1(7)

Scale: 1"=50' Date: Jan. 1962

SHEET NO. 4 OF 4 SHEETS
