


FED. ROAD DIST. NO.	STATE	FED. AID PROJ. NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
HAWAII	HAW.	I-HI(48):9	1968	3	133

SURVEY PLANNED BY	DATE
DESIGNED BY	
PLANNED BY	
QUANTITIES BY	
CHECKED BY	
ORIGINAL PLAN	
NOTE BOOK	
No.	

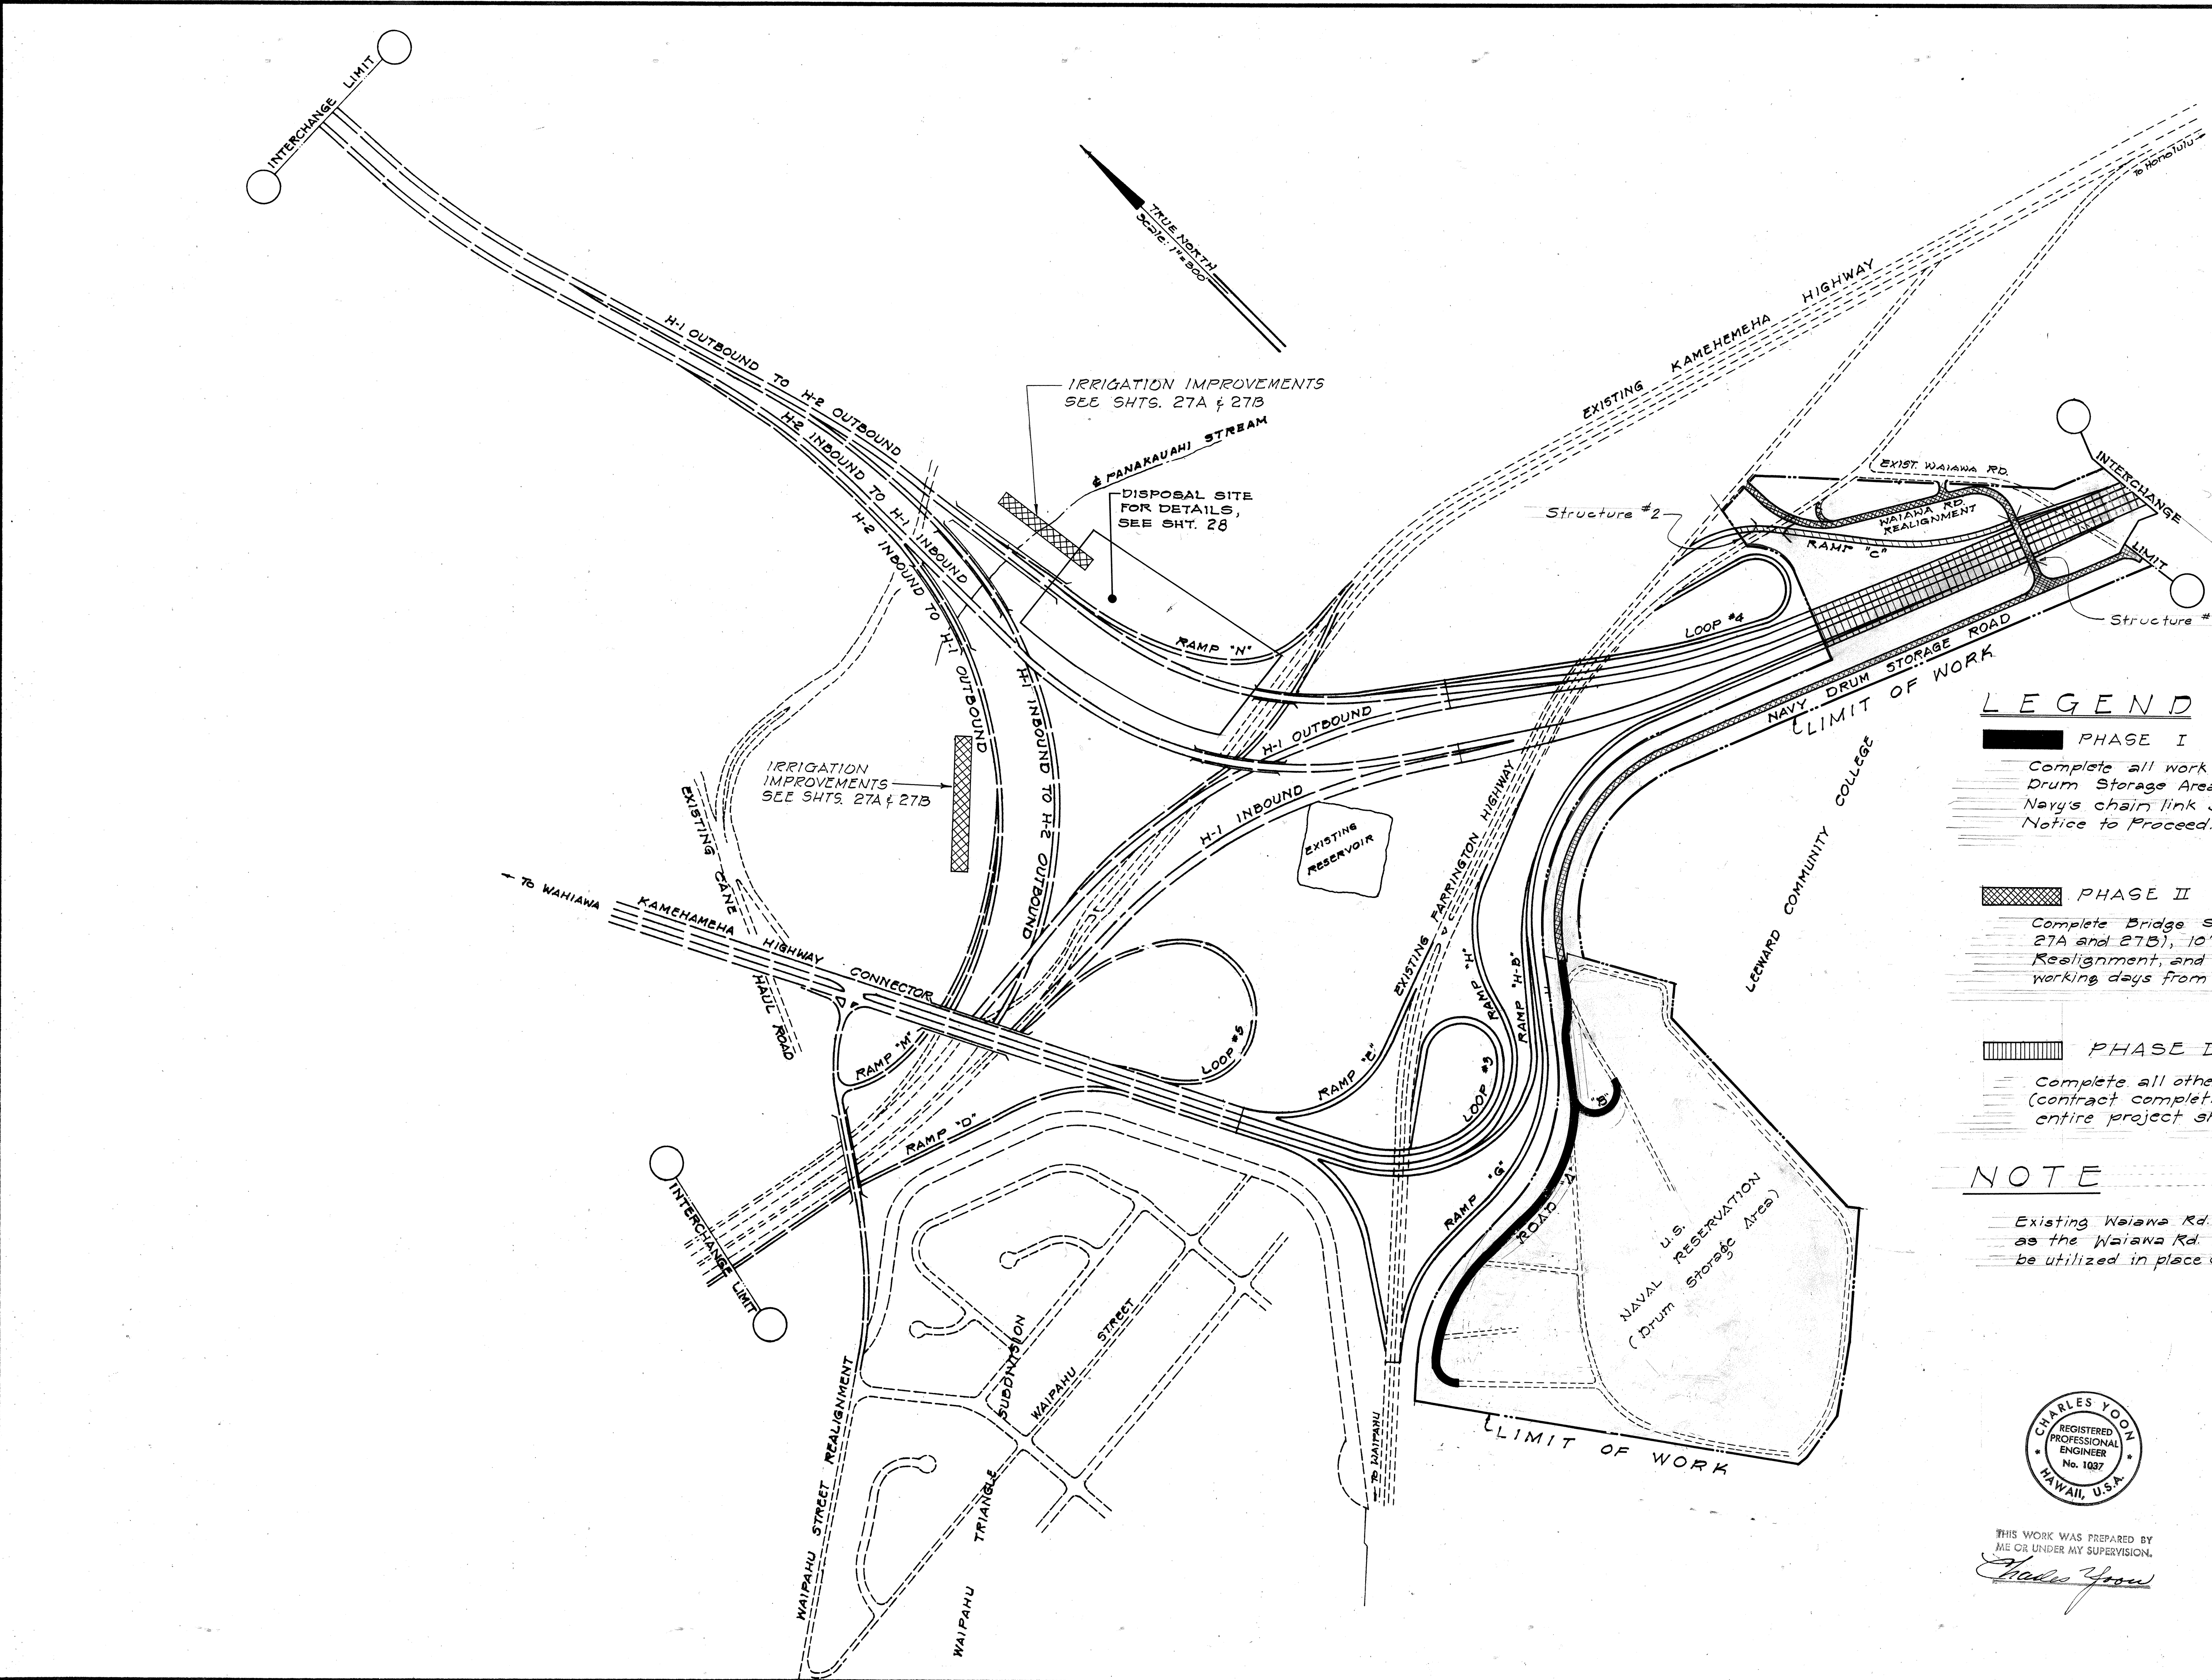

LEGEND

- PHASE I**


Complete all work required in the relocation of the existing Navy Drum Storage Area (sheets 16 to 18) together with relocating of the Navy's chain link security fence, within 30 working days from the Notice to Proceed.
- PHASE II**

Complete Bridge Structure No. 1, Irrigation Improvements (Sheets 27A and 27B), 10" Aviation gas lines, the Waiawa Road Realignment, and the Navy Drum Storage Road within 90 working days from the Notice to Proceed.
- PHASE III**

Complete all other remaining work within 180 working days (contract completion time) from the Notice to Proceed. The entire project should be completed at the end of this phase.

NOTE

- Existing Waiawa Rd. shall be kept open to traffic until such time as the Waiawa Rd. Realignment has been completed and may be utilized in place of the Existing Waiawa Road.



THIS WORK WAS PREPARED BY
ME OR UNDER MY SUPERVISION.
Charles Yoon

STATE OF HAWAII
DEPARTMENT OF TRANSPORTATION
HIGHWAYS DIVISION

CONSTRUCTION
PHASING

F.A.I. PROJ. NO. I-HI-1 (48):9
Scale: 1" = 300'

SHEET No. 1 OF 1 SHEETS
