



FED. ROAD DIST. NO.	STATE	FED. AID PROJ. NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
HAWAII	HAW.	I-HI-1(133):17	1981	2	153

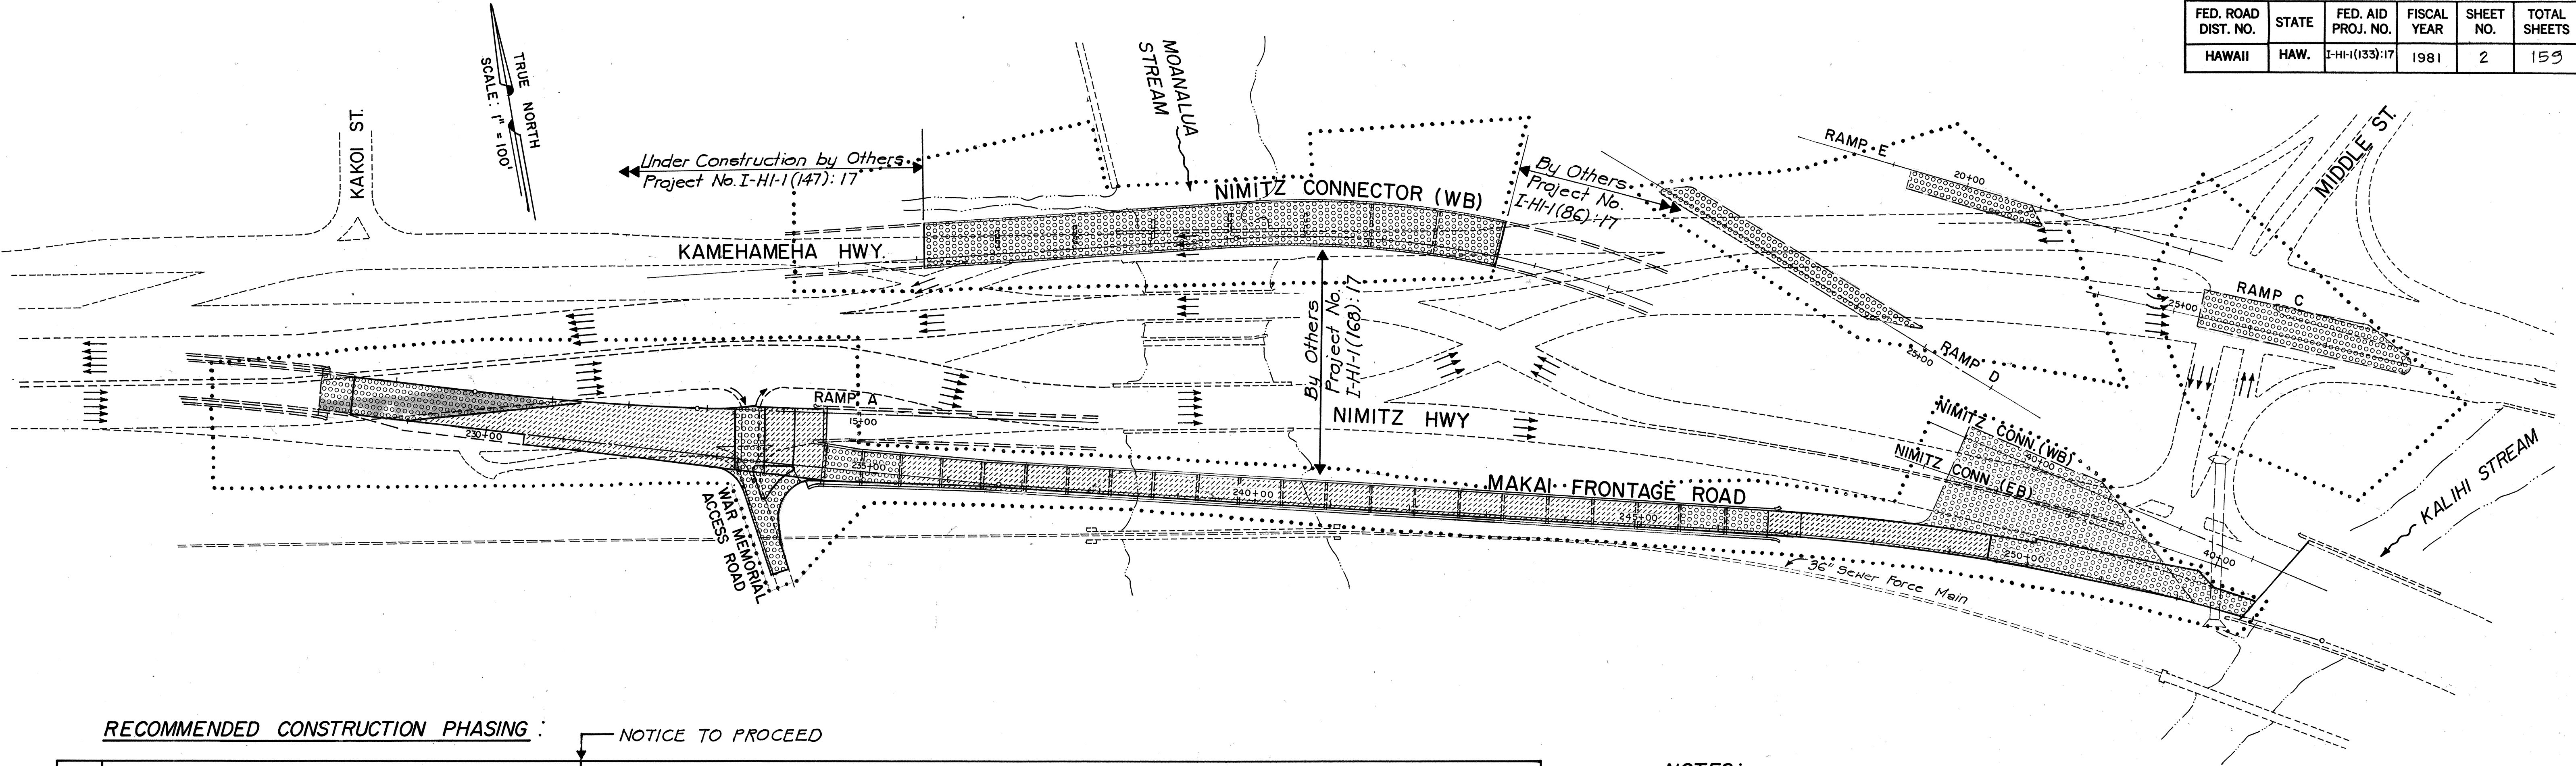

RECOMMENDED CONSTRUCTION PHASING :

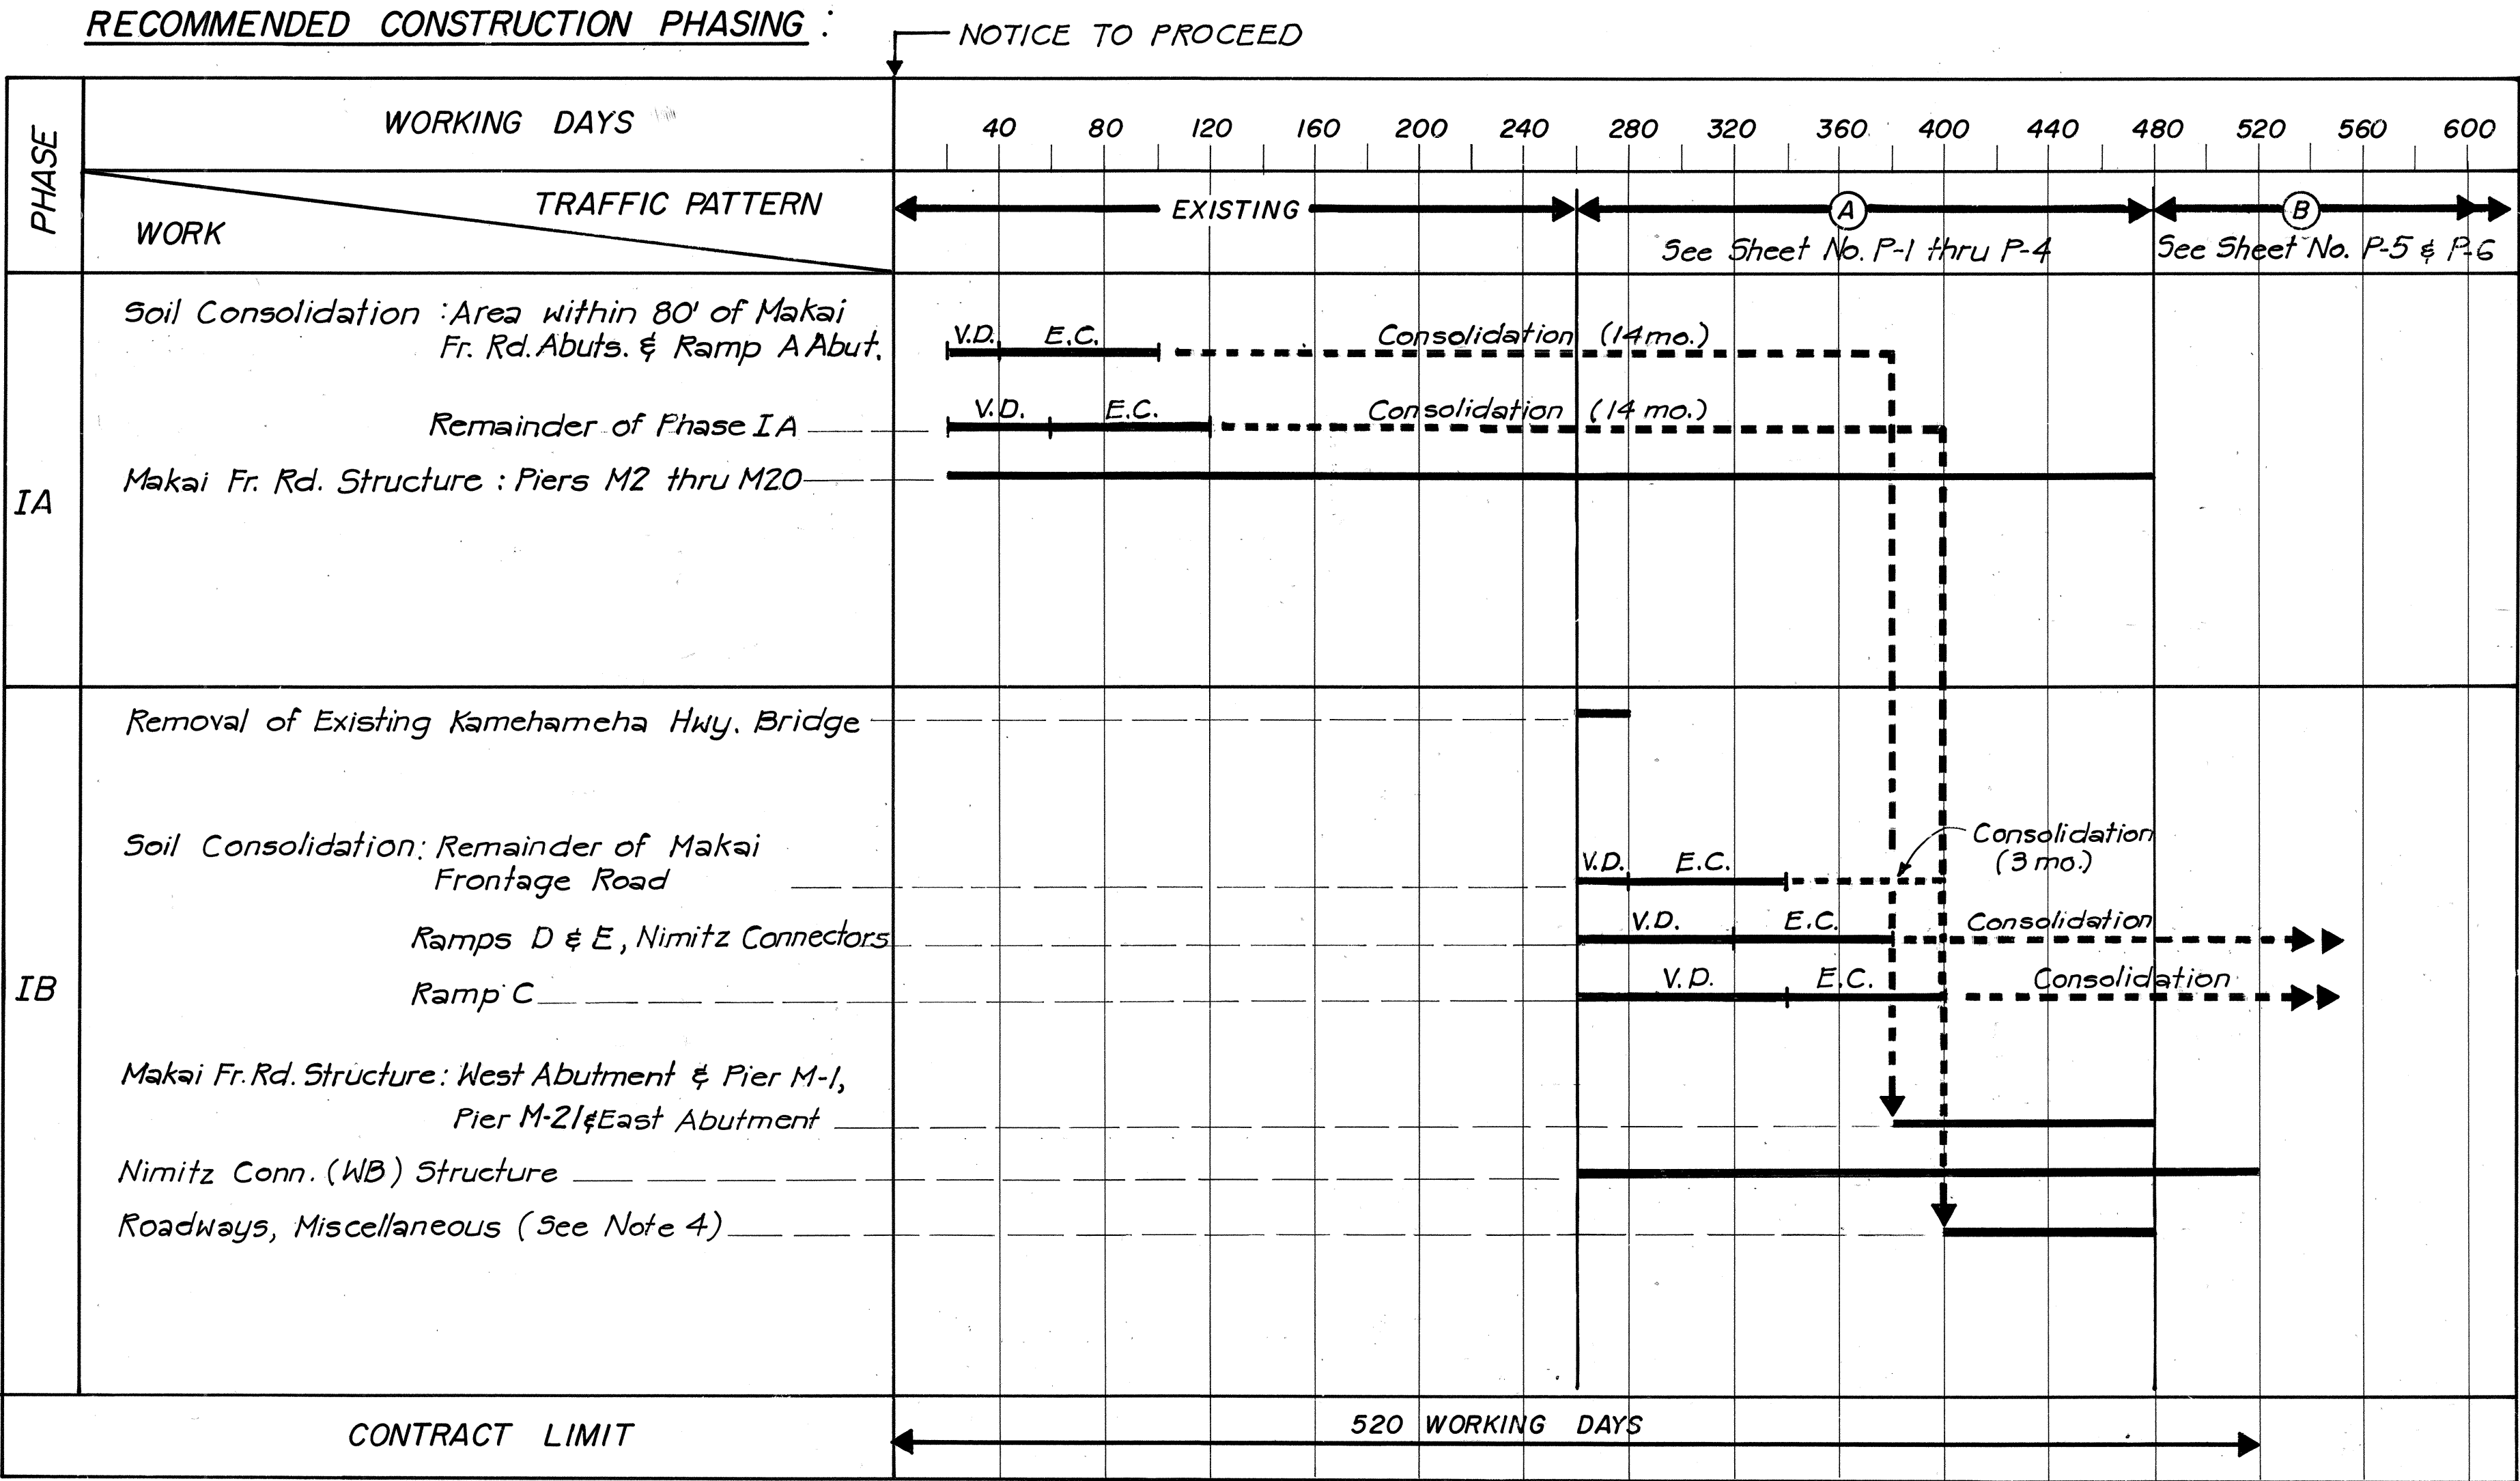


NOTES:

- For mandatory completion requirements see Special Provisions, Subsection 108.03
- The Contractor shall submit to the Engineer for approval a Traffic Control Plan (TCP) for each traffic pattern change not shown herein. The TCP shall be in full accordance with FHFM 6-4-2.12.
- For restrictions on embankment & surcharge construction, begin & end of consolidation period, etc., see Special Provisions Section 203 and Soil Consolidation Plans.
- Placing of pavement structure at Makai Front Road Sta. 252+50± shall be delayed until Contractor of Project I-HI-1(86):17 has completed the box culvert and the Engineer authorizes placing of pavement structure. Authorization will be issued at least 40 working days prior to implementation of Traffic Pattern B.

LEGEND

- PHASE IA
- PHASE IB
- EXISTING TRAFFIC LANES
- V.D. INSTALLATION OF VERTICAL DRAINS
- E.C. EMBANKMENT CONSTRUCTION
- APPROXIMATE LIMITS OF AVAILABLE WORK AREA DURING PHASE IB. (WORK AREA DURING PHASE IA IS CONTROLLED BY EXISTING TRAFFIC PATTERN & CONSTRUCTION ACTIVITIES OF PROJECT NO. I-HI-1(147):17)

SURVEY PLOTTED BY	DATE
DRAWN BY	
TRACED BY	
QUANTITIES BY	
CHECKED BY	
ORIGINAL PLAN	
NOTE BOOK	
No.	



THIS WORK WAS PREPARED BY ME OR UNDER MY SUPERVISION.

STATE OF HAWAII
DEPARTMENT OF TRANSPORTATION
HIGHWAYS DIVISION

RECOMMENDED
CONSTRUCTION PHASING

INTERSTATE ROUTE H-1
PROJECT NO. I-HI-1(133):17

SCALE : 1" = 100'

DATE : 4/30/81

SHEET No. CP-1 OF 1 SHEETS
