
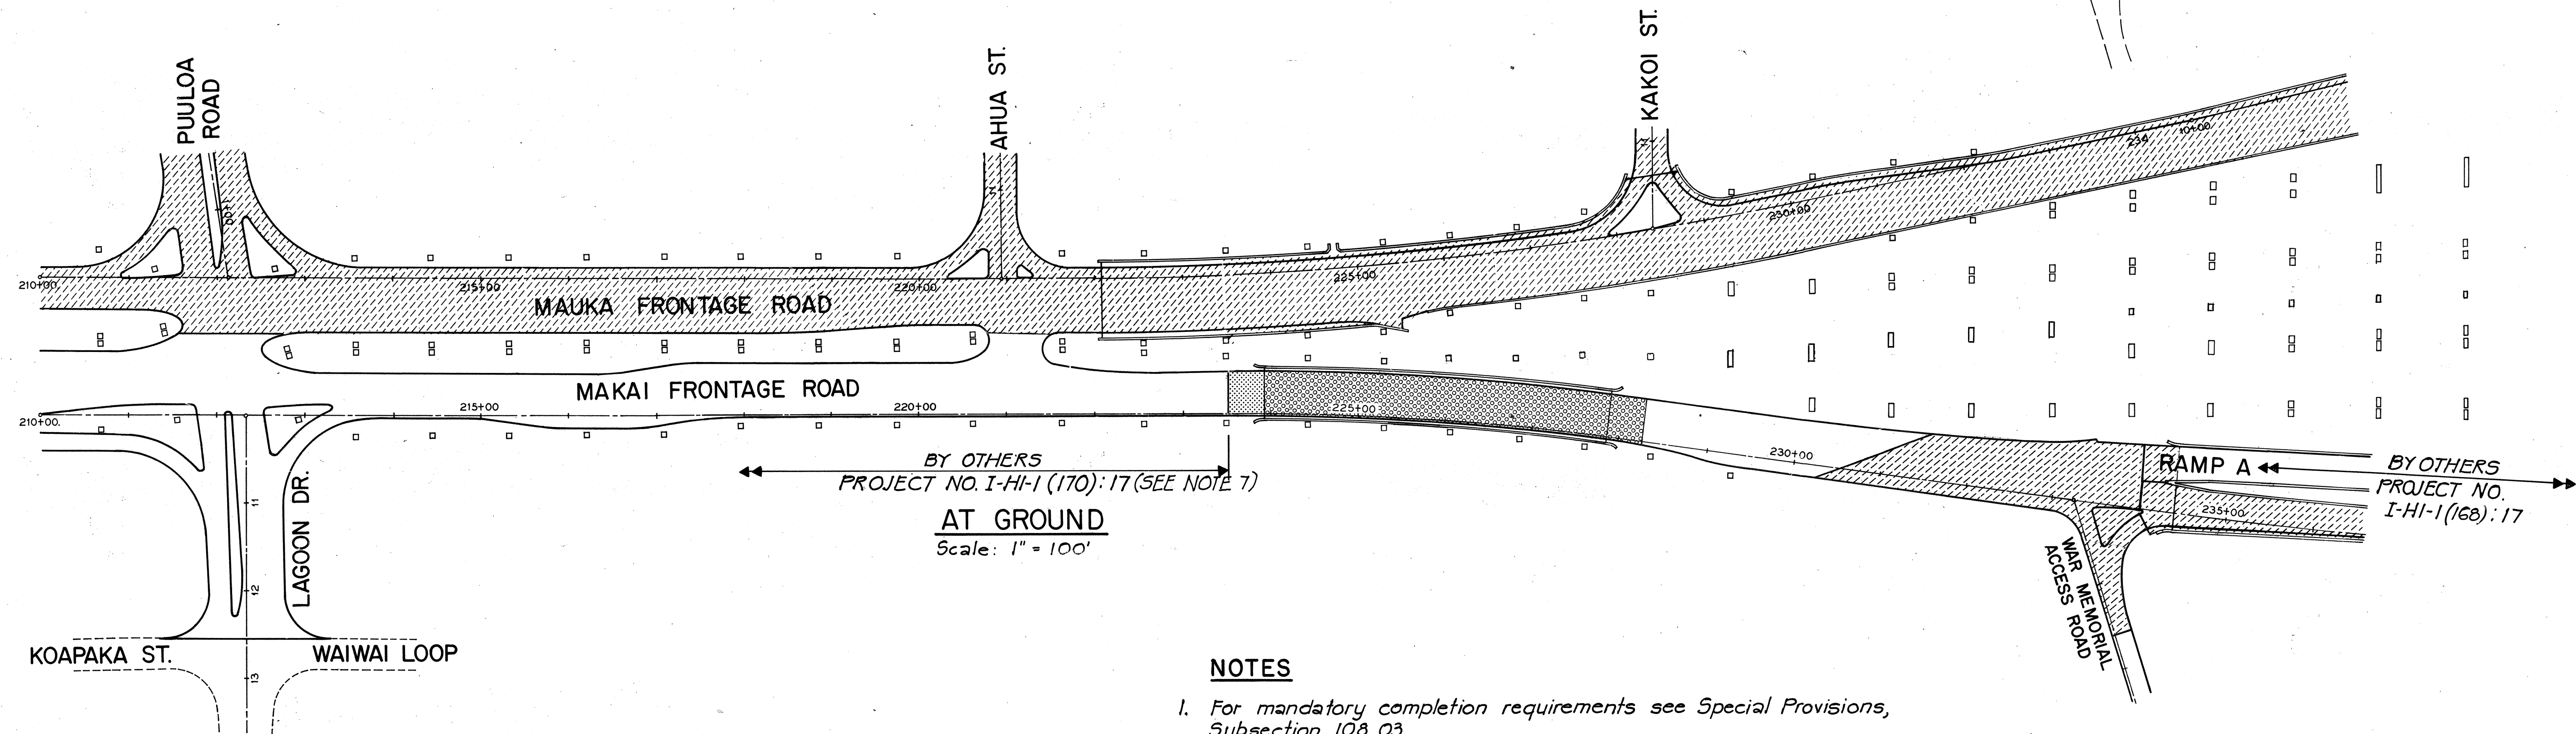


FED. ROAD DIST. NO.	STATE	FED. AID PROJ. NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
HAWAII	HAW.	I-HI-1(132):17	1983	2	192

LEGEND

	EXISTING
	PHASE II
	PHASE III
	UNDER CONSTRUCTION BY OTHERS

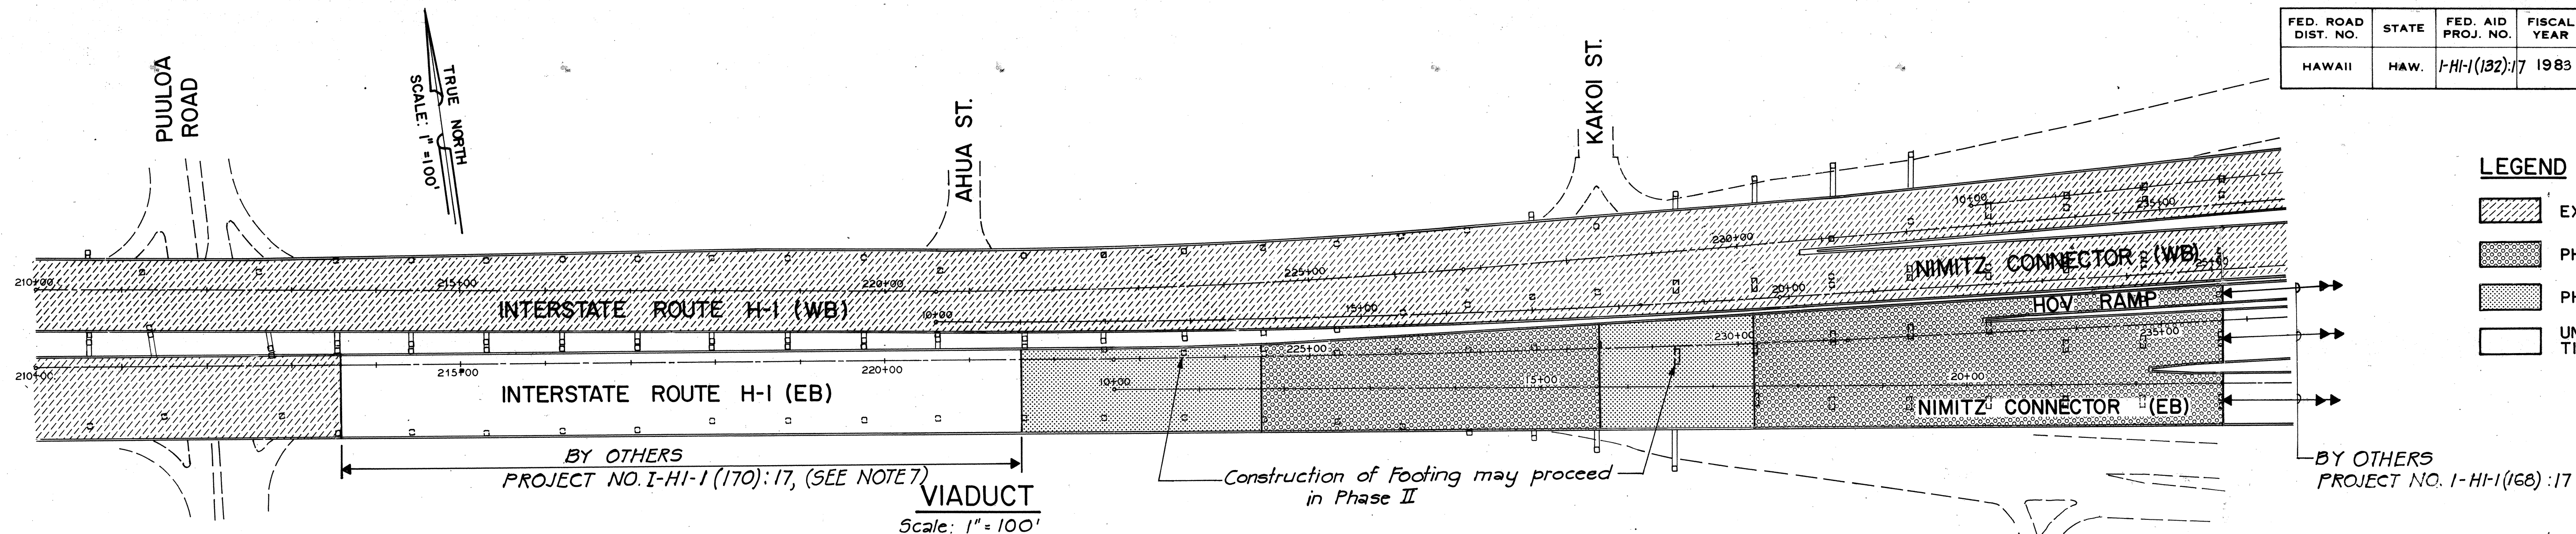


NOTES

- For mandatory completion requirements see Special Provisions, Subsection 108.03.
- The Contractor shall submit to the Engineer for approval a Traffic Control Plan (TCP) for each traffic pattern change not shown herein. The TCP shall be in full accordance with FHPM 6-4-2-12.
- Drainage Channel #3 shall be constructed during Phase II. (See Sheets D-1 & D-2 for additional phasing requirements)
- Pier No. 29 of H-1 (EB), NC (EB) and HOV Ramp shall be completed within 160 working days from the Notice-to-Proceed.
- Pier No. 13 shall be completed within 360 working days from the Notice-to-Proceed.
- Viaduct decks shall be completed and ready for installation of pavement markings within 460 working days from the Notice-to-Proceed.
- It is estimated that major construction work for Project No. I-HI-1(170):17 will commence 200 working days from the Notice-to-Proceed.
- Prestressed Concrete Girders will be furnished by Others.

CONSTRUCTION PHASING:

	NOTICE TO PROCEED	WORKING DAYS
		80 160 240 320 400 480 560 640 720
TRAFFIC PATTERN	SEE SHEET P-1	SEE SHEETS P-2 & P-3
PHASE II		
PHASE III		
CONTRACT LIMIT	480 WORKING DAYS	

7/20/83	Revised Construction Phasing & Completion Requirements.
DATE	REVISION
STATE OF HAWAII DEPARTMENT OF TRANSPORTATION HIGHWAYS DIVISION	
CONSTRUCTION PHASING (RECOMMENDED)	
INTERSTATE ROUTE H-1 PROJECT NO. I-HI-1(132):17	
SCALE: 1" = 100'	DATE: 11/16/81
SHEET NO. CP-1 OF 1 SHEETS	



THIS WORK WAS PREPARED BY
ME OR UNDER MY SUPERVISION.
Werner Beugert
