


| FED. ROAD DIST. NO. | STATE | FED. AID PROJ. NO. | FISCAL YEAR | SHEET NO. | TOTAL SHEETS |
|---------------------|-------|--------------------|-------------|-----------|--------------|
| HAWAII              | HAW.  | 17(170):17         | 1983        | 2         | 211          |

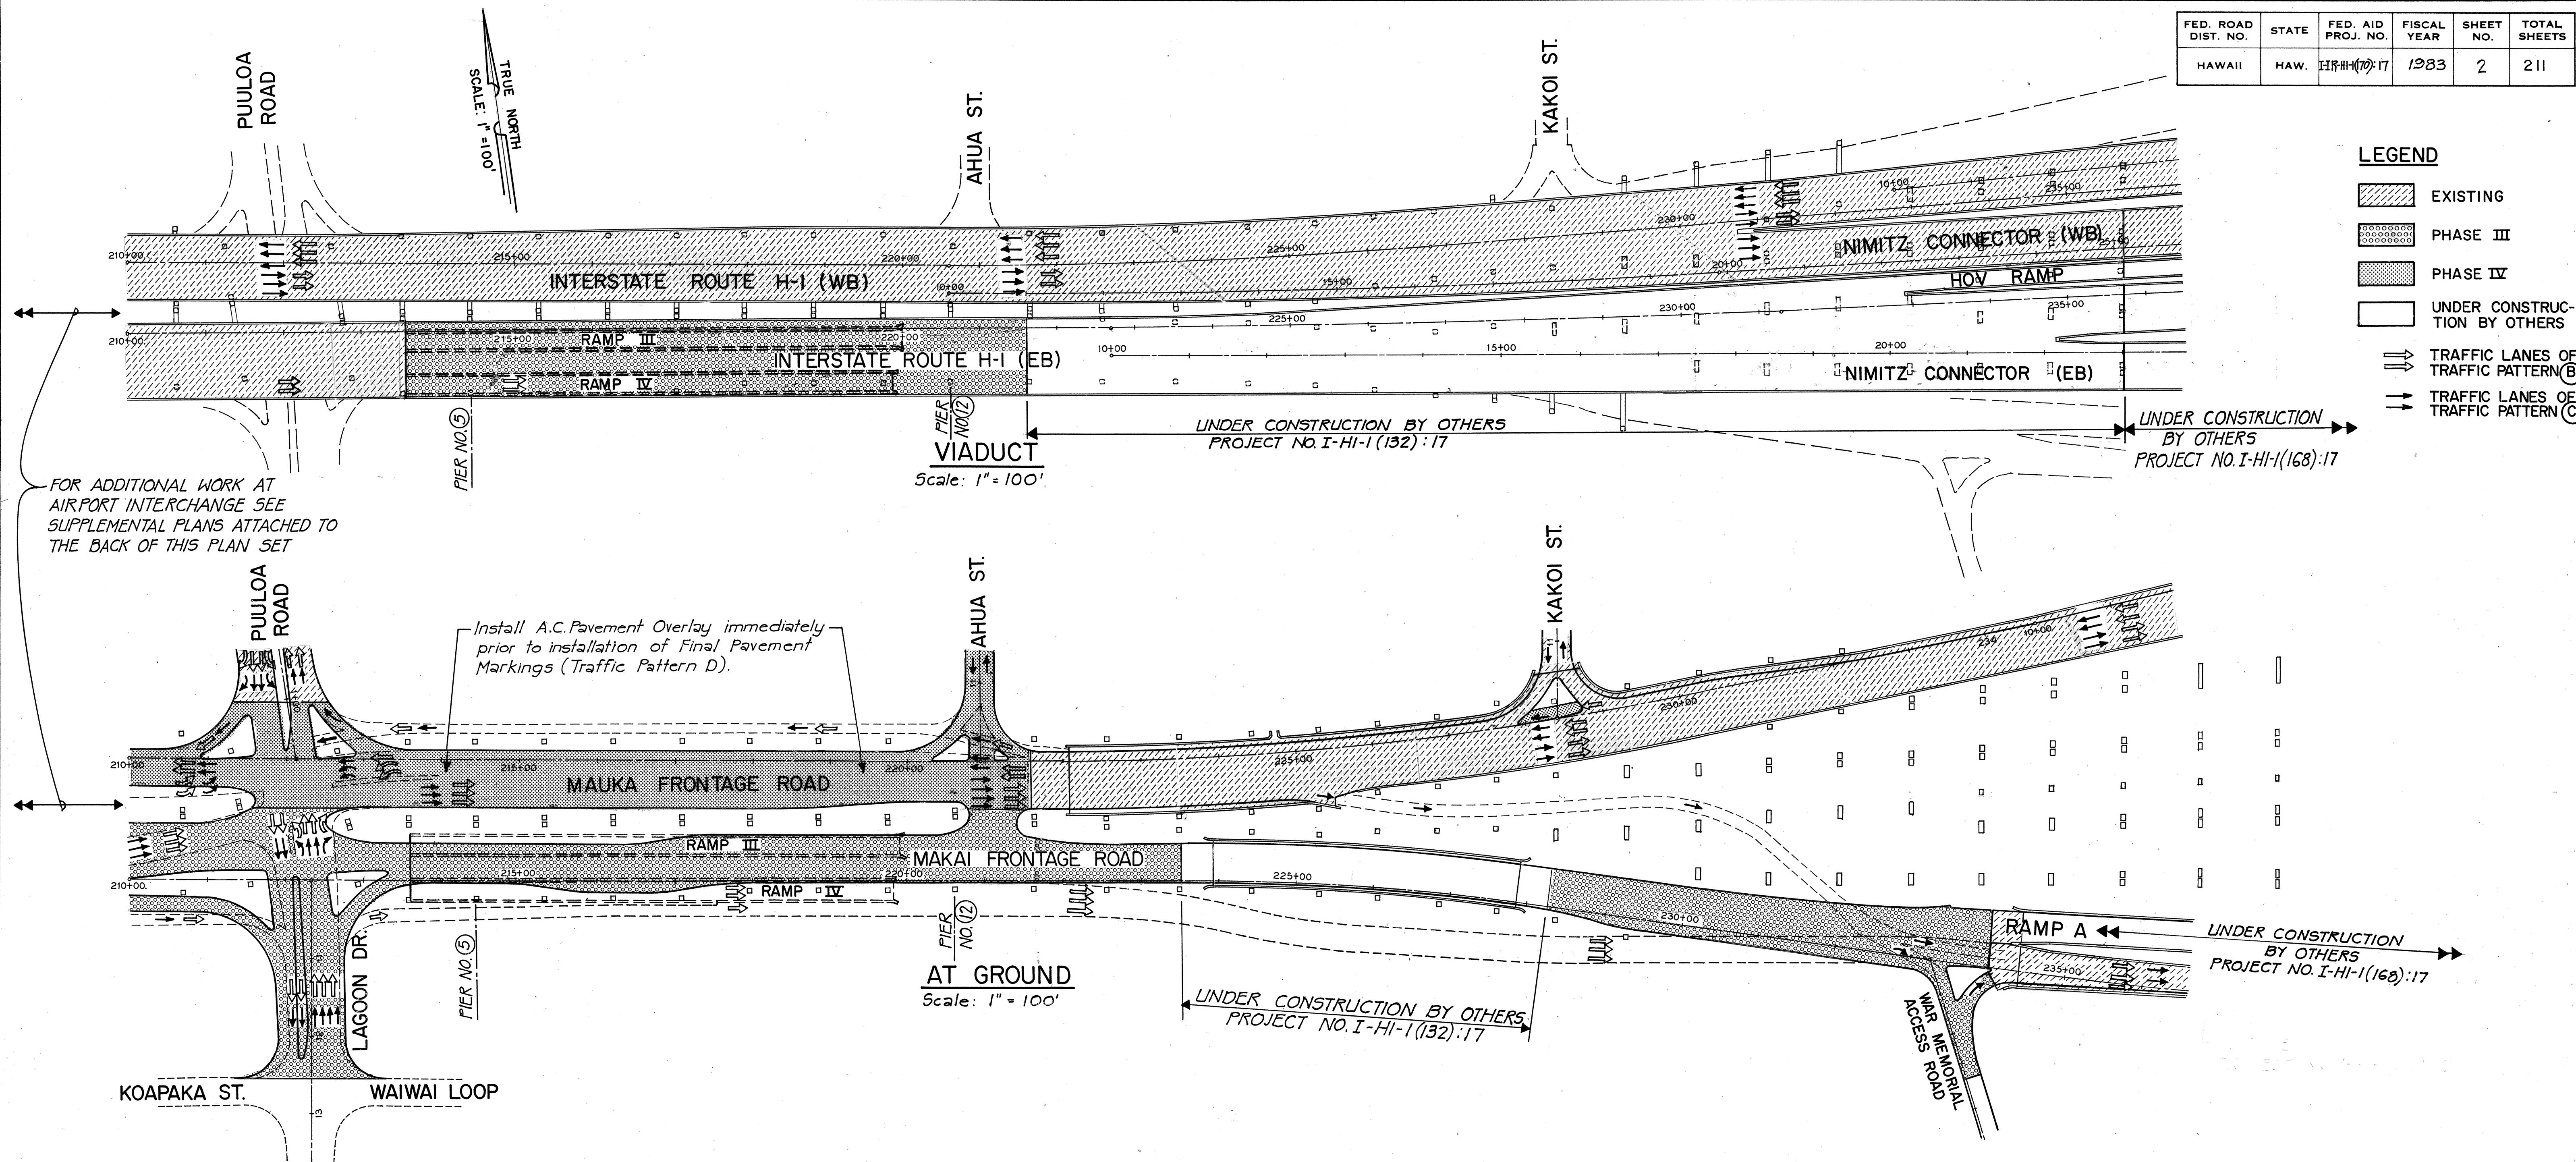

- LEGEND**
- EXISTING
  - PHASE III
  - PHASE IV
  - UNDER CONSTRUCTION BY OTHERS
  - TRAFFIC LANES OF TRAFFIC PATTERN (B)
  - TRAFFIC LANES OF TRAFFIC PATTERN (C)

FOR ADDITIONAL WORK AT AIRPORT INTERCHANGE SEE SUPPLEMENTAL PLANS ATTACHED TO THE BACK OF THIS PLAN SET


Install A.C. Pavement Overlay immediately prior to installation of Final Pavement Markings (Traffic Pattern D).

# CONSTRUCTION PHASING:

|                           | NOTICE TO PROCEED     | WORKING DAYS        |                |     |     |     |     |                        |     |     |     |
|---------------------------|-----------------------|---------------------|----------------|-----|-----|-----|-----|------------------------|-----|-----|-----|
|                           |                       | 80                  | 160            | 240 | 320 | 400 | 480 | 560                    | 640 | 720 | 800 |
| TRAFFIC PATTERN           | (B) → (C) → (D) → (E) | SEE THIS SH. & P-3A | SEE THIS SHEET |     |     |     |     | SEE SHEET P-5A         |     |     |     |
| MOBILIZATION (SEE NOTE 3) |                       |                     |                |     |     |     |     | SEE SHTS. P-1 THRU P-5 |     |     |     |
| PHASE III                 |                       |                     |                |     |     |     |     |                        |     |     |     |
| PHASE IV                  |                       |                     |                |     |     |     |     |                        |     |     |     |
| CONTRACT LIMIT            |                       | 370 WORKING DAYS    |                |     |     |     |     |                        |     |     |     |

## NOTES:

- For mandatory completion requirements see Special Provisions, Subsection 108.03.
- The Contractor shall submit to the Engineer for approval a Traffic Control Plan (TCP) for each traffic pattern change not shown herein. The TCP shall be in full accordance with FHPM G-4-2-12.
- Shift traffic from Ramp IV to Ramp III, and remove Ramp IV Structure. This permits construction of Makai Footings of H-1 (EB) Pier Nos (5) through (12) during Traffic Pattern (B).
- Shown Construction Phasing identifies only major construction activities. Certain specific work items, such as construction of curbs, which prevent maintaining traffic in accordance with the requirements of Special Provisions Subsection 104.04, shall be deferred until a later construction phase.



THIS WORK WAS PREPARED BY ME OR UNDER MY SUPERVISION.

STATE OF HAWAII  
DEPARTMENT OF TRANSPORTATION  
HIGHWAYS DIVISION

CONSTRUCTION PHASING  
(RECOMMENDED)  
INTERSTATE ROUTE H-1  
PROJECT NO. I-IR-HI-1(170):17

SCALE: 1" = 100' DATE: 12/15/81  
SHEET NO. CP-1 OF 1 SHEETS
