



FED. ROAD DIST. NO.	STATE	FED. AID PROJ. NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
HAWAII	HAW.	I-H3-1(53)	1988	2	124

- NOTE:
- CONSTRUCTION PHASE 1: Suggested Sequence of Work.
 - Excavate for Tunnel.
 - Utilize Tunnel Material to Construct Roadway Embankment.
 - Construct Tunnel.
 - Backfill Tunnel with Material from Red Dirt Cut.
 - Complete Roadway Embankment with Remainder of Red Dirt Cut.
 - Complete Roadway Construction to Sta. 330+10.
 - CONSTRUCTION PHASE 2:
 - Complete Roadway Construction from Sta. 330+10 to Sta. 335+00.
 - Contractor Will Not be Allowed to Work within Construction Phase 2 Area Until 18 Months After Notice to Proceed.

- NOTES:
- Unless approved otherwise, the Contractor shall keep the Haiku Access Road open to traffic for use by other Contractors during the progress of the work.
 - As ordered by the Engineer, relocate the Haiku Access Road. Cost of the relocation work complete in place including earthwork, pavement structure, temporary drainage, walls for the access road, mulching, traffic delineators, traffic control devices, etc., will be paid for on a force account basis under the pay item "Relocation of Haiku Access Road."
 - The relocation of the Haiku Access Road shall be included in the GPM schedule as required under the sub-section 100.03 "Prosecution and Progress" constructed by other project.

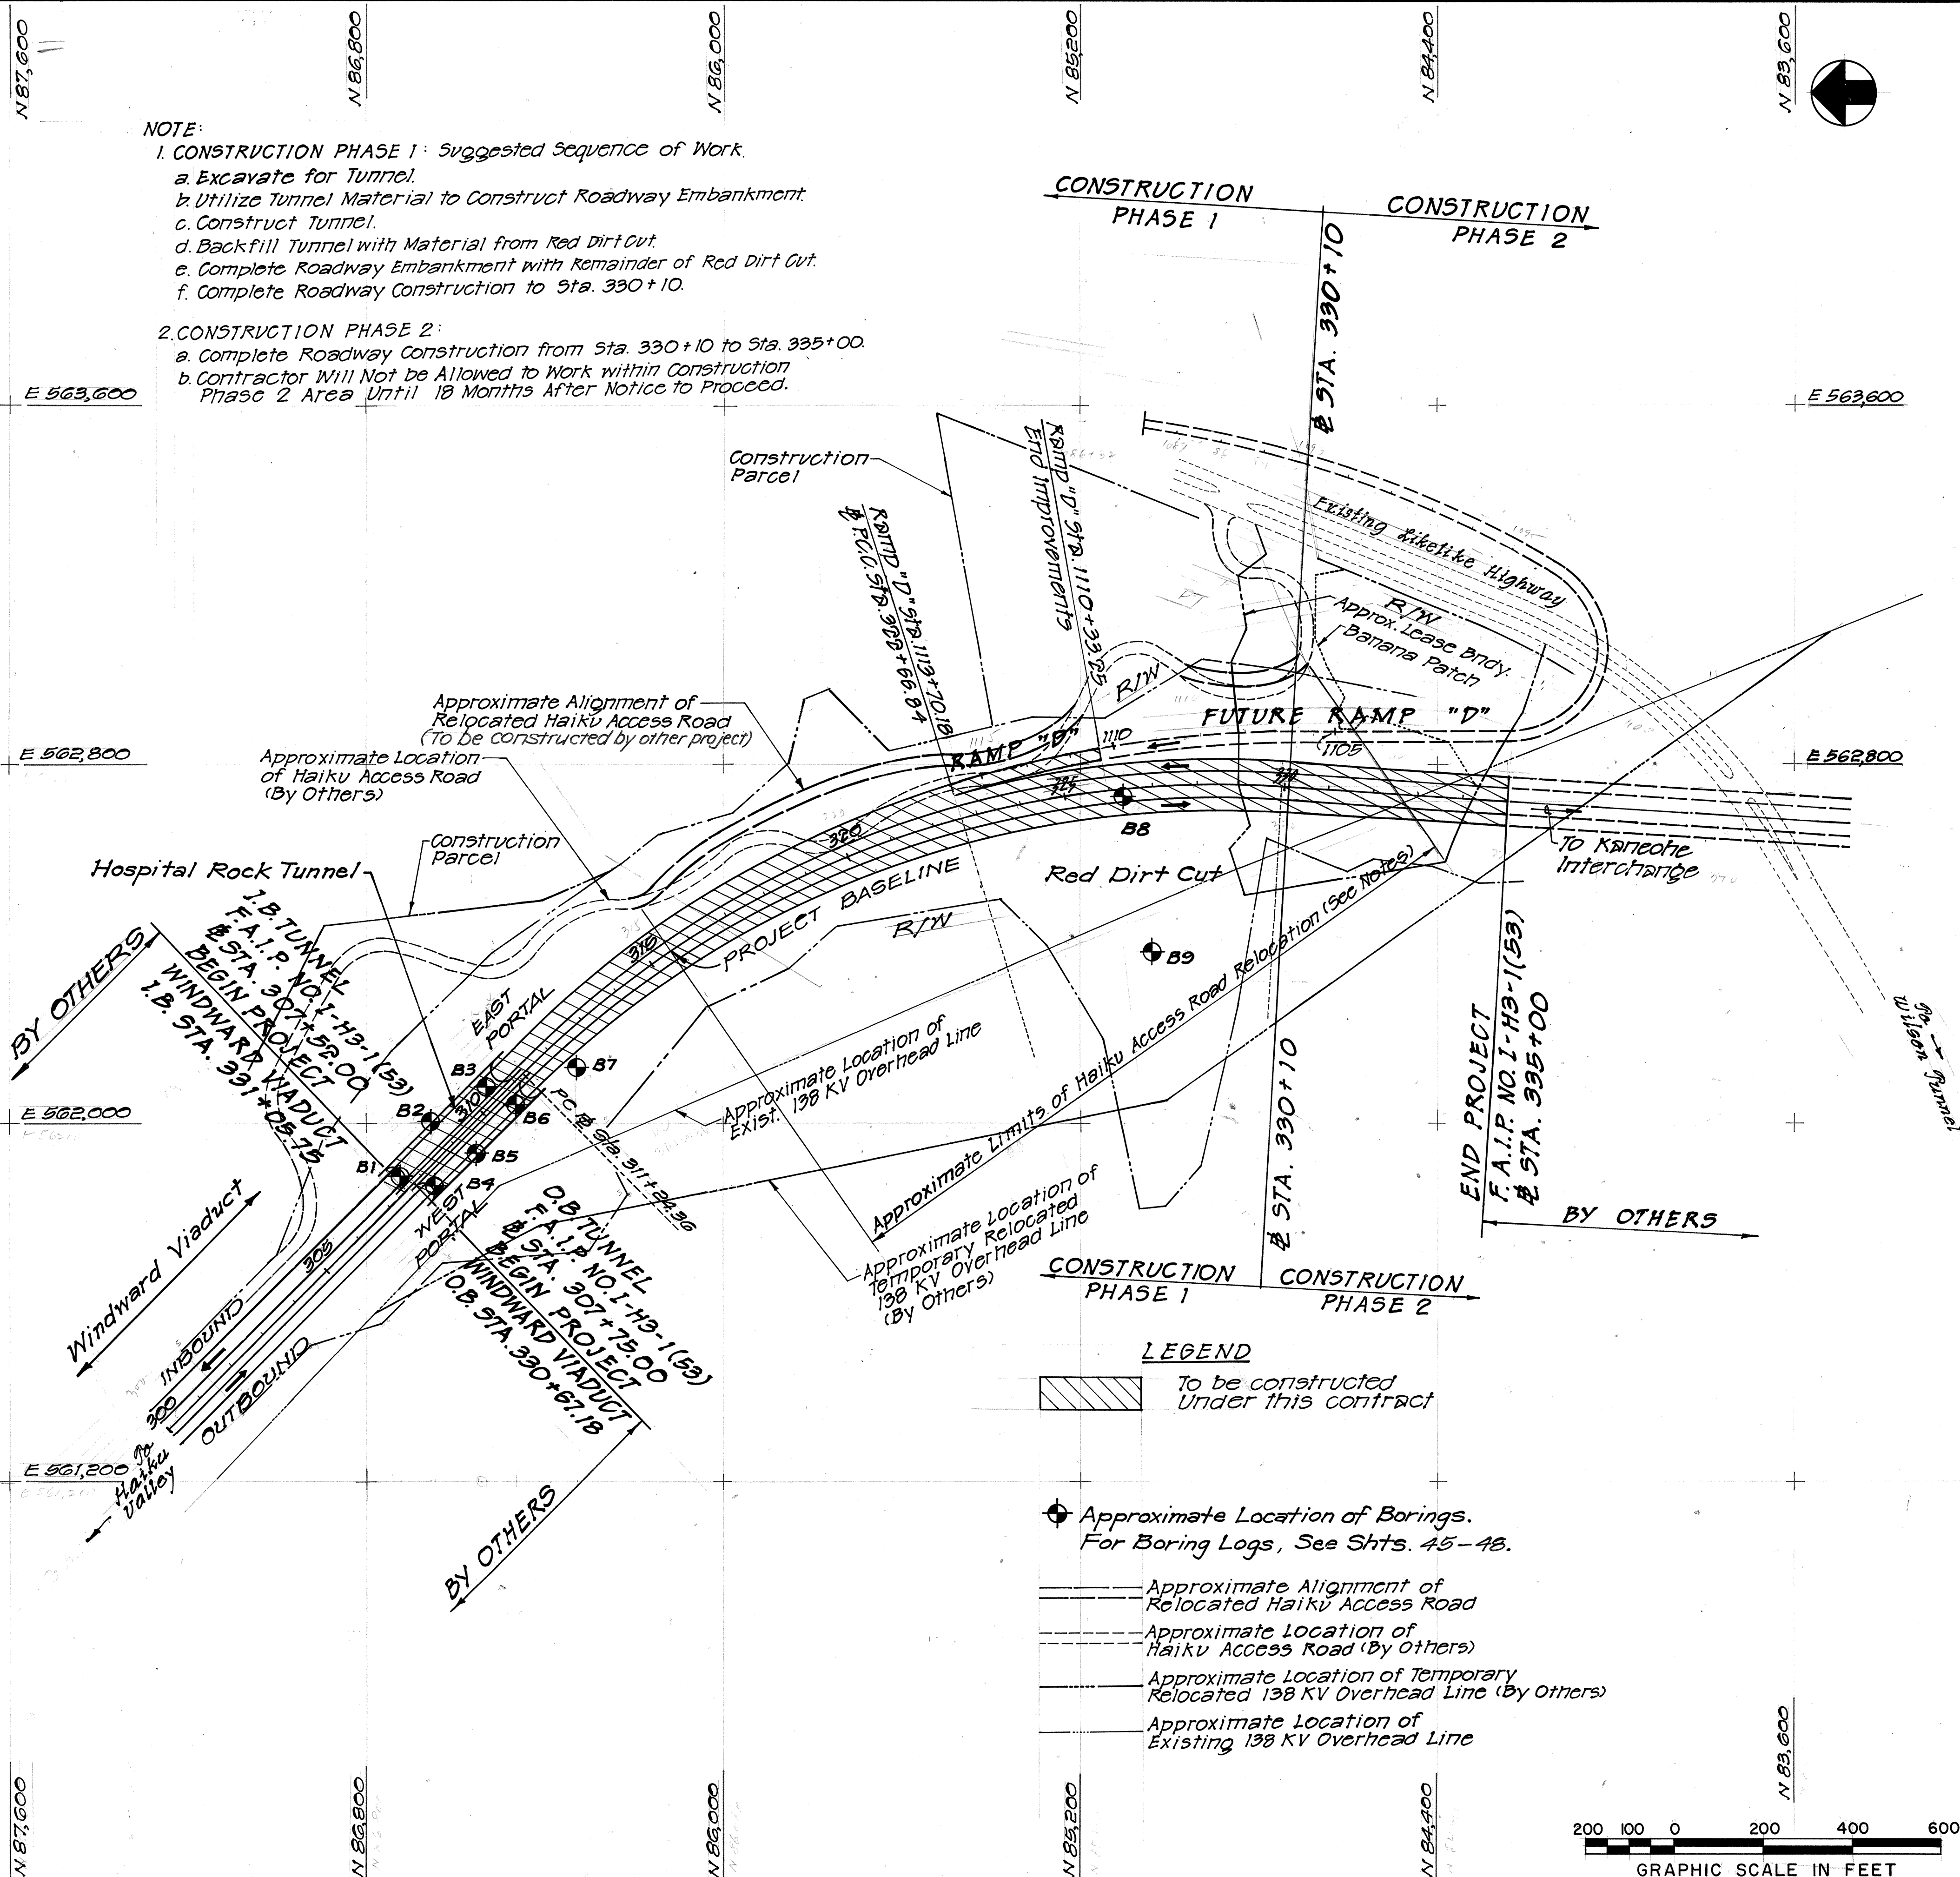

THIS WORK WAS PREPARED BY
ME OR UNDER MY SUPERVISION.
Robert L. Haghi

STATE OF HAWAII
DEPARTMENT OF TRANSPORTATION
HIGHWAYS DIVISION

GENERAL PLAN

INTERSTATE ROUTE H-3
F.A.I. PROJ. NO. I-H3-1(53)

SCALE: AS NOTED DATE: AUG., 1988

SHEET NO. 1 OF 1 SHEETS

ORIGINAL PLAN	DATE
DRAWN BY	
CHECKED BY	
NOTED BY	
CHECKED BY	
