


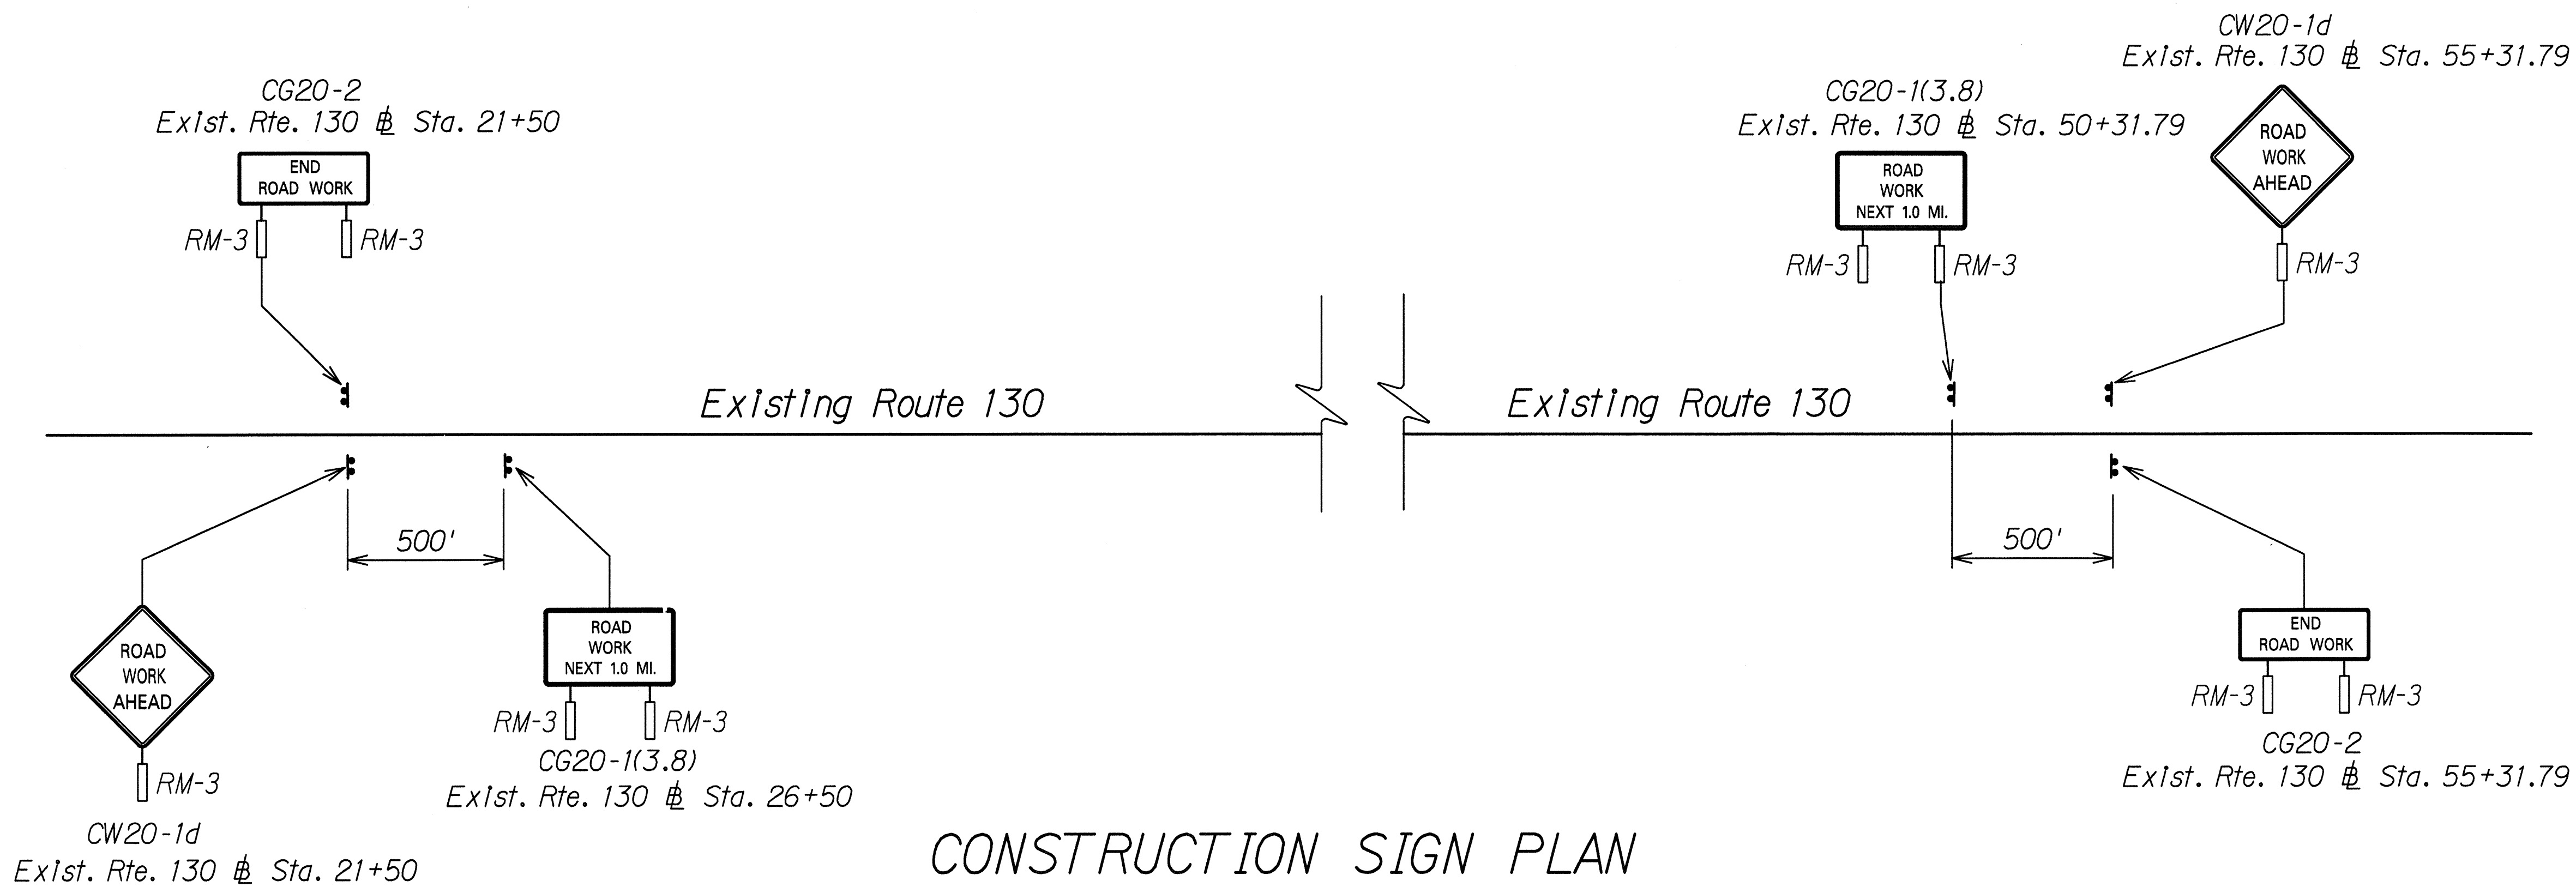

CONSTRUCTION SIGN SCHEDULE				
ROAD AND LOCATION *	STATION	LEFT	RIGHT	ITEM No. 621.7120 (two posts)
(Route 11)	I.B.L. 11 Sta 1087+90.00		●	CW20-1d
	I.B.L. 11 Sta 1092+90.00		●	CG20-1(3.8)
	O.B.L. 11 Sta 1088+60.00	●		CG20-2
	O.B.L. 11 Sta 1119+35.48	●		CG20-1(3.8)
	O.B.L. 11 Sta 1124+35.48	●		CW20-1d
	I.B.L. 11 Sta 1126+50		●	CG20-2
(M110 St.)	Bypass @ Sta 38+34 (500' L)	●		CG20-2
	Bypass @ Sta 38+34 (500' L)	●		CW20-1d
	Bypass @ Sta 38+34 (500' R)		●	CG20-2
	Bypass @ Sta 38+34 (500' R)		●	CW20-1d

CONSTRUCTION SIGN SCHEDULE CONT.				
ROAD AND LOCATION *	STATION	LEFT	RIGHT	ITEM No. 621.7120 (two posts)
(Route 130)	Exist. Rte. 130 @ Sta 21+50	●		CG20-2
	Exist. Rte. 130 @ Sta 21+50		●	CW20-1d
	Exist. Rte. 130 @ Sta 26+50		●	CG20-1(3.8)
	Exist. Rte. 130 @ Sta 50+31.79	●		CG20-1(3.8)
	Exist. Rte. 130 @ Sta 55+31.79	●		CW20-1d
	Exist. Rte. 130 @ Sta 55+31.79		●	CG20-2
	Total Construction Signs			16

SURVEY PLOTTED BY	DATE
DESIGNED BY	
QUANTITIES BY	
CHECKED BY	
ORIGINAL PLAN	
NOTE BOOK	
SECTION	

* - Final locations of all signs to be determined in the field by the Engineer .



THIS WORK WAS PREPARED BY ME OR UNDER MY SUPERVISION AND CONSTRUCTION OF THIS PROJECT WILL BE UNDER MY OBSERVATION.
Nancy E. Burke
DATE: 8/24/98

STATE OF HAWAII
DEPARTMENT OF TRANSPORTATION
HIGHWAYS DIVISION

CONST. SIGN PLAN & SCHED.

EXISTING ROUTE 130

KEA'AU-PAHOA ROAD VIC. OF KEA'AU TOWN (KEA'AU BYPASS ROAD), PH. 2

PROJECT NO. 130B-01-98

Scale: N.T.S. Date: August, 1998

SHEET No. 1 OF 1 SHEETS
