

PUMP STATION ELEVATION

Not To Scale

* See Notes

REMOVAL PLAN

Not To Scale

NOTES:


- 1. Remove items and equipment shown. This work is to be coordinated with the fuel dispensing system installation work so that fueling service is maintained during this project.
- 2. Site preparation activities shall include but not be limited to:

 Prepare area for the construction of a 15' wide and 64' long


 ACB refueling apron, as shown on the plans.

 Prepare area for the construction of a reinforced concrete

 slab. (See Sheet 7)
- 3. Install new aboveground fuel lines and dispensers prior to existing underground tank removals. (See Sheet No. 6)
- 4. Maintain fueling operations on the side of the station opposite the site from the new aboveground fuel tanks for the duration of the project. As each pump is replaced the Contractor shall provide temporary dispensing services directly from the new aboveground fuel tanks via temporary dispensing units until the new dispensers are operable.
- 5. Empty, excavate and remove existing underground fuel tanks and associated piping. Perform all soil tests, excavations and removals according to all County, State and Federal Regulations and guidelines.
- 6. Contractor shall provide compacted backfill and renew ground cover after removal of underground tanks. Soil to be seeded and fertilized to reestablish grass cover.

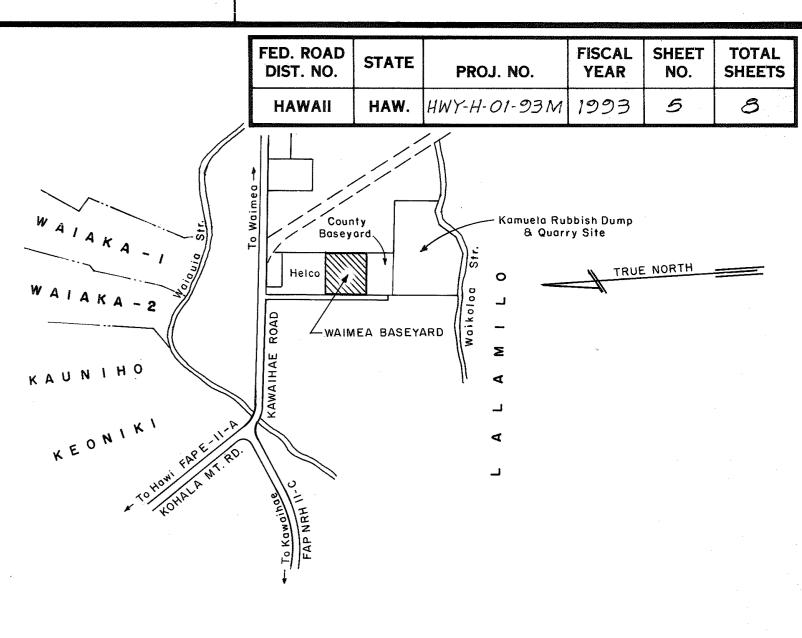

LOCATION MAP
Not To Scale

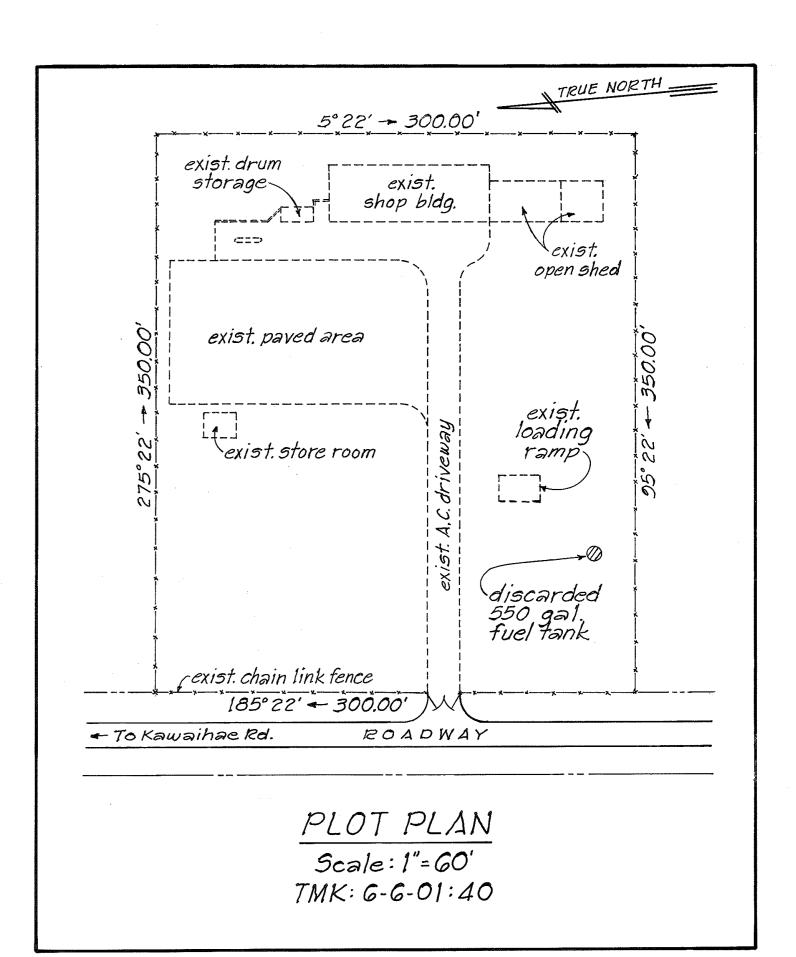

STATE OF HAWAII
DEPARTMENT OF TRANSPORTATION
HIGHWAYS DIVISION

FUEL SYSTEM REMOVAL PLAN WAIMEA BASEYARD

PROJ. No. HWY-H-01-93M

Scale: As Noted Date: March 1993
SHEET No. / OF 2 SHEETS

 ORIGINAL
 SURVEY PLOTTED BY
 DATE

 PLAN
 DRAWN BY
 "

 NOTE BOOK
 DESIGNED BY
 "

 QUANTITIES BY
 "

 CHECKED BY
 "

ţ
