


FED. ROAD DIST. NO.	STATE	FED. AID PROJ. NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
HAWAII	HAW.	FLH-0560(11)	2000	8	31

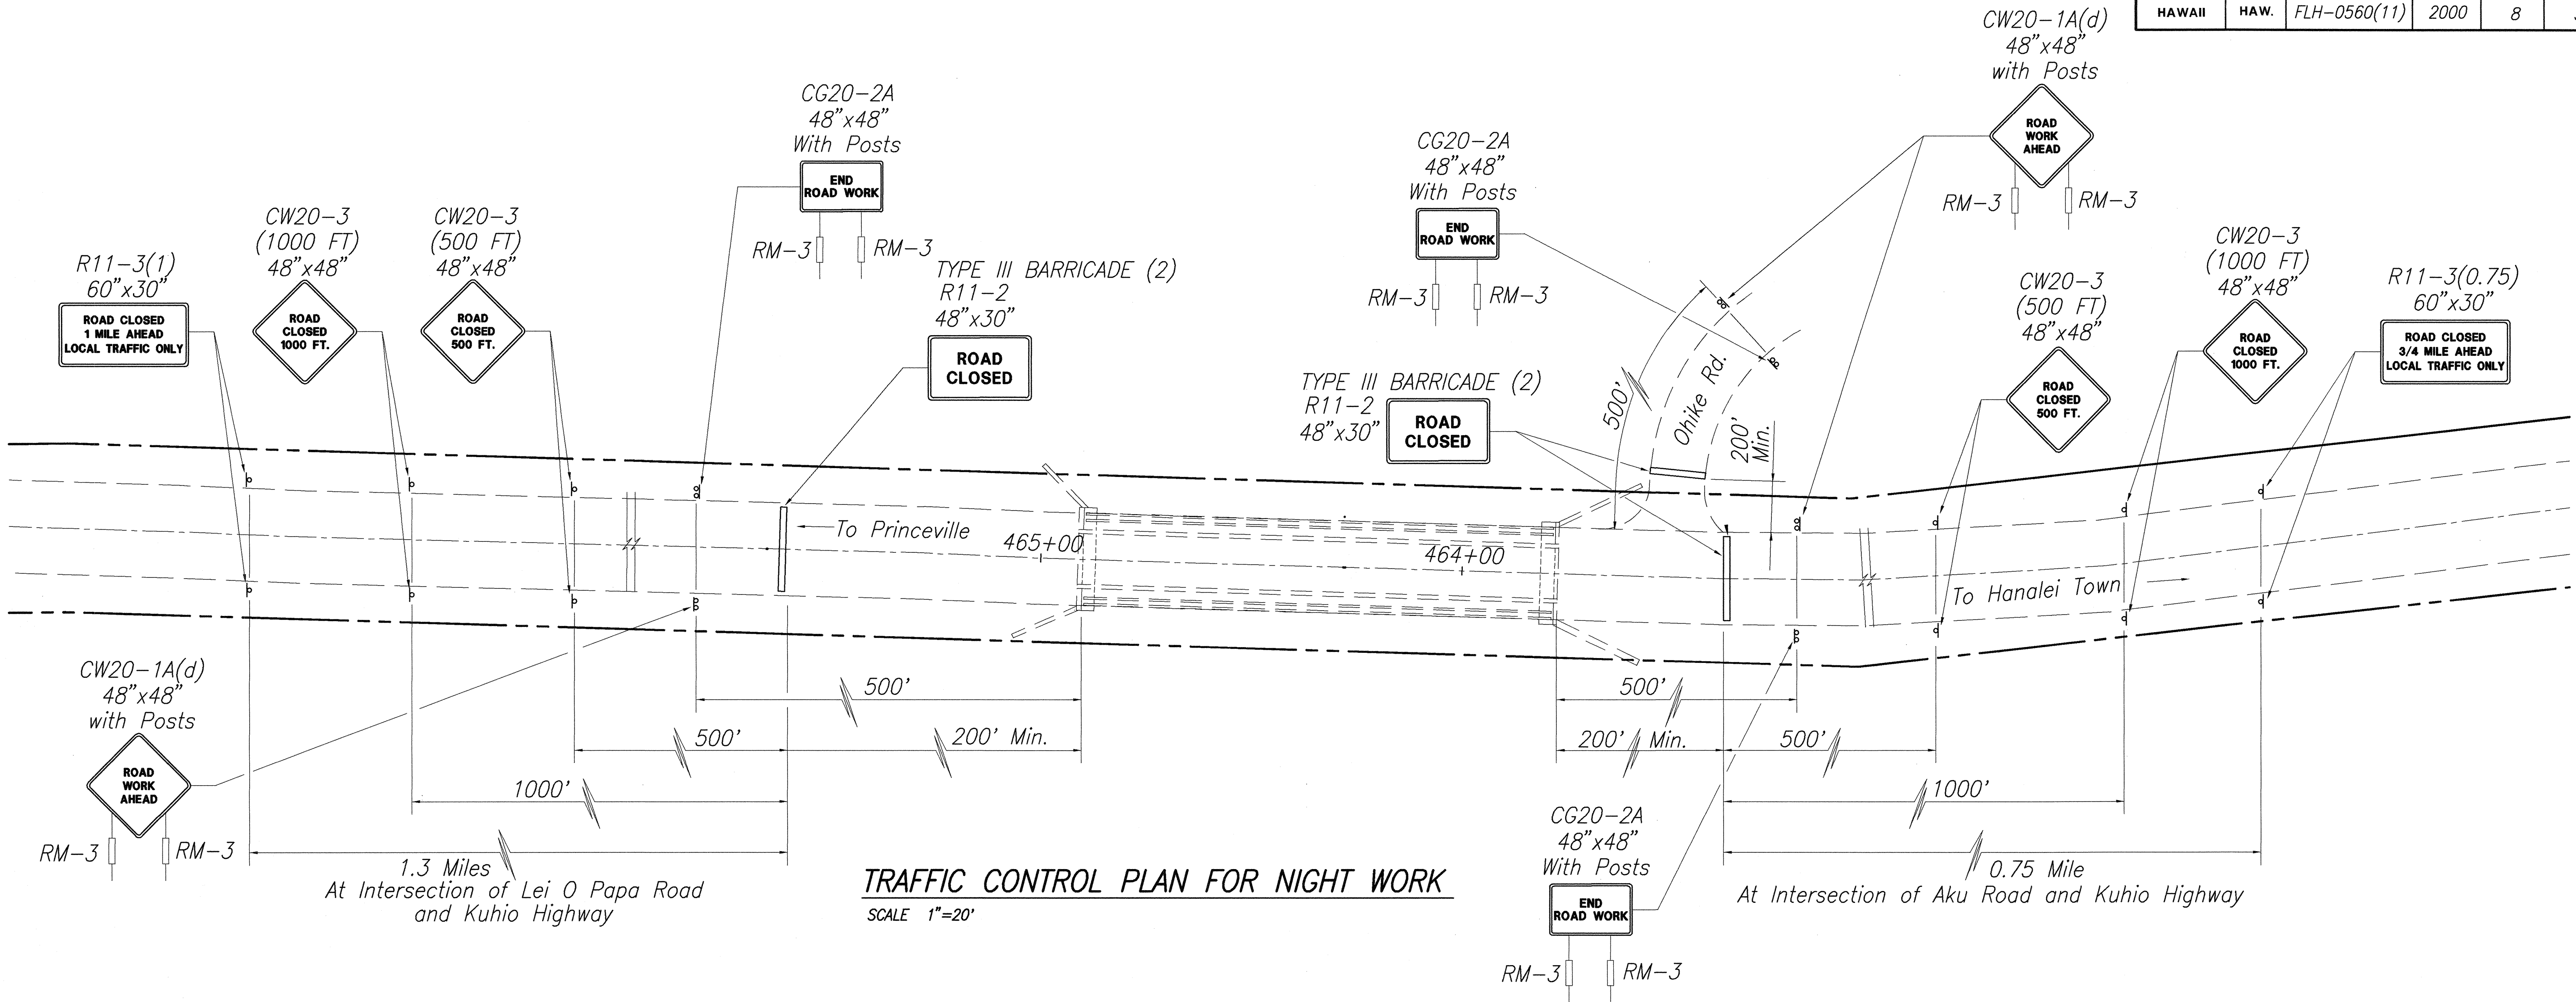

TRAFFIC CONTROL PLAN FOR NIGHT WORK
SCALE 1"=20'

GENERAL NOTES FOR TRAFFIC CONTROL PLAN:

1. The Hanalei Bridge shall remain open to vehicle traffic while the work is in progress.
2. The Contractor is to perform the work so as to minimize delays to traffic. No slow down of traffic is allowed between 6:00 A.M. to 8:00 A.M., and between 3:30 P.M. to 6:30 P.M.. The contractor shall not delay traffic for more than 5 minutes during the hours of 8:00 A.M. to 3:30 P.M..
3. The Contractor is allowed to close the bridge to traffic from Sunday thru Thursday starting at 10:00 P.M. until 5:00 A.M. the following day. During this time period the Contractor shall provide for the services for two special duty police officers to be stationed at the bridge approaches, to control traffic. Emergency vehicles shall be allowed to cross the bridge at all times.
4. Night closure of the bridge will be permitted for the removal and replacement of the deck wearing surface.
5. Intermittent closure of the bridge to traffic required during the tightening of the adjustment of post tensioning rods.
6. The Contractor shall make minor adjustments at intersections, driveways, bridges, structures, etc., to fit field conditions.

GENERAL NOTES FOR TRAFFIC CONTROL PLAN:


7. Traffic control devices shall be installed such that the sign or device farthest from the work area shall be placed first. The others shall then be placed progressively toward the work area.
8. Regulatory and warning signs within the construction zone that are in conflict with the Traffic Control Plans shall be removed or covered. All signs shall be restored upon completion of the work.
9. All construction warning signs shall be promptly removed or covered whenever the message is not applicable or not in use.
10. The backs of all signs used for traffic control shall be appropriately covered to preclude the display of inapplicable sign messages (i.e., when signs have messages on both faces).
11. At the end of each day's work or as soon as the work is completed, the Contractor shall remove all traffic control devices no longer needed to permit free and safe passage of public traffic. Removal shall be in the reverse order of installation.
12. Replace permanent pavement markings and traffic signs upon completion of each phase of work.
13. Final location of Traffic Control signs, barricades and cones shall be as directed by the Engineer.

Notes:

See Special Provisions Section 104.04
(Scope of Work - Maintenance of Traffic)
for Days and Times of Allowed Road Closure.

See Special Provisions Section 645
for Traffic Control Plans for daytime construction.
Install 1 - CW20-1A(d) with post and
1 - CG20-2A with post on Ohike Road.

ORIGINAL PLAN	DATE
DESIGNED BY	DATE
TRACED BY	DATE
NOTED BY	DATE
QUANTITIES BY	DATE
CHECKED BY	DATE



THIS WORK WAS PREPARED BY
ME OR UNDER MY SUPERVISION

Dennis T. Shiu

DATE	REVISION
STATE OF HAWAII DEPARTMENT OF TRANSPORTATION HIGHWAYS DIVISION TRAFFIC CONTROL AND CONSTRUCTION SIGNS PLAN KUHIO HIGHWAY, REMOVE/REPAIR/REPLACE METAL MEMBERS, HANALEI BRIDGE Federal Aid Project No. FLH-0560(11) Scale: Date: Jan. 2000	
SHEET No. 1 OF 1 SHEETS	
