




FED. ROAD DIST. NO.	STATE	PROJ. NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
HAWAII	HAW.	HWY-0-01-05M	2006	106	106

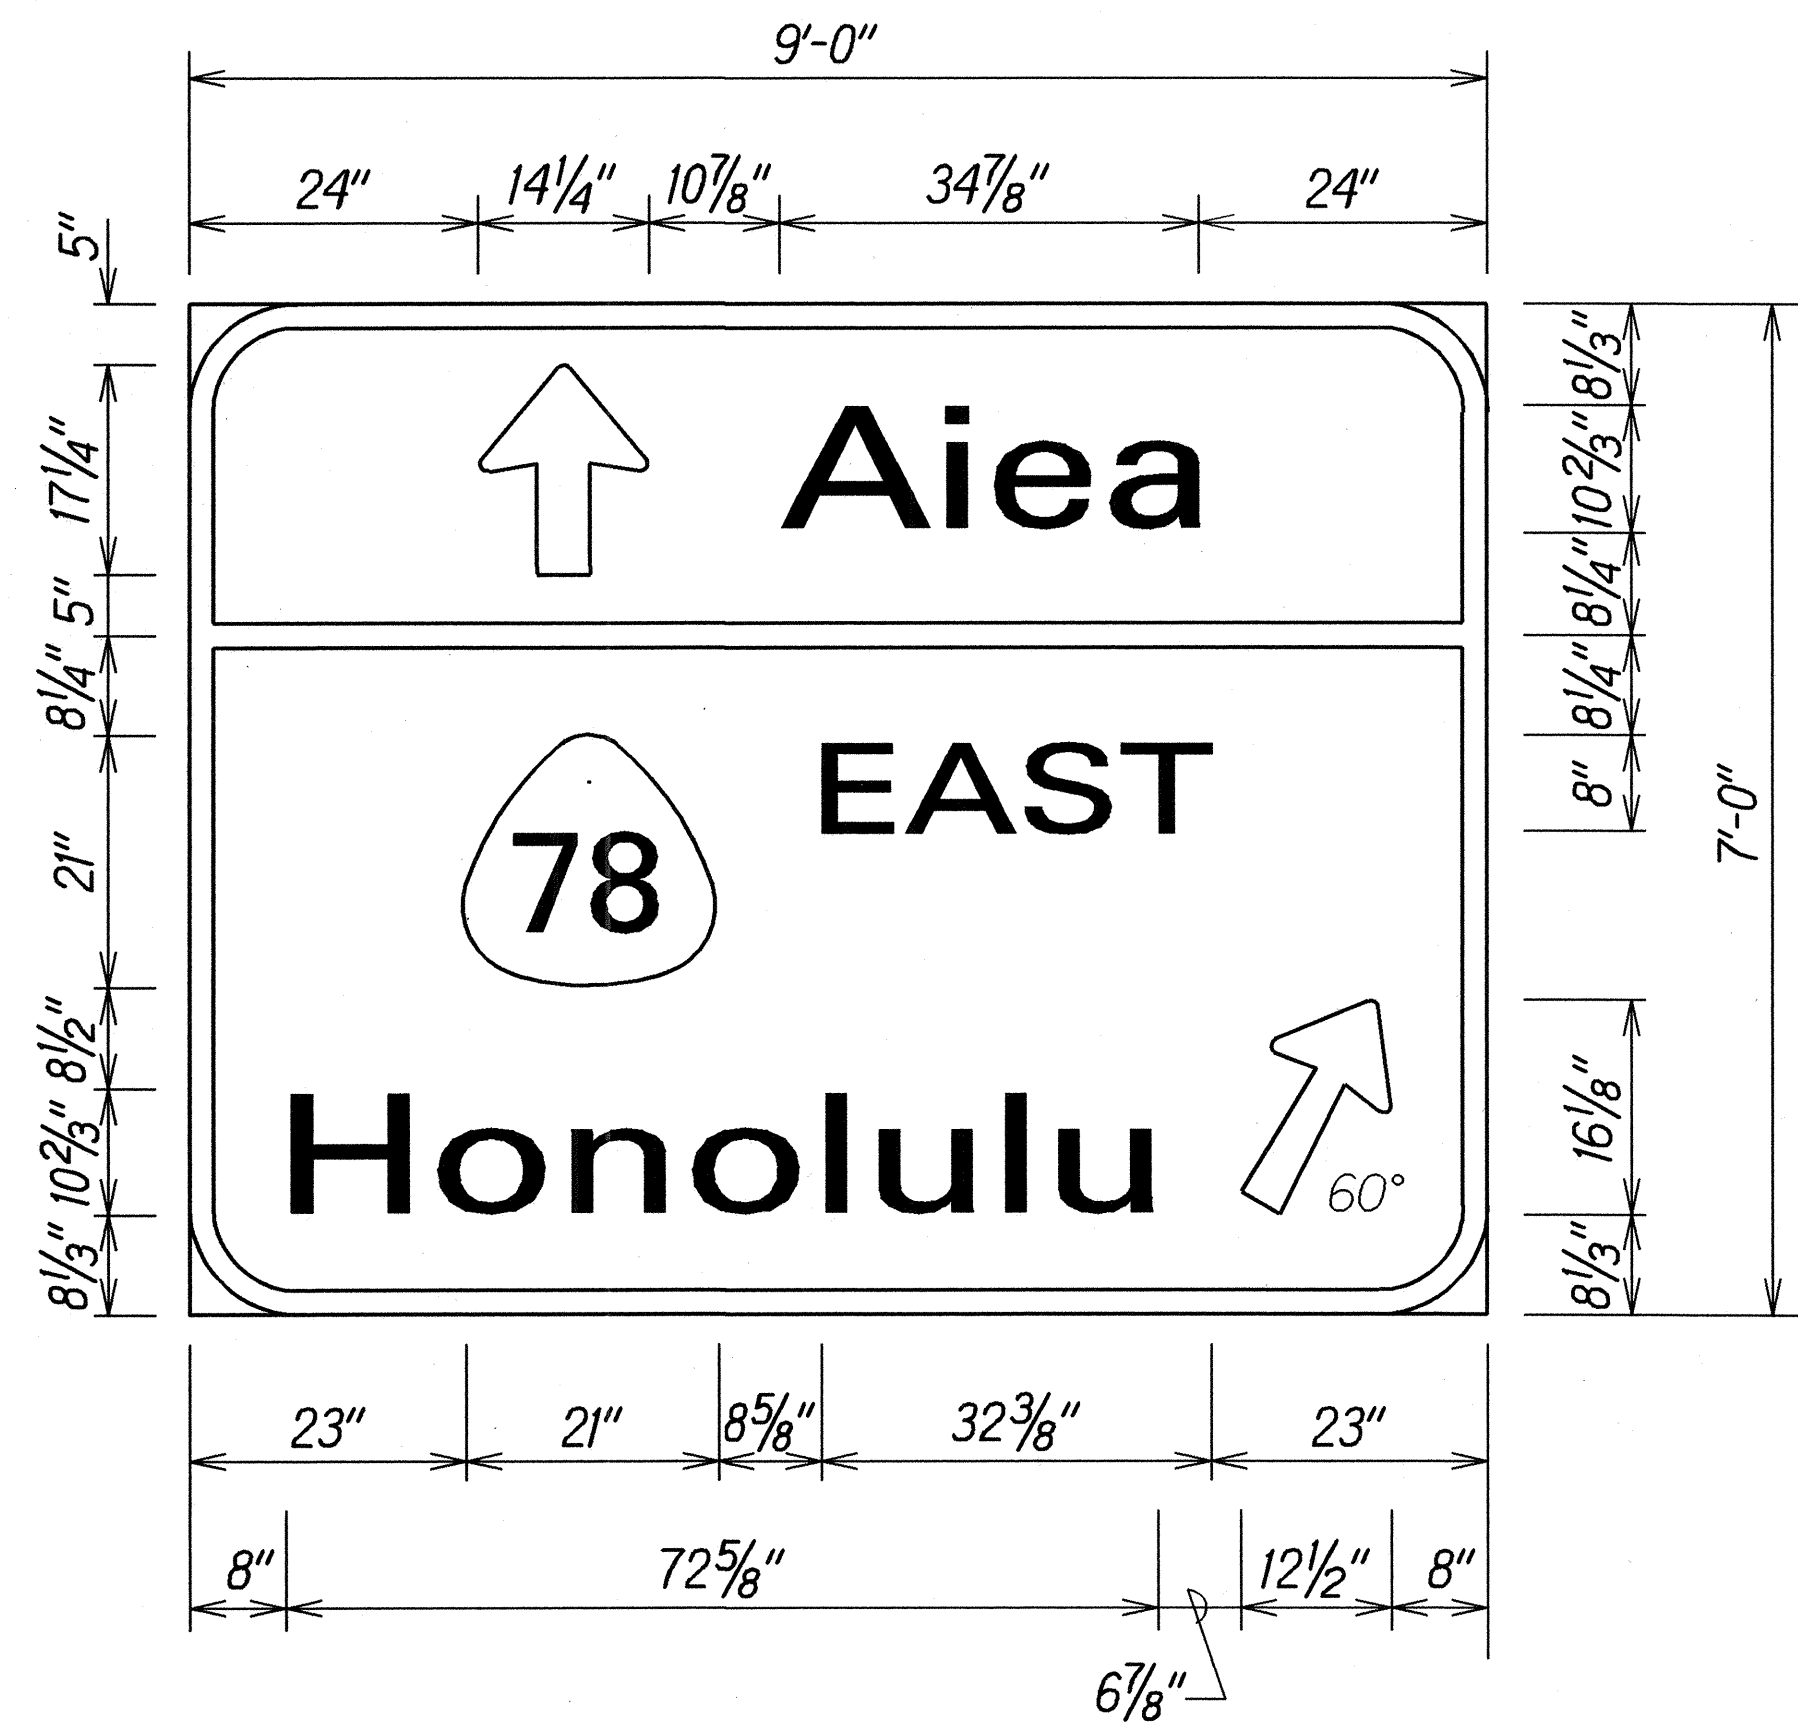


SIGN D-1  
Not to Scale

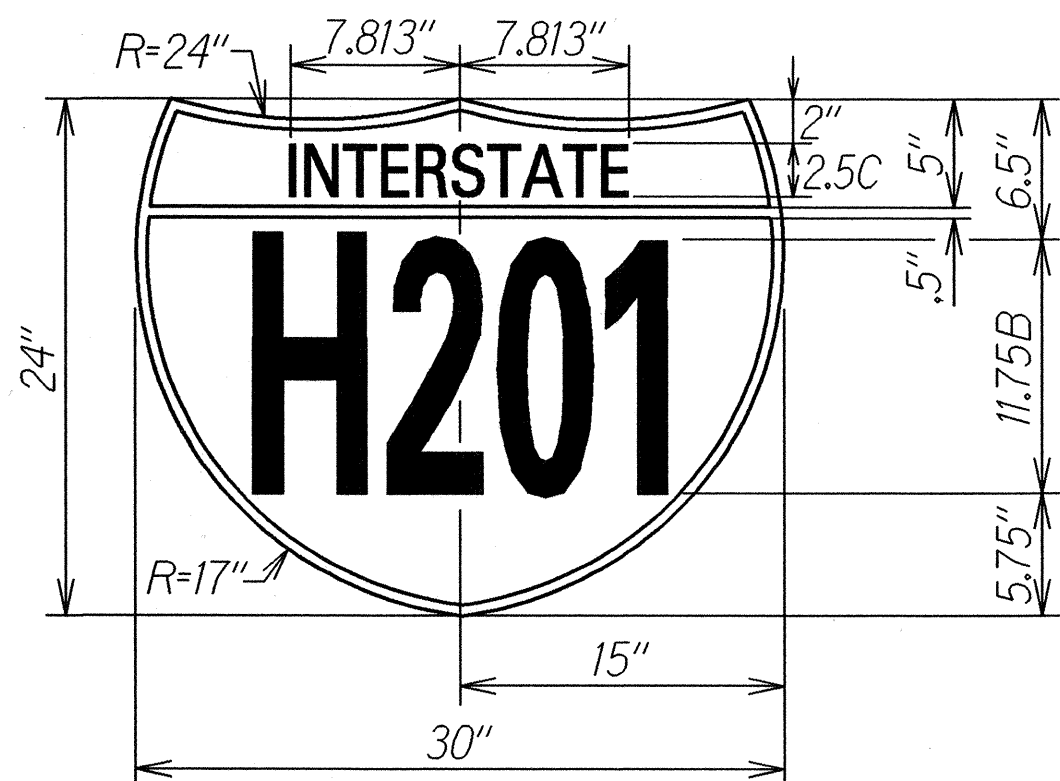

H201  
Not to Scale

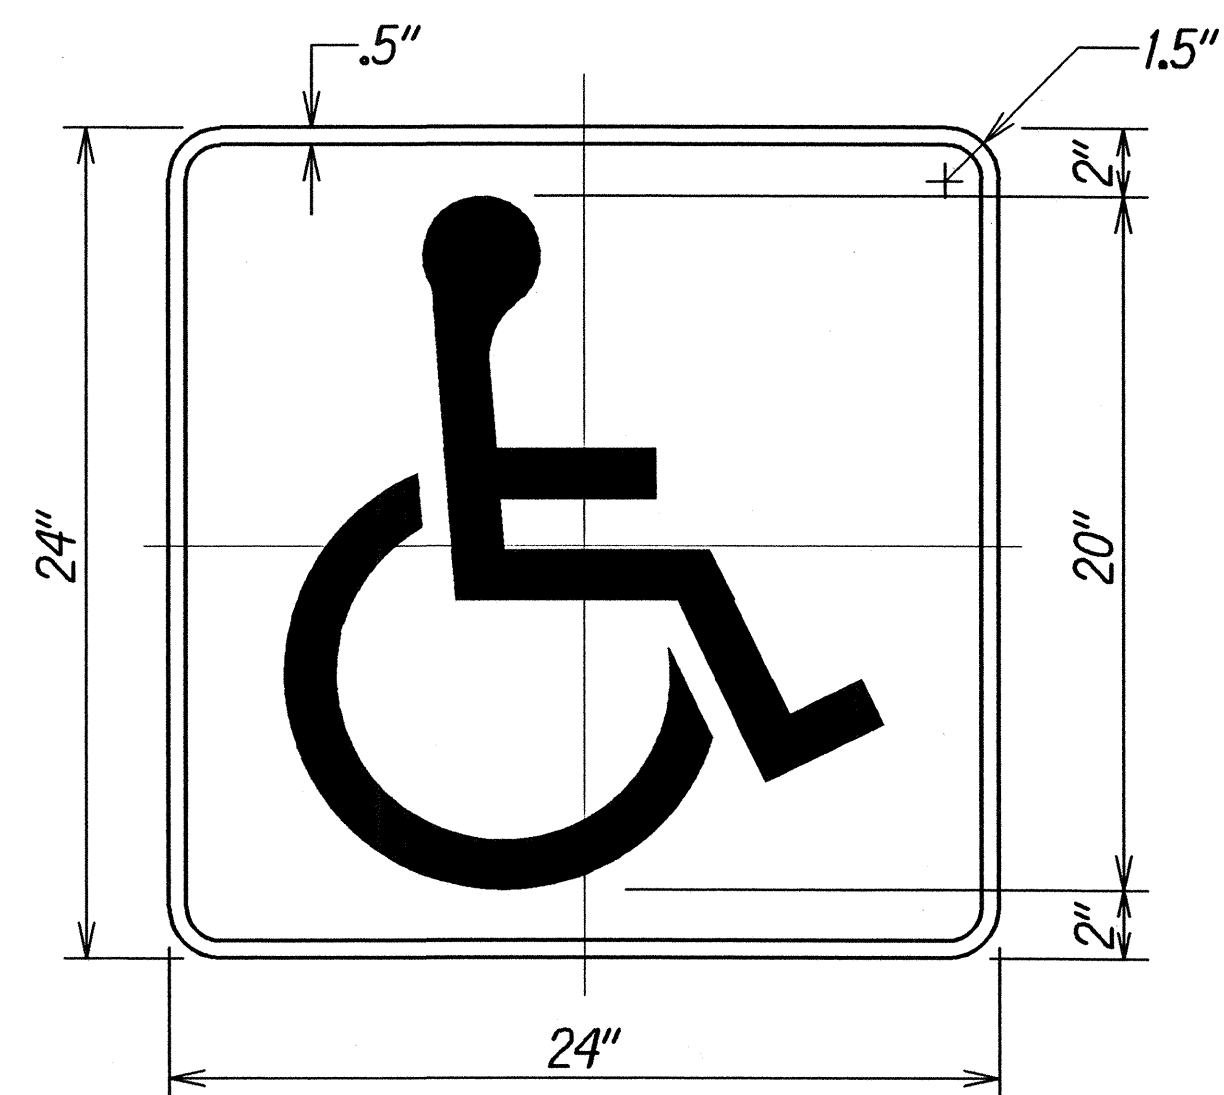

D9-6  
Not to Scale

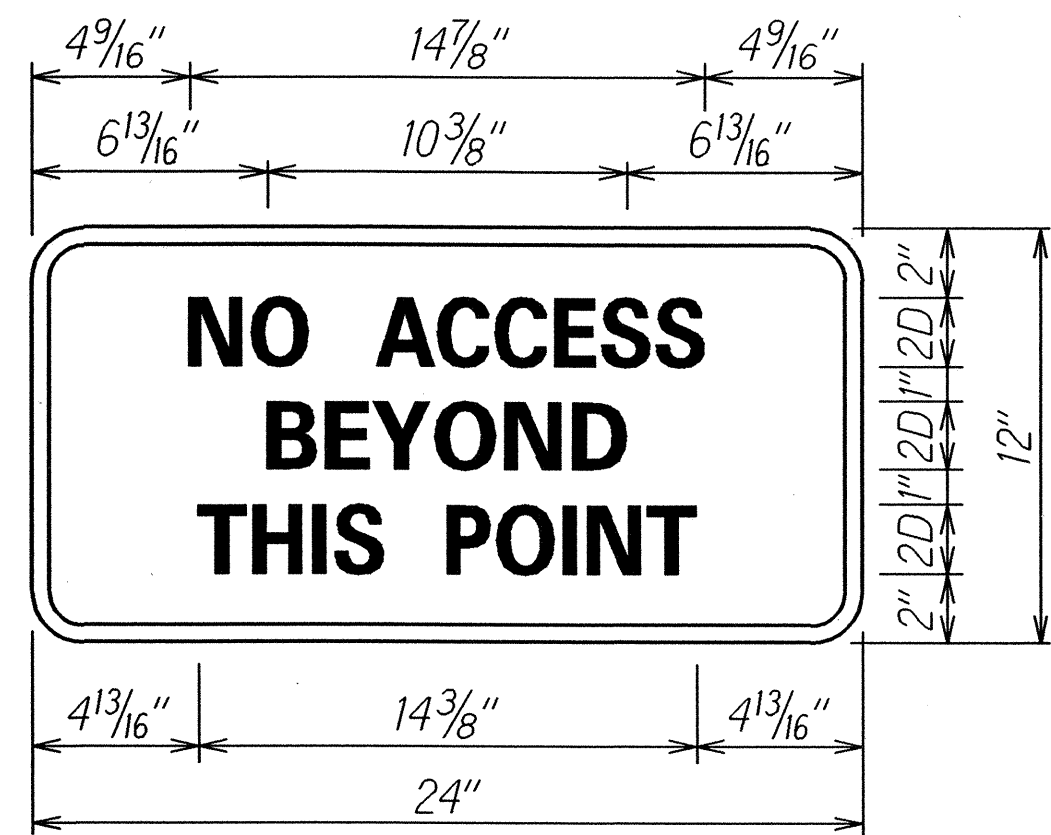

LEGEND & BORDER: White (Reflectorized)  
BACKGROUND: Blue

ADA DIRECTIONAL SIGN  
Not to Scale

DETOUR NOTES:

- Cones or delineators shall be installed at 10' o.c. max. in work area.
- Cones or delineators shall be installed at 20' o.c. max. along tapers and tangents.
- Minimum width of traffic lane through work area is 10'.
- Relocation and/or removal of temporary signs and posts used for Traffic Control shall be considered incidental to various contract items.
- Damage to signs, temporary pavement markers, delineators, barricades and lamps caused by the public shall be repaired or replaced by the Contractor as soon as possible, or as directed by the Engineer. This work shall be paid for under Item No. 645.0200 - Police Officers and/or Additional Traffic Control Devices. Damage caused by the Contractor's negligence shall be repaired or replaced at the Contractor's expense.
- All signs within the City and County right-of-way shall be installed on existing street light posts or temporary non-marring sign supports. This work shall be considered incidental to various contract items.
- The Type II and Type III Barricades with lamps used during construction shall be considered incidental to various contract items.
- Work required in the Detour/Traffic Control Plans will be paid under applicable contract items or otherwise specified herein. All other traffic control work shall be in accordance with Section 645 - Traffic Control. Work required for lane closures during the working day will not be paid for but shall be considered incidental to various contract items. Advance Construction Warning Signs as required under Section 645 of the Special Provisions shall be installed on all approaches to construction areas. This work shall be considered incidental to various contract items.
- The Flashing Arrow Signal used during construction shall be considered incidental to various contract items.
- The Contractor shall publish "Notice to Motorists" 1 week prior to the start of construction. Public notice shall be coordinated with the Department of Transportation, Highways Division.
- The Contractor shall notify Lowell Tom (848-4578) at Oahu Transit Authority (The Bus) 4 weeks prior to start of construction.

ORIGINAL PLAN	SURVEY PLOTTED BY	DATE
NOTE BOOK	DESIGNED BY	2/2/05
QUANTITIES BY	CHECKED BY	

STATE OF HAWAII  
DEPARTMENT OF TRANSPORTATION  
HIGHWAYS DIVISION

**SIGN DETAILS**  
**& DETOUR NOTES**

**AIEA ACCESS ROAD RESURFACING**  
**Moanalua Road to Kamehameha Highway**  
**HWY-0-01-05M**

Scale: As Shown Date: June 2005

SHEET No. T4 OF 4 SHEETS
