

FED. ROAD DIST. NO.	STATE	PROJ. NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
HAWAII	HAW.	83D-01-72	1972	3	26

BASELINE CURVE DATA				
CURVE	1	2	3	4
Δ	10°16'	15°57'	78°30'	20°38'
R	800	800	200	560
T	71.9	112.1	163.4	132.5
L	143.0	222.8	274.0	258.0

True North
Scale: 1" = 50'

Project Information Sign


GENERAL NOTES:

- Exact location of Signs and Reflector Markers to be determined in the field by the Engineer.
- Existing Reflector Markers with Posts shall be removed and Stockpiled. (Cost incidental to the various Contract Items.)
- Striping shall be done by State Forces.
- The existing Signal Corps Cable between Stations 910+45± to 913+25± will be abandoned. Cutting and capping of the existing cable will be done by Hawaiian Telephone Company. The Contractor shall refrain from his operations within this area until the cutting and capping operations has been completed. The Contractor shall verify the exact location of the remaining cables within the project limits and exercise caution during any of his operations within the vicinity of the cable. The Contractor shall be liable for any damages incurred due to his operations.

SUMMARY OF REFLECTOR MARKERS WITH POSTS		
LIMITS OF INSTALLATION	TYPE	QUANTITY AND SPACING
Sta. 913+79 to Sta. 916+19 (R)	RM-1	4 @ 80'
Sta. 916+54 to Sta. 918+99 (R)	RM-1	8 @ 35'
Sta. 919+69 (R)	RM-1	1
Sta. 920+34 to Sta. 922+29 (R)	RM-1	4 @ 65'
Sta. 923+54 (R)	RM-1	1


SUMMARY OF RAISED PAVEMENT MARKERS		
Sta. 906+50 to Sta. 909+57.5 (Passing Permitted) Prohibited	Type D	12 Each
Sta. 909+57.5 to Sta. 925+00 (Passing Prohibited)	Type D	40 Each

SUMMARY OF REGULATORY AND WARNING SIGNS		
TYPE	STATION	QUANTITY
R4-1	909+85 (R)	1 Each
R4-1	925+00 (L)	1 Each

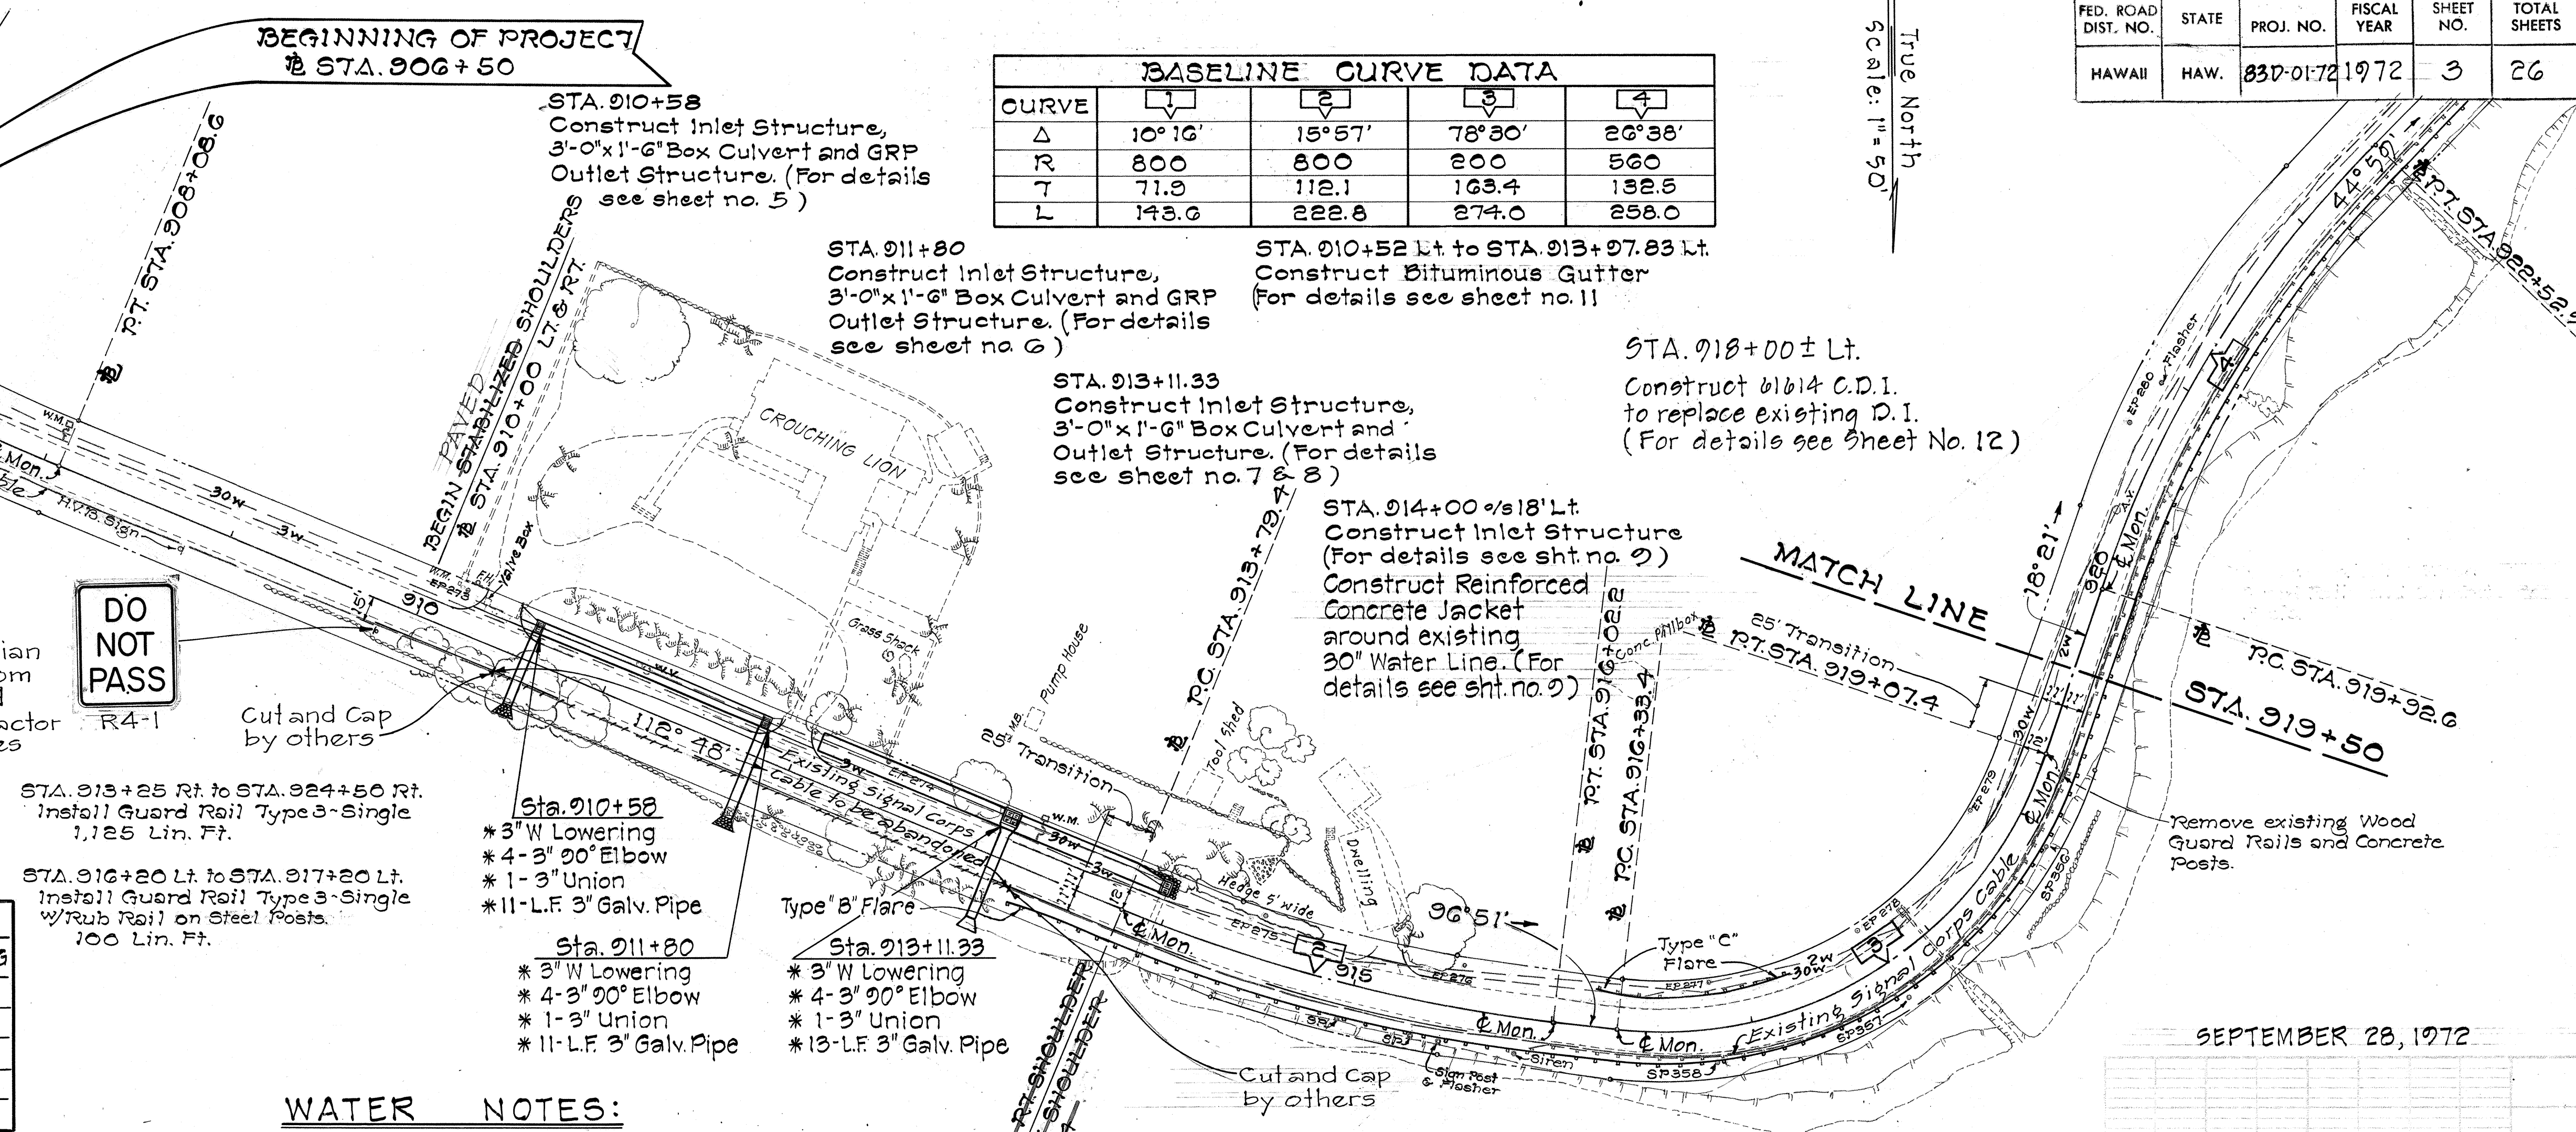

WATER NOTES:

- Unless otherwise specified, all materials and construction of water system facilities and appurtenances shall be in accordance with the STANDARD SPECIFICATIONS FOR ROAD AND BRIDGE CONSTRUCTION, dated 1969, as amended, of the Hawaii Highways Division, Department of Transportation.
- Prior to excavating for new drains and other utilities, the Contractor shall verify in the field the location of existing water mains and appurtenances. Where the installation of new drain or other utilities are to cross over or under existing water mains, the Contractor shall expose the existing water mains prior to trenching. Excavation around water mains shall be done by hand.
- Asterisk (*) indicates work to be performed by Board of Water Supply. Materials to be furnished by the Contractor.
- The Contractor shall notify the Board of Water Supply in writing one week prior to commencing work on the main.
- Approval by the Board of Water Supply is based solely on the adequacy of the water supply. Discrepancies, if any, of alignments, grades, fittings, etc. shall be the responsibility of the Engineer who prepared the plans.
- The existence and location of underground utilities and structures as shown on the plans are from the latest available data but is not guaranteed as to the accuracy or the encountering of other obstacles during the course of the work. The Contractor shall be responsible and shall pay for all damages to existing utilities.

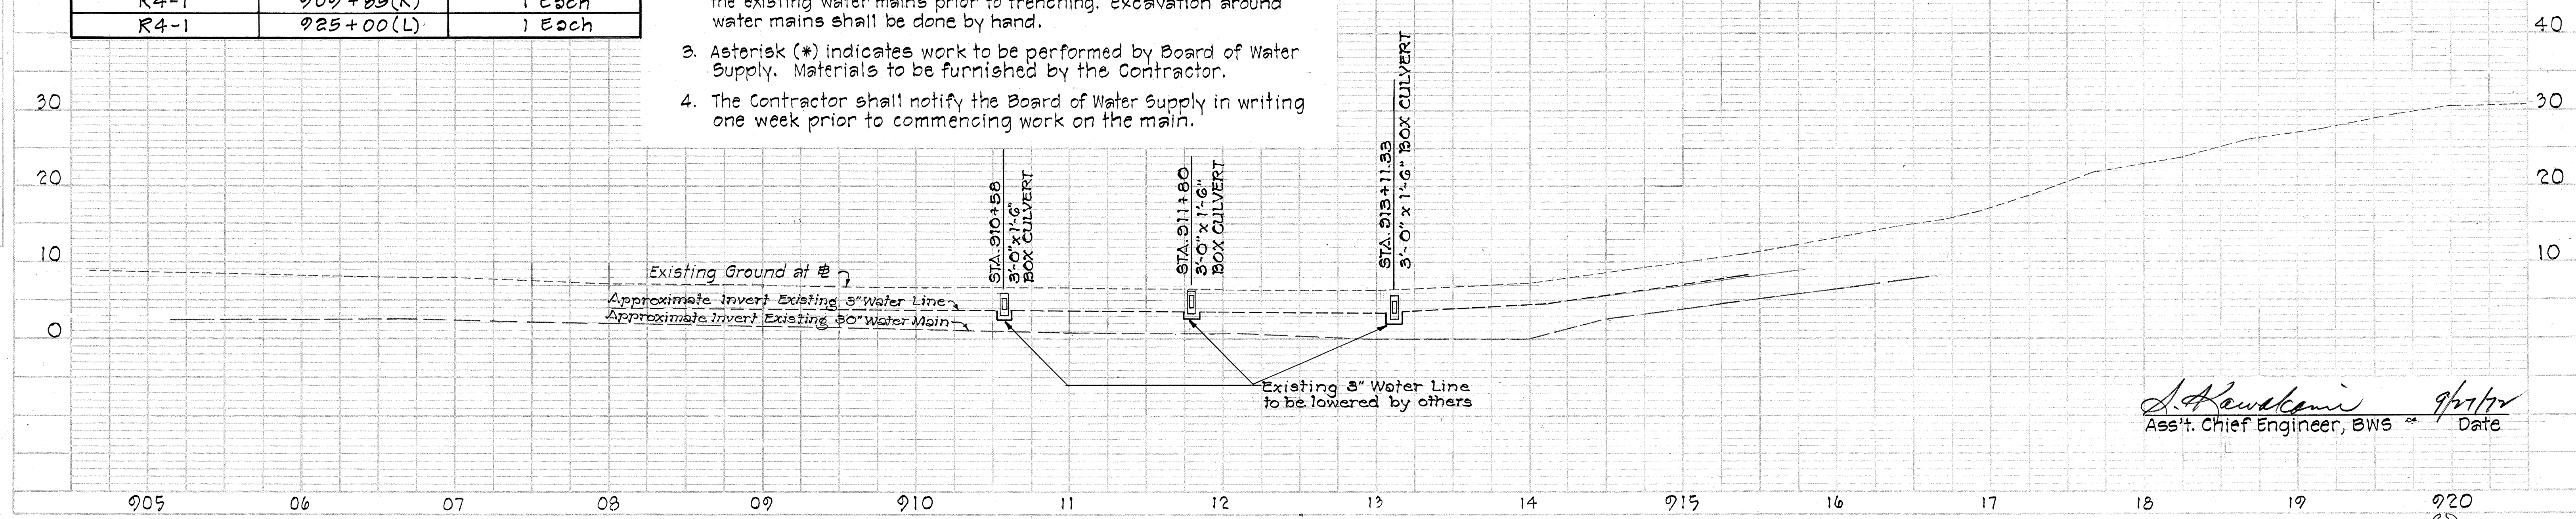

J. Kawakami
Ass't. Chief Engineer, BWS
9/27/72
Date

FED. ROAD DIST. NO.	STATE	PROJ. NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
HAWAII	HAW.	23D-01-72	1972	4	26

PLAN	DATE
SURVEYED	
PLOTTED	
NOTE BOOK ALIGNMENT CHECKED	
RT. OF WAY CHECKED	
NO.	

PROFILE	DATE
SURVEYED	
PLOTTED	
NOTE BOOK GRADES CHECKED	
STRUCTURE NOTATIONS CHECKED	
NO.	

