



FED. ROAD DIST. NO.	STATE	PROJ. NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
HAWAII	HAW.	19D-01-92M	1992	14	18

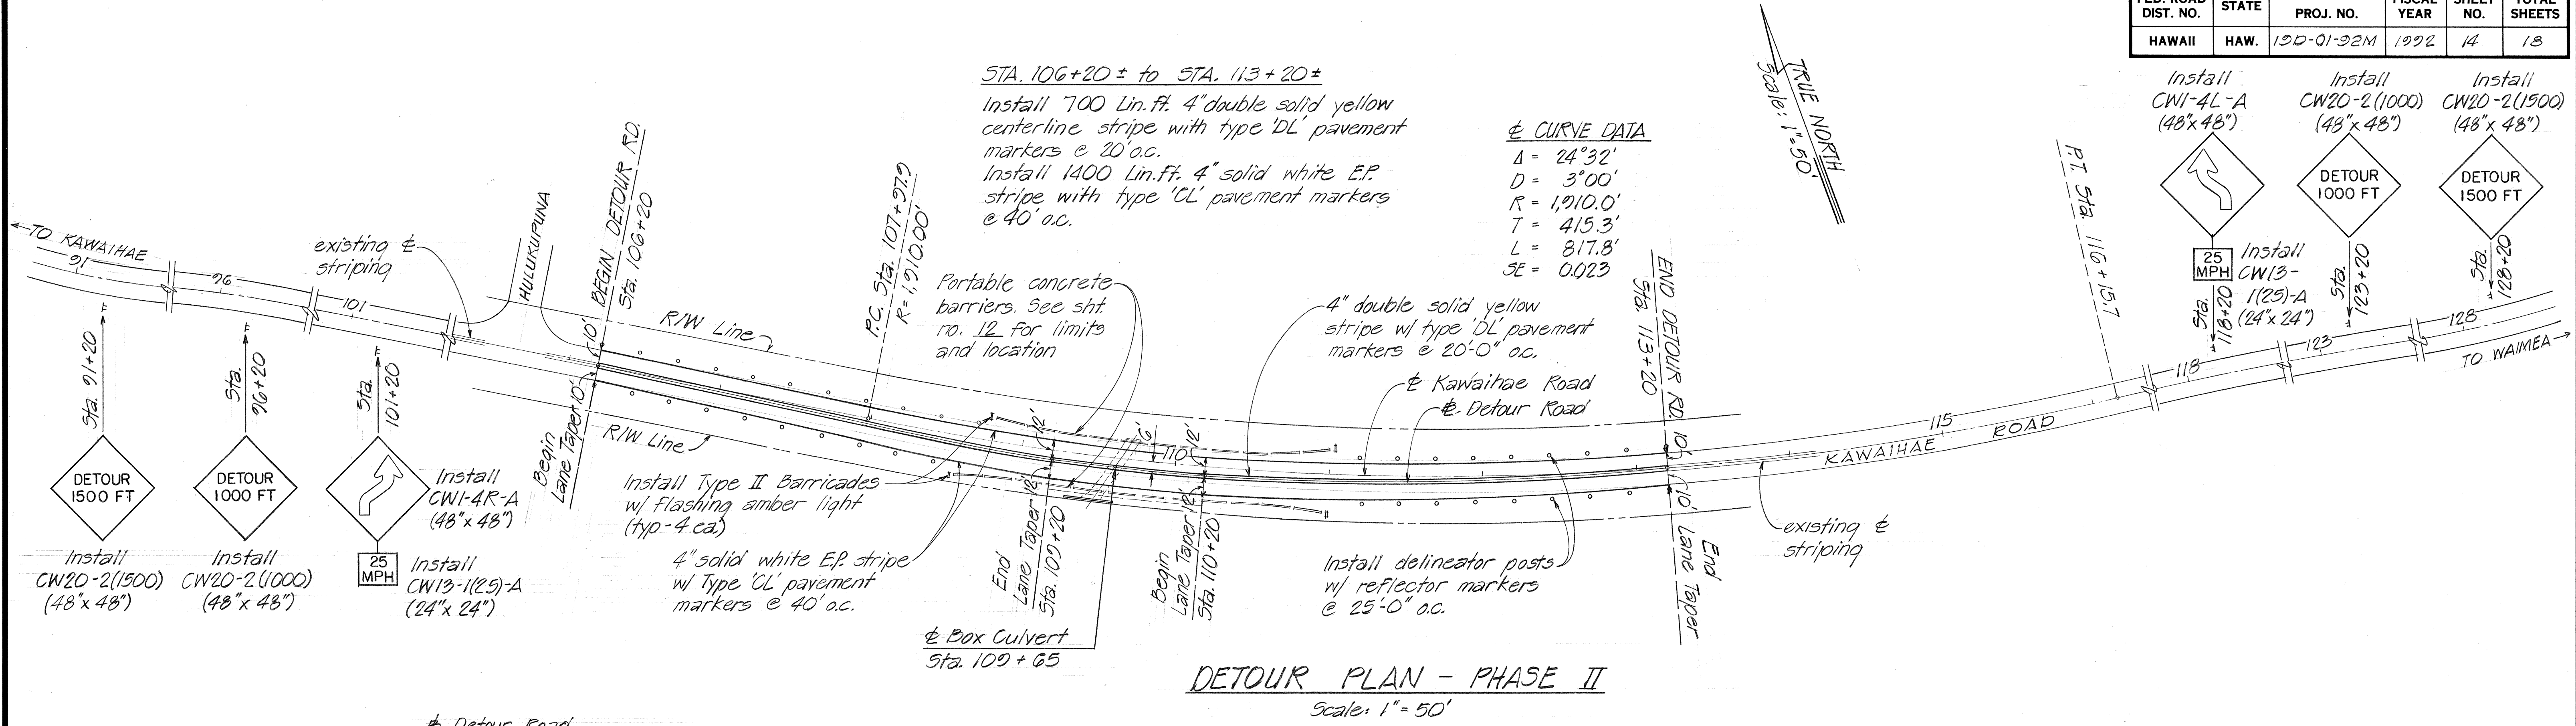

DETOUR PLAN - PHASE II
Scale: 1" = 50'

PHASE II DETOUR NOTES

- Upon completion of Phase I work, the Detour shall be put into effect as shown.
- The contractor's attention is directed to Section 107.13 of the Special Provisions regarding detour requirements.
- Existing pavement markings and striping which conflict with the detour plans shall be removed prior to detour implementation. Removal shall also include roadway signs not pertaining to the detour alignment.
- Installation of new pavement striping, markers and signs shall be as per Detour Plan and shall be paid for as provided under the contract items.
- Exact limits and locations of detour items shall be determined in the field by the Engineer.
- Contractor shall widen shoulder as needed to install the Detour. Payment shall be considered incidental to other contract items.
- Portable concrete barriers shall be paid for under item no. 645.1000 - 'Police Officers and/or Additional Traffic Control Devices' as provided for on sh. no. 12.
- The contractor shall be responsible for furnishing delineator posts with reflector markers.
- Payment for installation and maintenance of the detour shown shall be paid for on a Force Account basis under item no. 645.3000 - 'Construction and Maintenance of Detours,' including payment for publication of legal notices.
- Daily work zone traffic control, such as described in the Special Provisions, Section 645 - 'Traffic Control, Figures 1 thru 6,' shall be considered incidental to the contract items and no separate payment shall be provided.
- Contractor shall be responsible for submitting Traffic Control Plans for 12" waterline installation for review and approval of the Engineer.
- Upon completion of Phase II construction, the contractor shall remove detour striping, markers, and signs and restore original pavement striping, markers and signs. Payment for such restoration work shall be as provided for under the contract items.

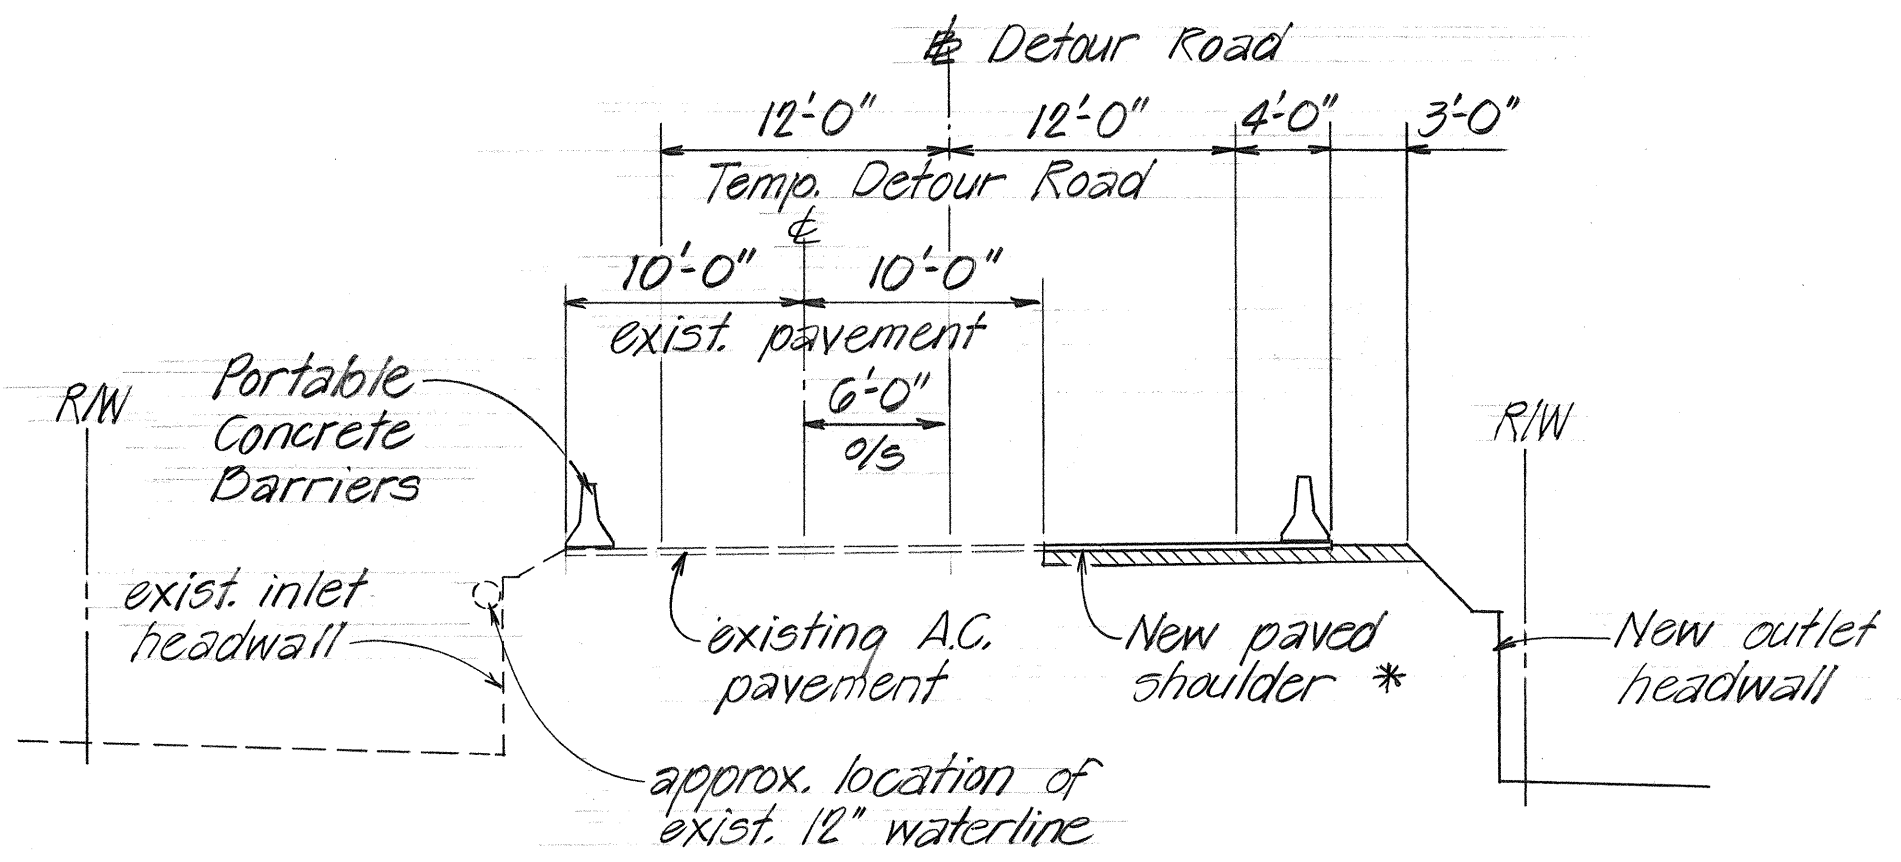

TYPICAL SECTION - DETOUR ROAD
@ STA. 109+70
Scale: 1/8" = 1'-0"

* Payment for Asphaltic Concrete Mix No. V shall be paid for under Item No. 401.0500 and payment for Aggregate Base Course shall be paid for under Item No. 304.1110.

SURVEY PLOTTED BY	DATE
DRAWN BY	
TRACED BY	
DESIGNED BY	
CHECKED BY	
ORIGINAL PLAN	
NOTE BOOK	
NO.	

STATE OF HAWAII
DEPARTMENT OF TRANSPORTATION
HIGHWAYS DIVISION

DETOUR ROAD - PHASE II

KAWAIIHAE ROAD
CULVERT EXTENSIONS
PROJECT No. 19D-01-92M

Scale: As Noted Date: April 1992

SHEET NO. 1 OF 1 SHEETS
