



FED. ROAD DIST. NO.	STATE	FED. AID PROJ. NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
HAWAII	HAW.	U-092-1(8)	1970	7	41

GENERAL NOTES

1. Unless otherwise specified, all traffic control devices at the work site or on adjacent public streets and highways shall conform to provisions of the "Manual on Uniform Traffic Control Devices for Streets and Highways" (U.S. Dept. of Commerce, Bureau of Public Roads, June 1961), as amended by the Rules and Regulations Governing the Use of Traffic Control Devices at Work Sites on or Adjacent to Public Streets and Highways" (Highway Safety Coordinator, State of Hawaii, effective May 1, 1968.)
2. Except for the traffic lane markings, the Contractor shall install all traffic control devices necessary for the detours.
3. The Contractor shall make his request to the Division of Highways for pavement markings one week in advance.
4. The Contractor shall maintain driveway access for abutting properties at all times.
5. Removal of existing concrete curb, curb and gutter, sidewalk and pavement due to roadway widening shall not be measured and paid for directly but shall be considered as incidental to Roadway Excavation, Item 203.02
6. Curb and gutter transitions shall be paid for as curb and gutter of the type to be constructed adjacent to the transition.

SUMMARY OF SIGNS REQUIRED

MUTCD DESIG.	MESSAGE	DISPOSITION	QTY (EA)
A. ADVANCED WARNING SIGNS *			
W20-1b	Road Construction-1000ft.	1000' from work site	2
W20-2d	Detour Ahead	750' from work site	2
W20-2c	Detour Ahead -500ft.	500' from work site	2
W20-2d	Detour Ahead	250' from work site	2
B. PHASE I TRAFFIC SIGNS WITHIN PROJECT			
W1-1(L)		Relocate with Post	1
W1-6(R)		New- 2 on Barricades	2
W1-6(L)		New- 3 on Barricades	3
RG-1(R)	— ONE WAY →	New- 1 on Post	
		Relocate- 1 on Post	2
R10-2	Road Closed	New- 4 on Barricades	4
R1-1	STOP	Relocate- 1 with Post 1 on Lite std.	2
R2-1(20)	Speed Limit 20 m.p.h.	New- 1 with Post, 9 on Posts & 4 on Lite Std.	8
R3-7A	Right Lane must turn right at River or Awa	New- 1 with Post	1
R3-8B		New- 8 with posts	2

- * Install on both sides of approach work site.

NOTE: For 50 gal. drum markings, see det. sheet 8.


STATE OF HAWAII
DEPARTMENT OF TRANSPORTATION
HIGHWAYS DIVISION

CONSTRUCTION PHASING
AND TRAFFIC DETOUR
PHASE I

NIMITZ HIGHWAY IMPROVEMENTS
SUNNER STREET TO AWA STREET
PROJECT NO. U-092-1(S)

SCALE: AS NOTED DATE: MAY 1969

SHEET No. 1 OF 2 SHEETS

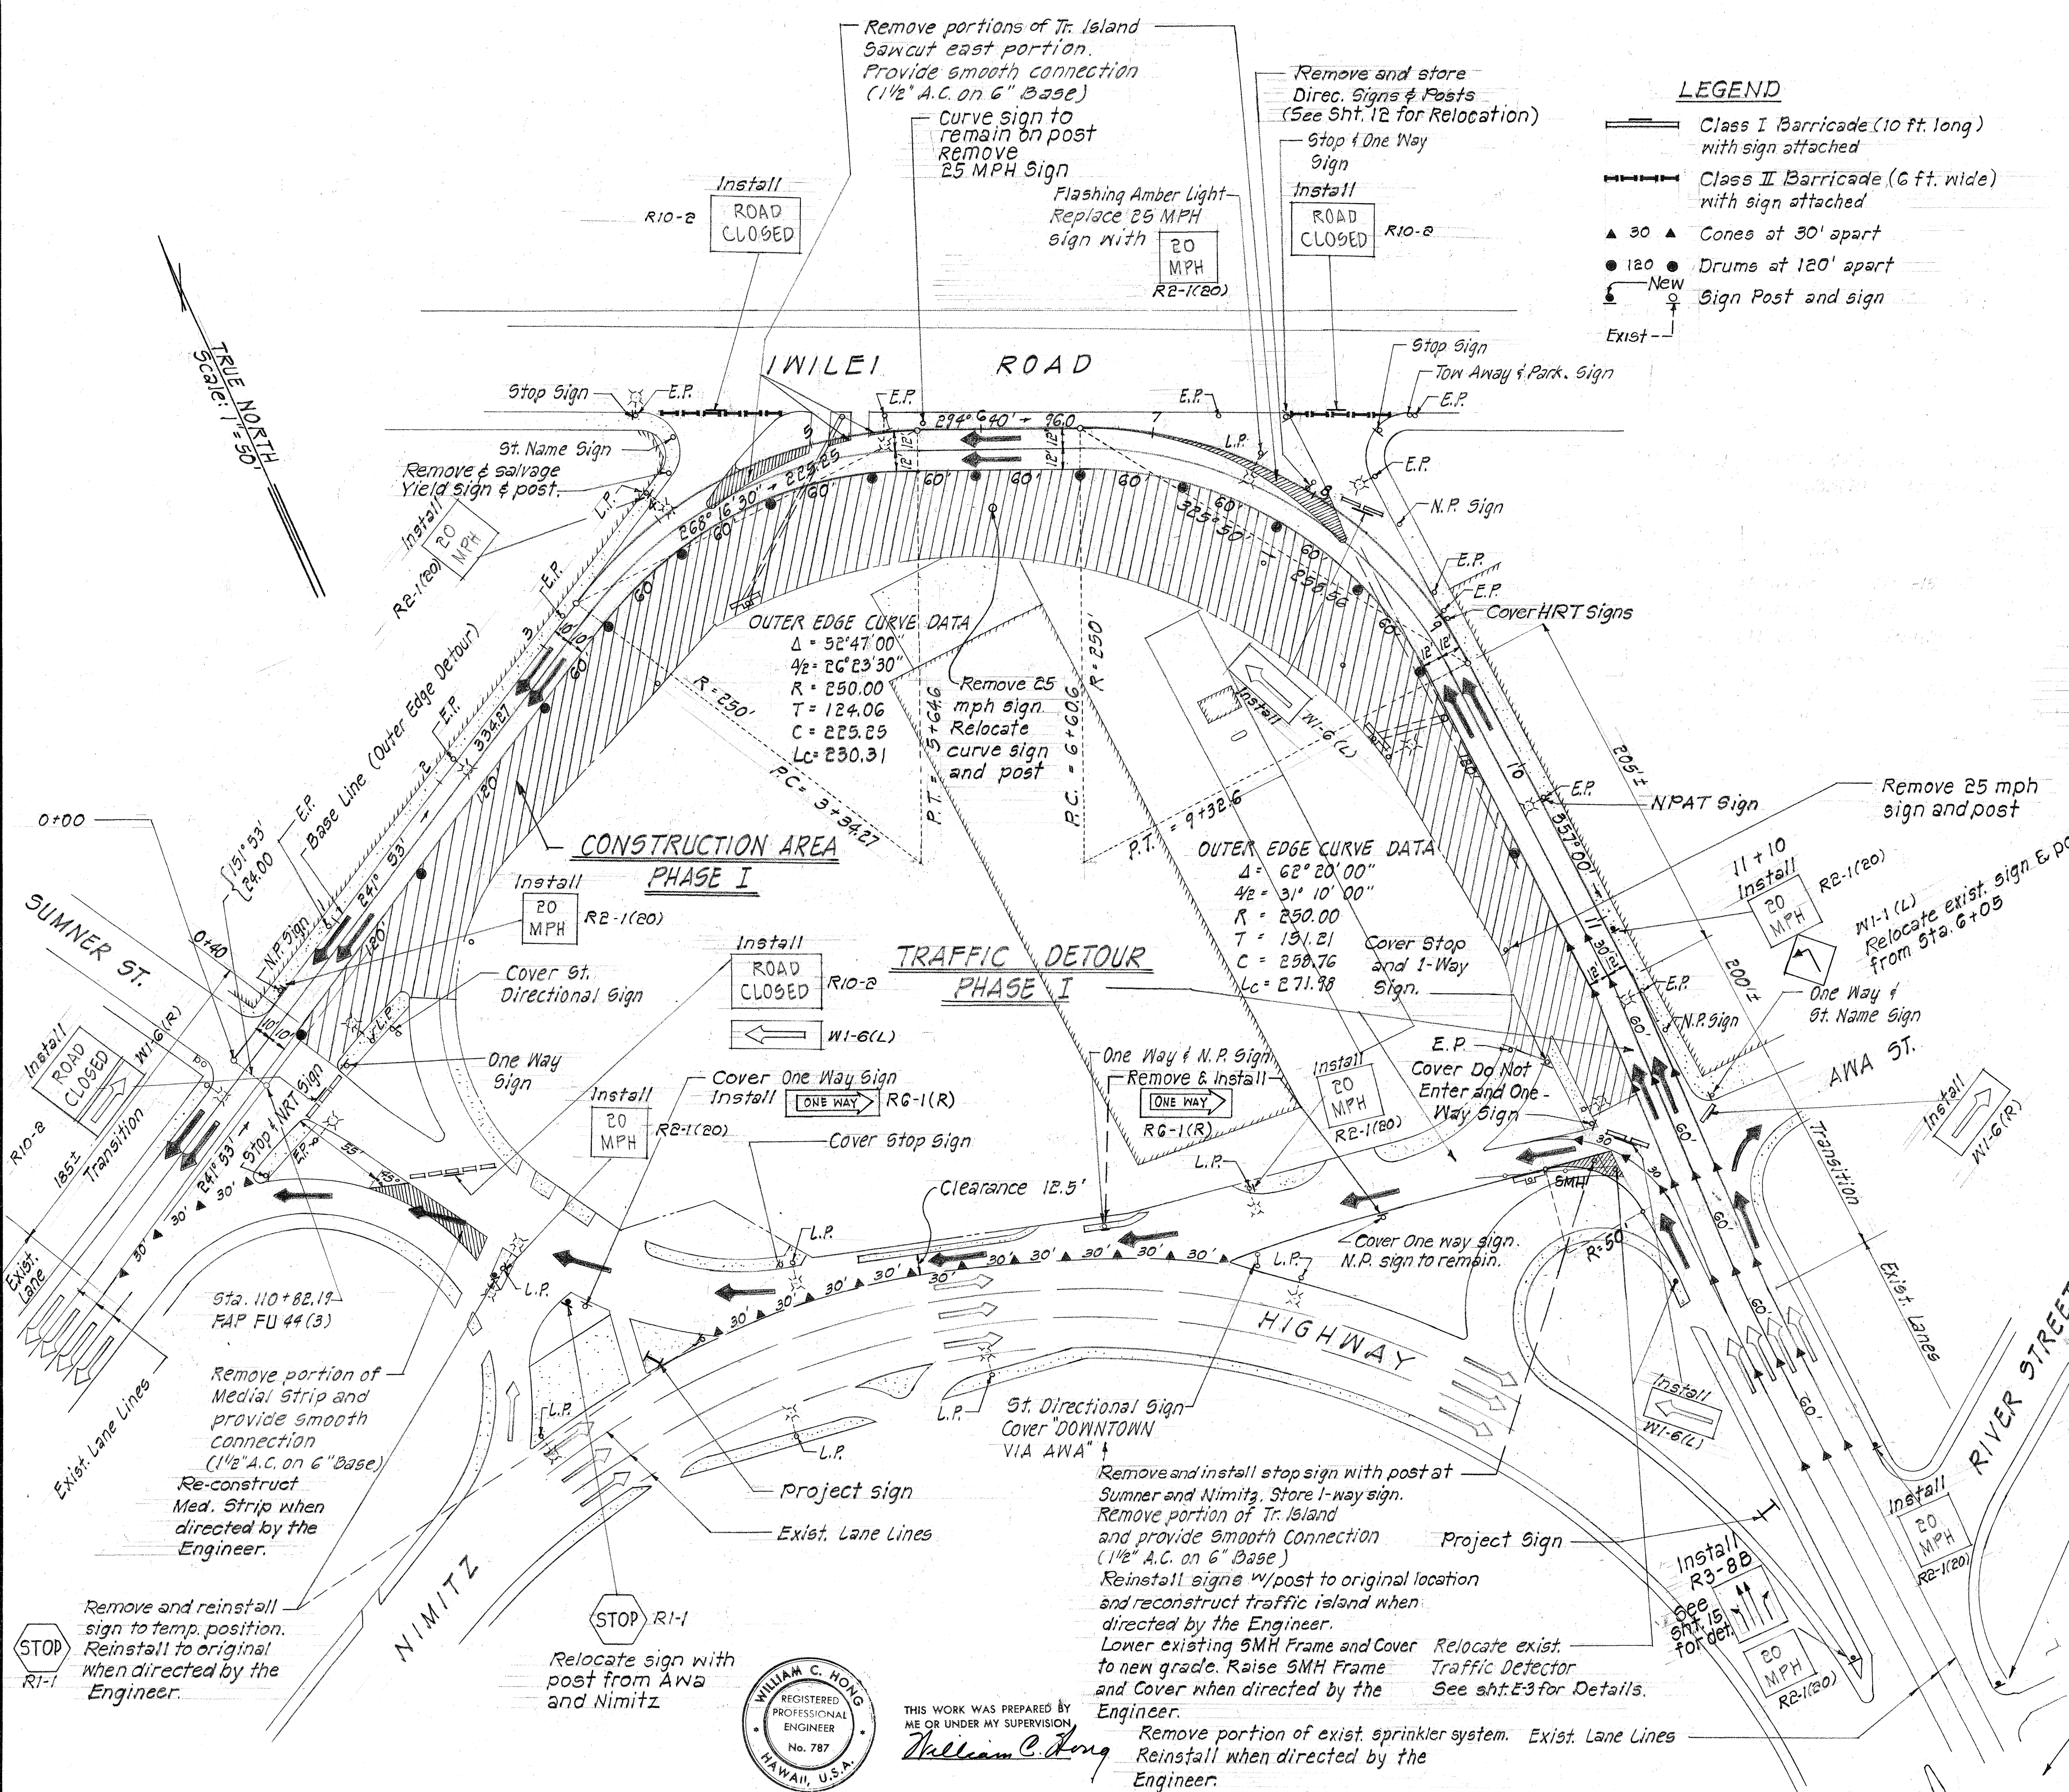

ORIGINAL PLAN	SURVEY PLOTTED BY.....	DATE.....
	DRAWN BY.....	".....
	TRACED BY.....	".....
NOTE BOOK	DESIGNED BY.....	".....
	QUANTITIES BY.....	".....
	CHECKED BY.....	".....
No.....		



THIS WORK WAS PREPARED BY
ME OR UNDER MY SUPERVISION
William C. H.

PRINTED ON NO. 1000H CLEARPRINT

